

MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

30-JUNE- 2017

1. PACKAGE-II

PACKAGE-II	STATUS AS ON 30/06/2017
Block D03	<ul style="list-style-type: none"> • All R.C.C. work completed up to basement roof slab level. • 50% Stilt Roof slab casted. • Total Columns casted upto soffit of Stilt Roof beams.
Current Month Activity	<ul style="list-style-type: none"> • Balance 50% of Stilt Roof slab casted. Total (100%) • First Floor Slab 100% casting done. • 20 Columns casted upto soffit of 2nd Floor Roof beams.
Block D04	<ul style="list-style-type: none"> • All work upto pile caps completed. • Both the Staircases casted upto Basement Roof level. • All columns casted up to soffit of basement roof beams. • Basement Roof Slab 25% casted.
Current Month Activity	<ul style="list-style-type: none"> • Basement Roof Slab 50% casted. • Basement Roof slab shuttering work for Remaining one flat is in progress. • Total 21 Columns casted upto Soffit of Stilt Roof beams.
Block D05	<ul style="list-style-type: none"> • All work upto pile caps completed. • All columns casted up to soffit of basement roof beams.
Current Month Activity	<ul style="list-style-type: none"> • Single flight Reinforcement binding of Both the Staircases done.
Block D06	<ul style="list-style-type: none"> • All work upto pile caps completed. • Total 64 columns casted up to soffit of basement roof beam bottom.
Current Month Activity	<ul style="list-style-type: none"> • Balance 4 columns casted upto soffit of Basement Roof beam bottom.
Block D07	<ul style="list-style-type: none"> • All work upto Stilt slab and grade beams completed. • Total Pile Caps Casted.
Current Month Activity	<ul style="list-style-type: none"> • Total 49 Columns casted upto a height of 2400mm. • Remaining Columns Reinforcement binding work completed.
Block D08	<ul style="list-style-type: none"> • 100% P.C.C. for foundation work completed. • 50% Stilt slab and grade beams casted.
Current Month Activity	<ul style="list-style-type: none"> • Balance Stilt slab 50% & 50% Grade Beams casted. • 100% Pile Caps casted.
Non Tower	<ul style="list-style-type: none"> • Total 549 nos. of piles casted out of 593 nos. • 20% P.C.C. for foundation work completed. • 5% of Stilt slab casted.
Current Month Activity	<ul style="list-style-type: none"> • 5.57% P.C.C. for foundation work completed (Total 25.57%) & further work in Progress. • 6% of Stilt slab casted. • Balance 44 Piles Casted.
Retaining Wall	<ul style="list-style-type: none"> • Total 68 nos. of piles casted out of 72 nos. • Retaining wall footing of length 40 mtrs. • Retaining wall of length 40 mtr casted (1st lift).



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Current Month Activity	<ul style="list-style-type: none">• Retaining wall of length 17mtrs casted (2nd lift).• Balance 4 Piles casted. (Total 72 Piles i.e. 100% completed).• Reinforcement binding work for 2nd lift is in progress
-------------------------------	--

PHOTOGRAPHS OF PACKAGE-II on 30thJUNE-2017

BLOCK D-04 BASEMENT SLAB SHUTTERING IS IN PROGRESS



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

BLOCK D-04 STILT FLOOR SLAB SHUTTERING IS IN PROGRESS



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

BLOCK D-03 2ND FLOOR SLAB SHUTTERING WORK IS IN PROGRESS.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

BLOCK D-06 COLUMNS CASTING 100% COMPLETED.



Progress Report No. **14** (1st June – 30th June- 17)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

2. PACKAGE-III

PACKAGE-III	STATUS AS ON 30/06/2017
Block C06	
Current Month Activity	<ul style="list-style-type: none">• 80% Excavation work completed.• Layout for piling in progress.
Block C07	
Current Month Activity	<ul style="list-style-type: none">• 80% Excavation work completed.
Block C08	
Current Month Activity	<ul style="list-style-type: none">• 80% Excavation work completed.
Block C01	
Current Month Activity	<ul style="list-style-type: none">• 50% Excavation work completed.
Block C02	
Current Month Activity	<ul style="list-style-type: none">• 80% Excavation work completed.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

EXCAVATION WORK IN BLOCK C06, C07 & C08 COMPLETED.



Progress Report No. 14 (1st June – 30th June- 17)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

EXCAVATION WORK IN BLOCK C06, C07 & C08 COMPLETED.



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

3. PACKAGE-IV

PACKAGE-IV	STATUS AS ON 30/06/2017
Block A01	<ul style="list-style-type: none"> • All civil work completed upto Pile caps.
Current Month Activity	<ul style="list-style-type: none"> • 80% columns casting completed for basement roof. • 50% Basement slab casting work completed.
Block B04	<ul style="list-style-type: none"> • Stilt roof slab casting 100% (8 flats) completed.
Current Month Activity	<ul style="list-style-type: none"> • 100% Columns casting of First floor completed. • First floor roof slab 50% (4 flats) shuttering & steel binding work completed.
Block B05	<ul style="list-style-type: none"> • Second floor roof slab casting 100% (8 flats) completed.
Current Month Activity	<ul style="list-style-type: none"> • 100% Steel binding completed & casting started of third floor columns. • Shuttering work for third floor roof slab started.
Block C13	<ul style="list-style-type: none"> • First floor roof slab casting 100% (4 flats) completed.
Current Month Activity	<ul style="list-style-type: none"> • 50% Steel binding & casting of second floor columns is completed.
Block C14	<ul style="list-style-type: none"> • Second floor roof slab casting 100% (4 flats) completed.
Current Month Activity	<ul style="list-style-type: none"> • 50% columns casting of third floor completed.
Block C03	<ul style="list-style-type: none"> • Total 195 nos. of piles casted out of 195. • Routine pile testing completed.
Current Month Activity	<ul style="list-style-type: none"> • Piling work completed. • 50% PCC work completed.
Block C04	<ul style="list-style-type: none"> • Total 44 nos. of piles casted out of 194.
Current Month Activity	<ul style="list-style-type: none"> • No work done.
Block C05	<ul style="list-style-type: none"> • Total 120 nos. of piles casted out of 195.
Current Month Activity	<ul style="list-style-type: none"> • Piling work is in progress.
Non Tower	<ul style="list-style-type: none"> • Total 630 nos. of piles casted out of 825. • 106 nos. Pile casting for STP completed. • 800 sqm slab casting of extended basement completed.
Current Month Activity	<ul style="list-style-type: none"> • Casting of pile cap, stitch slab, columns and retaining wall is in progress. • Kota stone water proofing work on outer side of retaining wall is in progress.
Permission for Excavation	<ul style="list-style-type: none"> • Required permission obtained from the Mining Authority Greater Noida on 12th April 2017.



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

PHOTOGRAPHS OF PACKAGE-IV on 30th June2017

BLOCK B05 3RD FLOOR COLUMNS CASTING 50% COMPLETED.




MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

BLOCK C14 3rd FLOOR COLUMNS CASTING 40% COMPLETED



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

BLOCK C13 3rd FLOOR SLAB SHUTTERING IN PROGRESS

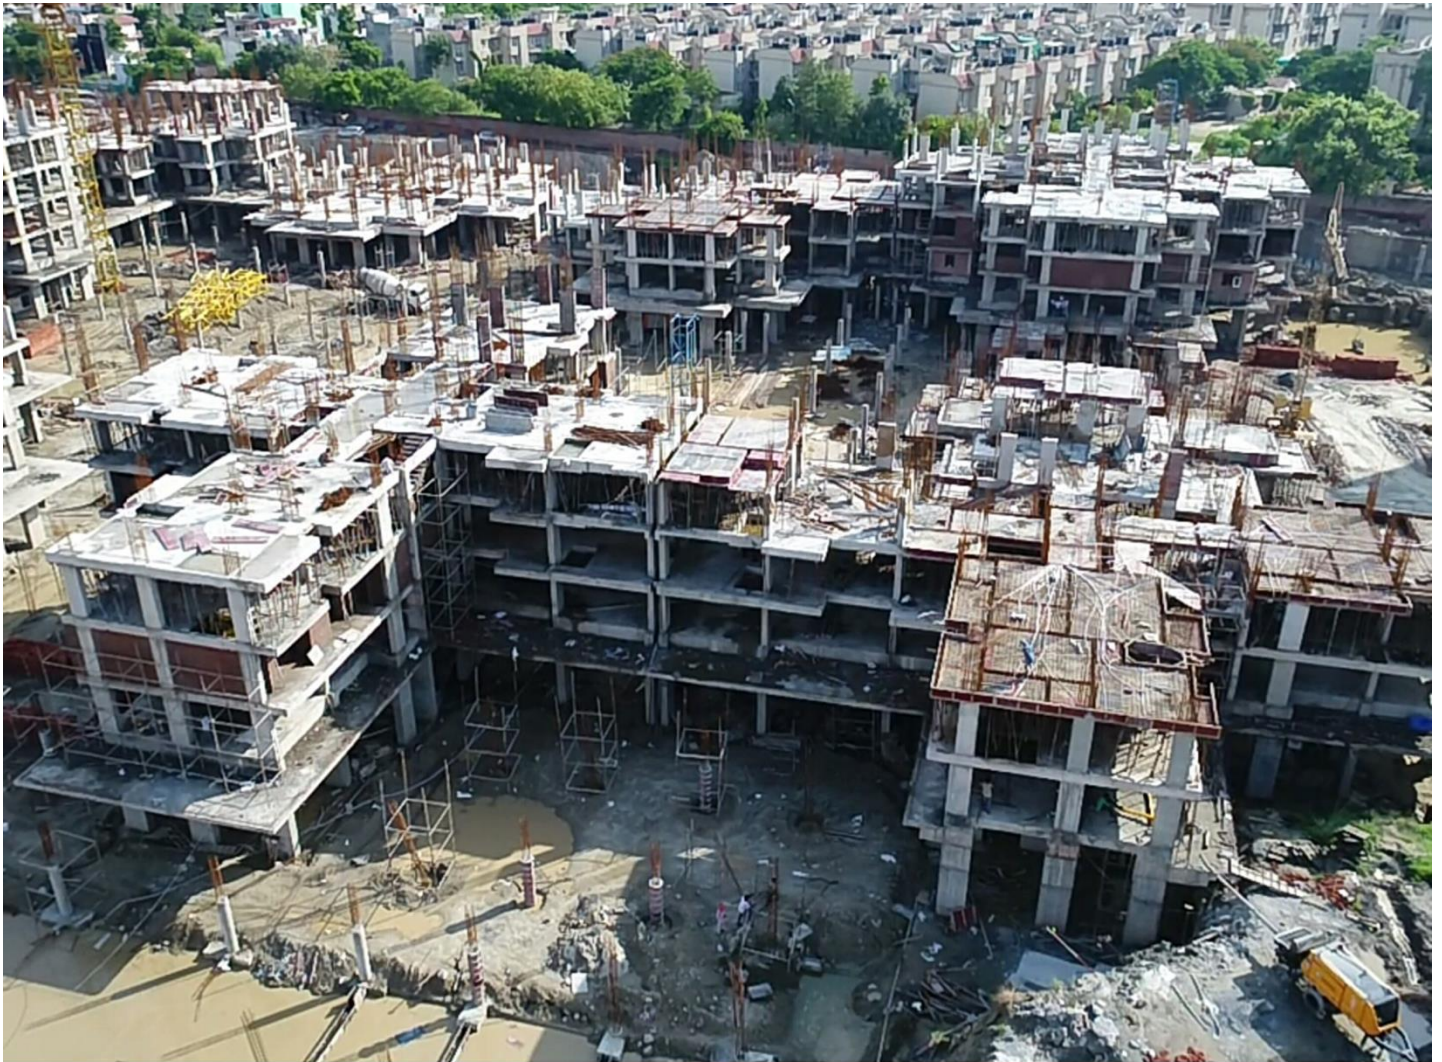

MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

BLOCK C05 PILING WORK IN PROGRESS



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

4. PACKAGE-V

PACKAGE-V	STATUS AS ON 30/06/2017
Block B01	<ul style="list-style-type: none"> • 50% casting of 2nd floor slab completed. • Sample flat Brick work upto lintel level is completed.
Current Month Activity	<ul style="list-style-type: none"> • 50% casting of 2nd floor slab completed. Total (100%) • 100 % 3rd Floor slab Casting done. • 50% columns casted up to soffit of 3rd floor Roof Beam bottom. • Balance Sample flat Brick work is completed. Total (100%) • Total 50% Brick work in stilt floor done. • Total 3 Flats Brick work in First floor is completed.
Block B02	<ul style="list-style-type: none"> • 50% casting of Stilt floor slab completed.
Current Month Activity	<ul style="list-style-type: none"> • Balance 50% casting of Stilt floor slab completed. Total (100%). • 100% First floor slab casted. • 75 % Columns casted at 2nd floor level. • 50% Brick work in Stilt floor done.
Block B03	<ul style="list-style-type: none"> • 50% casting of Basement Roof slab done.
Current Month Activity	<ul style="list-style-type: none"> • Balance 50% casting of Basement Roof slab done. Total (100%). • 50% Columns casted at Stilt floor level.
Block C15	<ul style="list-style-type: none"> • 75% casting of Stilt floor slab completed.
Current Month Activity	<ul style="list-style-type: none"> • Balance 25% casting of Stilt floor done. Total (100%) • 75% casting of First floor done. • 50% Columns casted at 2nd floor level.
Block C16	<ul style="list-style-type: none"> • 50% casting of Basement roof slab done.
Current Month Activity	<ul style="list-style-type: none"> • Balance 50% casting of basement roof slab is completed. Total (100%). • 100% columns casted upto Soffit of Stilt Roof Beam bottom. • Shuttering work of Stilt Roof slab is in progress.
Non Tower	<ul style="list-style-type: none"> • Piling work is completed. • 97% stitch slab casting completed. • 75 % columns casting completed.
Current Month Activity	<ul style="list-style-type: none"> • 3 % of P.C.C work for foundation done. • 1% of stitch slab casting done.
Retaining Wall	<ul style="list-style-type: none"> • Piling work is completed. • Casting of retaining wall upto a length of 140 mtr completed.
Current Month Activity	<ul style="list-style-type: none"> • Casting of Retaining wall footing upto a length of 40 mtrs done.



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

PHOTOGRAPHS OF PACKAGE-V on 30Th JUNE-2017

BLOCK C-15 STILT FLOOR SLAB SHUTTERING IN PROGRESS.



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

**BLOCK B-01 3RD FLOOR SLAB REINFORCEMENT BINDING WORK
IS IN PROGRESS.**



Progress Report No. 14 (1st June – 30th June- 17)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

BLOCK B-01 4TH FLOOR SLAB SHUTTERING WORK IN PROGRESS



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

BLOCK C-15 1ST FLOOR SLAB SHUTTERING WORK IS IN PROGRESS



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

QUALITY CONTROL

**DURING CONSTRUCTION FOLLOWING QUALITY CONTROL TESTS
CONDUCTED AT SITE:**

S. No	Materials	Source from	Test Date	Tests done	Result
1	Coarse Sand	Bajpur		Each truck	Sieve/ Silt
2	Coarse Aggregate	Nagal		Each truck	Sieve Analysis
3	Fine Sand				
4	Cement	Third party testing is being done			
5	Steel	Third party testing is being done			
6	RCC Cubes are being tested and Register is being maintained.				
7	Slump test conducted at site to insure workability if concrete.				



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

PHOTOGRAPHS TAKEN DURING QUALITY CONTROL AT SITE

20mm & 10mm Aggregate Testing



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

SLUMP TESTING



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

CUBE TESTING



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

TESTING OF COARSE SAND

