

MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

31st OCT-2019

Comparative Progress of Site works: -

PACKAGE-II	STATUS AS ON 31/10/2019
Up to Last Month Block D03	<ul style="list-style-type: none"> • Terrace GI water Supply Piping work 20% completed. (Total 95%). • Aluminum Door window DW-7 in Kitchen fixing completed up to 14th floor.. • Staircase-1 M.S. Railing completed from Basement to 3rd floor lvl. • Staircase -2 M.S. Railing completed from 1st to 10th floor . • S.S. Balcony Railing fixing work completed from 3rd to 7th floor • Staircase-1 stone flooring fixing completed from stilt to 7th floor • Staircase-2 stone flooring fixing completed from 1st to 3rd floor • Tiles flooring in corridor completed from 1st to 14th floor lvl. • Internal 1st coat Painting work completed from 1st to 14th floor. • Aluminium louvers in Plumbing shafts fixing work completed up to 5th floor l.
Current Month Activity	<ul style="list-style-type: none"> • Staircase-1 stone flooring completed from 8th floor to 14th floor. • Staircase-2 stone flooring completed from 4th floor to 6th floor • S.S. Balcony Railing fixing work completed from 8th to 14th floor. • Kota stone flooring in Machine Room completed. • Door frame beading fixing work completed up to 6th floor. • Aluminium louvers in Plumbing shafts fixing work completed from 6th floor to 11th floor. • Basement plaster in wings 1 completed.
Up to Last Month Block D04	<ul style="list-style-type: none"> • Terrace floor Brick coba water proofing work 100% completed. • Internal 2nd coat Birla putty work completed from 1st to 7th floor. • Aluminium door window frames fixing work completed from 1st to 5th floor • Basement Brick work 65% completed.(Total 100%). • Stilt floor Brick work 100% completed. • Terrace floor GI water supply piping work 90% completed.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

Current Month Activity	<ul style="list-style-type: none"> • Brick coba waterproofing work at Machine Room Terrace completed. • Internal 2nd Coat Birla putty work completed from 8th to 13th floor • 1st Coat Paint work completed from 2nd to 12th floor l. • Staircase-1 & 2 Ms Railing fixing completed from Basement to Terrace floor. • S.S. Balcony Railing fixing work completed in wing-1 from 1st to 6th floor • Aluminium door window frames fixing work completed from 6th to 14th floor • Basement plaster in wings-1 & 2 completed.
Up to Last Month Block D05	<ul style="list-style-type: none"> • Toilets Water proofing completed from 13th to 14th floor • Tiles Dado work in Toilets & Kitchen completed from 4th to 8th floor. • Tiles flooring work completed from 2nd to 8th floor • Stilt floor Brick work 95% completed. • Terrace Brick coba water proofing work is in progress. • Terrace GI Water supply piping work is in Progress.
Current Month Activity	<ul style="list-style-type: none"> • Brick coba water proofing 70% completed. • Terrace floor GI water supply Piping work 65% completed. • Tiles Dado in Toilets completed from 1st to 13th floor • Tiles flooring completed from 1st to 13th floor .
Up to Last Month Block D06	<ul style="list-style-type: none"> • Over Head water tank RCC wall casted. • Balcony RCC wall casted from 5th to 14th floor. • External Plaster 10% completed. (Total 60%). • Balcony water proofing work completed up to 9th floor. • Internal Birla putty 1st coat completed up to 14th floor. • Basement & Stilt floor Brick work completed.
Current Month Activity	<ul style="list-style-type: none"> • Machine Room & overhead water tank Roof slab casted. • Balcony Waterproofing completed from 10th to 14th floor. • Toilets Water proofing completed from 1st to 8th floor • External Plaster 30% completed. (Total 90%).
Up to Last Month Block D07	<ul style="list-style-type: none"> • Balance 50% 14th floor columns casted. (Total 100%) • 14th floor Roof slab Reinforcement binding work in wings-1 & 4 completed. • Balance 50% Brick work in 9th floor completed. • 11th & 12th floor lvl Brick work 90% completed. • Balcony RCC wall casted up to 6th floor.
Current Month Activity	<ul style="list-style-type: none"> • 14th floor Roof slab wings 1 & 4 casted. • Balcony RCC wall casted up to 10th floor • 13th floor Brick work 70% completed. • Door frames fixing completed up to 6th floor • • Cpvc piping completed up to 12th floor



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Up to Last Month Block D08	•
Current Month Activity	•
Up to Last Month Non-Tower	<ul style="list-style-type: none"> • PCC below VDF 840 Sqm completed. (Total 11660/16656Sqm). • Basement Ceiling Plaster 550 Sqm completed. (Total 10805/16656Sqm). • 42 Nos Circular columns plaster completed.(Total 190/290). • Basement Soil,waste and Rain water piping work 15% completed.(Total 65%). • Vd flooring 2936 Sqm completed. (Total 6386/16656). • Basement Firefighting piping work 2% completed.
Current Month Activity	<ul style="list-style-type: none"> • Basement ceiling plaster 200Sqm completed.(11005/16656 Sqm). • Vdflooring 3275 Sqm completed .(Total 9661/16656). • Basement Firefighting piping work 20% completed. • Basement Water supply piping work is in progress. • Ramp-06 Shuttering work is in Progress.
Up to Last Month Retaining Wall	<ul style="list-style-type: none"> • Retaining wall 1st lift 40mtrs casted. • Retaining wall 2nd lift 15mtrs casted.
Current Month Activity	<ul style="list-style-type: none"> • Front Retaining wall of length 100mtrs casted. Total 100/187Mtrs).



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

PHOTOGRAPHS OF PACKAGE-II on 31st OCT-2019

Block D-03

In Block D-03 SS Balcony Railing fixing work completed .



Progress Report No. 42 (1st OCT-19–31st OCT-19)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

**In Block D-06 Machine Room Roof Slab casted. Block D-07 14th floor
Roof slab 100% casted.**



Progress Report No. 42 (1st OCT-19–31st OCT-19)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Block D-05 Brick coba waterproofing is in progress.



Progress Report No. 42 (1st OCT-19–31st OCT-19)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

Block D-04 Aluminum Door window frames fixing work completed.




Progress Report No. 42 (1st OCT-19–31st OCT-19)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

BLOCK D-03

Staircase stone flooring and M.S.railing work completed.

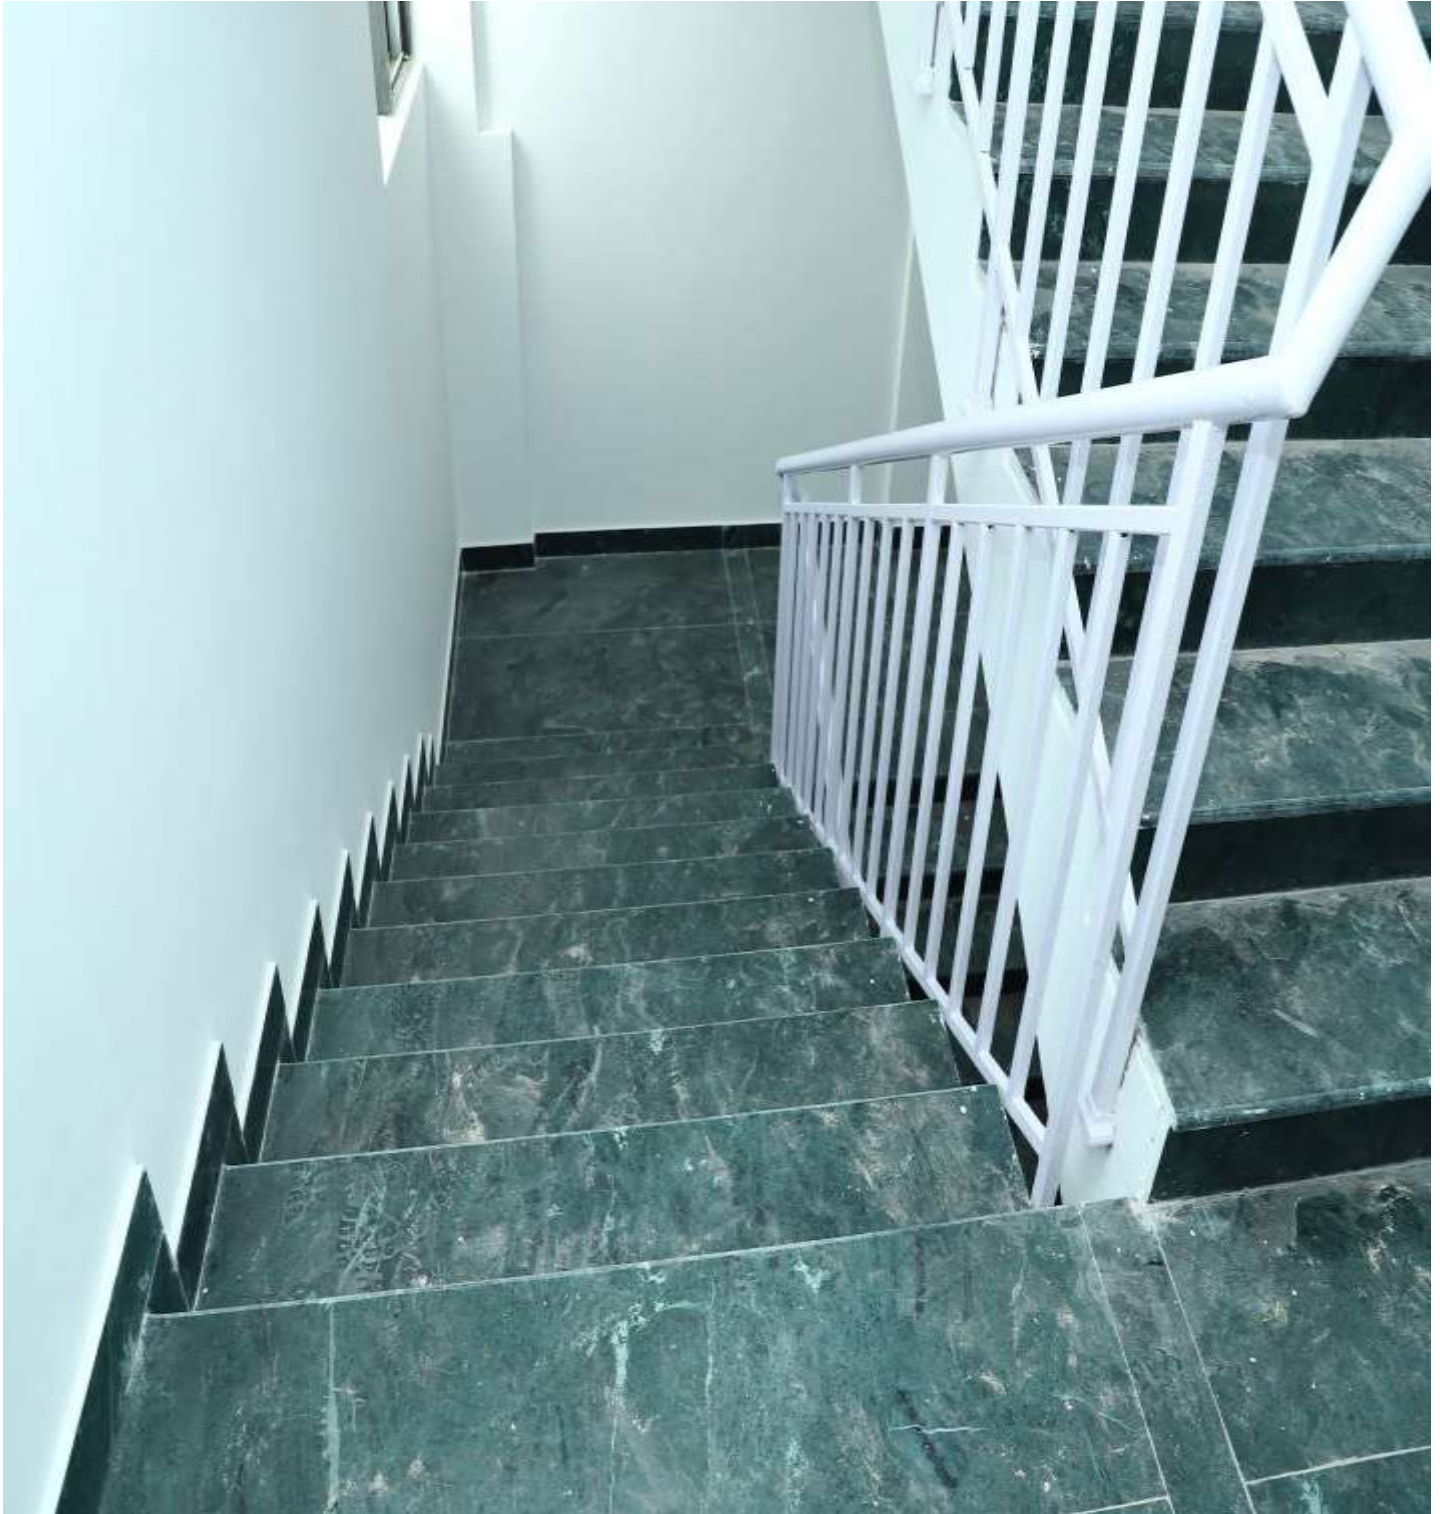

Progress Report No. 42 (1st OCT-19–31st OCT-19)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

**Basement CI Piping (Soil, waste & Rain water) & Water piping
works in progress.**



Progress Report No. 42 (1st OCT-19–31st OCT-19)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

Basement Firefighting Piping work is in progress.



Progress Report No. 42 (1st OCT-19–31st OCT-19)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Comparative Progress of Site works: -

PACKAGE-III	STATUS AS ON 31/10/2019
Up to Last Month Block C01	<ul style="list-style-type: none"> • Level 15(Terrace): 100% slab casting completed. <ul style="list-style-type: none"> ▪ Terrace projection column 100% & slab 50% casting completed & remaining reinforcement is on progress. ▪ Mumty column & slab casting completed. ▪ Overhead tank column & base slab casted completed & wall shuttering is on progress. • Level 14: Brick work completed. • Level 14: Door frame completed. • Level 11: Internal plaster completed. • Level 12: Internal plaster is on progress. • Level 13: Electrical wall conduit completed. • Level 14: Electrical wall conduit is on progress. • Level 13: Internal plumbing (CPVC) work completed. • Level 14: Internal plumbing (CPVC) work is on progress. • Level 01-03: POP cornice completed. • Level 04: POP cornice is on progress.
Current Month Activity	<ul style="list-style-type: none"> • Level 15(Terrace): 100% slab casting completed. <ul style="list-style-type: none"> ▪ Above Terrace stub column of projection slab casting completed. ▪ Terrace elevation of parapet wall casting completed. ▪ Mumty slab 100% completed. ▪ Overhead Tank base slab and wall casting completed. ▪ Machine room slab shuttering is on progress. • Level 14: Brick work completed. • Level 14: Door frame completed. • Level 14: Electrical wall conduit completed. • Level 12: Internal plaster completed. • Level 13: Internal plaster is on progress. <ul style="list-style-type: none"> ▪ External plaster 15% completed. • Level 14: Internal plumbing (CPVC) work completed. • Level 04: POP cornice completed. • Level 05: POP cornice is on progress.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

<p>Up to Last Month</p> <p>Block C02</p>	<ul style="list-style-type: none"> • Level 15 (Terrace): 100% slab casting completed. <ul style="list-style-type: none"> ▪ Terrace stub column & projection slab 100% casting completed. ▪ Mumty column & slab casting completed. ▪ Over Head tank base slab & wall casting completed. ▪ Machine room column casting completed & slab shuttering work is on progress. • Level 14: Brick work 100% completed. • Level 14: Door frame completed. • Level 14: Electrical wall conduit completed. • Level 14: Internal plaster completed. • External plaster 90% completed. • Level 01 to 08: Water proofing completed. • Level 09: Water proofing is on progress. • Level 01-05: Wall tile (Toilet & Kitchen) completed. • Level 06: Wall tile (Toilet & Kitchen) is on progress. • Level 14: Internal plumbing (CPVC) work completed. • Level 14: External & internal plumbing (CI) work completed. • Level 14: POP cornice completed.
<p>Current Month Activity</p>	<ul style="list-style-type: none"> • Level 15 (Terrace): 100% slab casting completed. <ul style="list-style-type: none"> ▪ Above Terrace stub column of projection slab casting completed. ▪ Terrace elevation of parapet wall casting completed. ▪ Mumty slab 100% completed. ▪ Overhead Tank base slab and wall casting completed. ▪ Machine room slab shuttering and reinforcement work is on progress. • Level 14: Brick work 100% completed. • Level 14: Door frame completed. • Level 14: Electrical wall conduit completed. • Level 14: Internal plaster completed. <ul style="list-style-type: none"> ▪ External plaster 95% completed. • Level 09 to 11: Water proofing completed. • Level 12: Water proofing is on progress. • Level 06 to 10: Wall tile (Toilet & Kitchen) completed. • Level 11: Wall tile (Toilet & Kitchen) is on progress. • Level 14: Internal plumbing (CPVC) work completed. • Level 14: External & internal plumbing (CI) work completed. • Level 14: POP cornice completed.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

<p>Up to Last Month</p> <p>Block C06</p>	<ul style="list-style-type: none"> • Level 15(Terrace): 100% slab casting completed. <ul style="list-style-type: none"> ▪ Terrace Stub column & projection slab casting completed. ▪ Mumty column & slab completed. ▪ Overhead tank base slab & wall casting completed. ▪ Machine room column & slab casting completed. ▪ Projection above machine room casting completed. • Level 14: Brick work completed. • Level 14: Door frame completed. • Level 14: Electrical wall conduit completed. • Level 14: Internal plaster completed. <ul style="list-style-type: none"> ▪ External plaster 95% completed. • Level 14: Water proofing completed. • Level 11-14: Wall tile (Toilet &Kitchen) completed. • Level 14: Internal plumbing (CPVC) work completed. • Level 14: External & internal plumbing (CI) work completed. • Level 14: External vertical (GI) work completed. • Level 06-14: POP cornice completed. • Level 01-10: Wall putty completed. • Level 11: Wall putty is on progress.
<p>Current Month</p> <p>Activity</p>	<ul style="list-style-type: none"> • Level 15(Terrace): 100% slab casting completed. <ul style="list-style-type: none"> ▪ Above Terrace stub column of projection slab casting completed. ▪ Terrace elevation of parapet wall casting completed. ▪ Mumty slab 100% completed. ▪ Overhead Tank base slab and wall casting completed. ▪ Machine room slab casting completed. ▪ Projection above machine room casting completed. • Level 14: Brick work completed. • Level 14: Door frame completed. • Level 14: Electrical wall conduit completed. • Level 14: Internal plaster completed. <ul style="list-style-type: none"> ▪ External plaster 95% completed. • Level 14: Water proofing completed. • Level 14: Wall tile (Toilet &Kitchen) completed. • Level 04: Floor tile completed. • Level 05: Floor tile is on progress. • Level 14: Internal plumbing (CPVC) work completed. • Level 14: External & internal plumbing (CI) work completed. • Level 14: External vertical (GI) work completed. • Level 14: POP cornice completed. • Level 11: Wall putty completed. • Level 12: Wall putty is on progress.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

Up to Last Month

Block C07

- Level 15(Terrace): 100% slab casting completed.
 - Terrace Stub column casting completed & projection slab shuttering is on progress.
 - Mumty column & slab completed.
 - Overhead tank base slab & wall casting completed.
 - Machine room column & slab casting completed.
 - Projection above machine room reinforcement work is on progress.
- Level 14: Brick work 100% completed.
- Level 14: Door frame completed.
- Level 14: Internal plaster completed.
- External plaster 90% completed.
- Level 14: Electrical wall conduit completed.
- Level 14: Water proofing completed.
- Level 14: Wall tile (Toilet & Kitchen) completed.
- Level 06-10: Floor tile completed.
- Level 11: Floor tile is on progress.
- Level 14: Internal plumbing (CPVC) work completed.
- Level 14: External & internal plumbing (CI) work completed.
- Level 14: External vertical (GI) work completed.
- Level 10-13: POP cornice completed.
- Level 14: POP cornice is on progress.
- Level 01-03: Wall putty is completed.
- Level 04: Wall putty is on progress.



Progress Report No. 42 (1st OCT-19–31st OCT-19)



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

Current Activity	Month	
		<ul style="list-style-type: none">• Level 15(Terrace): 100% slab casting completed.<ul style="list-style-type: none">▪ Above Terrace stub column of projection slab casting completed.▪ Terrace elevation of parapet wall casting completed.▪ Mumty slab 100% completed.▪ Overhead Tank base slab and wall casting completed.▪ Machine room slab casting completed.▪ Projection above machine room casting 50% completed and remaining shuttering is on progress.• Level 14: Brick work 100% completed.• Level 14: Door frame completed.• Level 14: Electrical wall conduit completed.• Level 14: Internal plaster completed.<ul style="list-style-type: none">▪ External plaster 95% completed.• Level 14: Water proofing completed.• Level 14: Wall tile (Toilet & Kitchen) completed.• Level 11 to 14: Floor tile completed.• Level 14: Internal plumbing (CPVC) work completed.• Level 14: External & internal plumbing (CI) work completed.• Level 14: External vertical (GI) work completed.• Level 14: POP cornice completed.• Level 04: Wall putty is completed.• Level 05: Wall putty is on progress.• Level 01 to 14: Both Staircase railing completed.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

Up to Last Month

Block C08

- Level 15(Terrace): 100% slab casting completed.
 - Stub column of projection slab casting completed.
 - Terrace elevation of parapet wall casting completed.
 - Mumty slab 100% completed.
 - Overhead tank base slab & wall casting completed.
 - Machine room slab casting completed.
 - Projection above machine room casting completed.
- Level 14: Brick work 100% completed.
- Level 14: Door frame completed.
- Level 14: Internal plaster completed.
- External plaster 95% completed.
- Level 14: Electrical wall conduit completed.
- Level 01 to 14: Water proofing completed.
- Level 14: Wall tile (Toilet & kitchen) completed.
- Level 13: Floor tile completed.
- Level 14: Floor tile is on progress.
- Level 14: Internal plumbing (CPVC) work completed.
- Level 14: External & internal plumbing (CI) work completed.
- Level 14: External vertical (GI) work completed.
- Level 08-12: POP cornice completed.
- Level 13: POP cornice is on progress.
- Level 01-07: Wall putty completed.
- Level 08: Wall putty is on progress.



Progress Report No. 42 (1st OCT-19–31st OCT-19)



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

Current Month Activity	<ul style="list-style-type: none"> • Level 15(Terrace): 100% slab casting completed. <ul style="list-style-type: none"> ▪ Above Terrace Stub column of projection slab casting completed. ▪ Terrace elevation of parapet wall casting completed. ▪ Mumty slab 100% completed. ▪ Overhead tank base slab & wall casting completed. ▪ Machine room slab casting completed. ▪ Projection above machine room casting completed. ▪ Brick coba work is on progress. • Level 14: Brick work 100% completed. • Level 14: Door frame completed. • Level 14: Electrical wall conduit completed. • Level 14: Internal plaster completed. <ul style="list-style-type: none"> • External plaster 95% completed. • Level 14: Water proofing completed. • Level 14: Wall tile (Toilet & kitchen) completed. • Level 14: Floor tile completed. • Level 14: Internal plumbing (CPVC) work completed. • Level 14: External & internal plumbing (CI) work completed. • Level 14: External vertical (GI) work completed. • Level 13&14: POP cornice completed. • Level 08&09: Wall putty completed. • Level 10: Wall putty is on progress. • Level 01 to 14: Both Staircase railing completed.
Up to Last Month Block C09	<ul style="list-style-type: none"> • Level 05: Remaining 50% column casting completed. • Level 06: 100% Slab casting is on progress & column reinforcement is on progress. • Level 02-03: Brick work completed. • Level 04: Brick work is on progress.
Current Month Activity	<ul style="list-style-type: none"> • Level 07: 100% Slab & 50% column casted. • Level 08: Slab shuttering is on progress. • Level 04: Brick work completed. • Level 05: Brick work is on progress. • Level 05: Door frame completed. • Level 06: Door frame is on progress. • Level 02: Electrical wall conduit completed. • Level 03: Electrical wall conduit is on progress.
Up to Last Month Block C10	<ul style="list-style-type: none"> • Level 01: Remaining 50% column casting completed. • Level 02: 100% slab casting completed & column reinforcement work is on progress.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Current Month Activity	<ul style="list-style-type: none"> • Level 03: 100% slab & 50% column casting completed. • Level 04: Slab shuttering is on progress.
Up to Last Month Block C11	<ul style="list-style-type: none"> • Level 10: 100% slab & column casting completed. • Level 05: Brick work 100% completed. • Level 06: Brick work is on progress. • Level 04: Door frame completed. • Level 05: Door frame is on progress. • Level 03: Electrical wall conduit completed. • Level 04: Electrical wall conduit is on progress. • Level 01-02: Internal plaster completed. • Level 03: Internal plaster is on progress.
Current Month Activity	<ul style="list-style-type: none"> • Level 11: 100% slab & 100% column casting completed. • Level 12: Slab shuttering & reinforcement work is on progress. • Level 06: Brick work 100% completed. • Level 07: Brick work is on progress. • Level 05&06: Door frame completed. • Level 07: Door frame is on progress. • Level 05&06: Electrical wall conduit completed. • Level 07: Electrical wall conduit is on progress. • Level 03-05: Internal plaster completed. • Level 06: Internal plaster is on progress. • Level 01 to 06: Internal plumbing (CPVC) completed. • Level 07: Internal plumbing (CPVC) is on progress.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

<p>Up to Last Month</p> <p>Block C12</p>	<ul style="list-style-type: none"> • Level 15(Terrace): 100% slab casting completed. <ul style="list-style-type: none"> ▪ Terrace projection column 100% reinforcement completed. ▪ Mumty column & slab casting completed. ▪ Overhead tank column casting completed & base slab reinforcement work is on progress. • Level 12-13: Brick work 100% completed. • Level 13: Brick work is on progress. • Level 11-12: Door frame completed. • Level 13: Door frame is on progress. • Level 09-10: Internal plaster completed. • Level 11: Internal plaster is on progress. • Level 11-12: Electrical wall conduit completed. • Level 13: Electrical wall conduit is on progress. • Level 09: Internal plumbing (CPVC) work completed. • Level 10: Internal plumbing (CPVC) work is on progress.
<p>Current Month Activity</p>	<ul style="list-style-type: none"> • Level 15(Terrace): 100% slab casting completed. <ul style="list-style-type: none"> ▪ Above Terrace Stub column of projection slab casting completed. ▪ Terrace elevation of parapet wall casting completed. ▪ Mumty slab 100% completed. ▪ Overhead tank base slab reinforcement is on progress. • Level 14: Brick work 100% completed. • Level 13: Door frame completed. • Level 14: Door frame is on progress. • Level 12: Electrical wall conduit completed. • Level 13: Electrical wall conduit is on progress. • Level 10: Internal plaster completed. • Level 11: Internal plaster is on progress. • Level 10 to 14: Internal plumbing (CPVC) work completed.
<p>Up to Last Month</p> <p>UG Tank</p>	<ul style="list-style-type: none"> • U.G. Tank 100% RCC work completed.
<p>Current Month Activity</p>	<ul style="list-style-type: none"> • U.G. Tank water proofing work is on progress.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Up to Last Month Non-Tower	<ul style="list-style-type: none"> • Pile casting completed. (848/848) Nos. • Laying P.C.C completed. (Total 17257/18731) Sqm • Stitch slab casting completed. (Total 16658/18731) Sqm • Circular column casting completed. (Total 294/339) Nos. • Basement non-tower slab casting completed Total (11617/18731) Sqm • Retaining wall casting completed (277/294) m • Boundary wall casted (115/277) sqm
Current Month Activity	<ul style="list-style-type: none"> • Stitch slab casting 390 sqm casting (17048/18731) sqm • Basement non-tower slab 676 sqm casting (12293/18731) sqm • Boundary wall 50 sqm casting (165/277) sqm

(B) Status of Test Piles: -

Location	Status
Block C01, C02, C06, C07, C08, C09, C10, C11 & C12	Routine test completed.
Block C07, C08, C11 & Non-Tower	Initial test conducted.



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

PHOTOGRAPHS OF PACKAGE-III on 31st OCT-2019

Block C-01 Above terrace over head tank slab reinforcement is on progress.

Block C-02 Above terrace over head tank slab reinforcement is on progress.

Block C-12 Above terrace water tank wall reinforcement is on progress.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Block C-06 Above terrace plater work is on progress.

Block C-07 Above terrace plater work is on progress.

Block C-08 Brick coba is on progress.



Progress Report No. 42 (1st OCT-19–31st OCT-19)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Block C-09 Level -07 column reinforcement is on progress.

Block C-10 Level -03 column reinforcement is on progress.

Block C-11 Level-12 slab shuttering is on progress.



Progress Report No. 42 (1st OCT-19–31st OCT-19)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Block C-09 Level -07 column reinforcement is on progress.

Block C-10 Level -03 column reinforcement is on progress.

Block C-11 Level-12 slab shuttering is on progress.



Progress Report No. 42 (1st OCT-19–31st OCT-19)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Boundary wall brick work is on progress.



Progress Report No. 42 (1st OCT-19–31st OCT-19)



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

Comparative Progress of Site works.

PACKAGE-IV	STATUS AS ON 31/10/2019
Block A01 UpTo Last Month	<ul style="list-style-type: none"> • Machine room Kota Stone fixing work completed. • Wall primer work completed with common passage. • 1st coat of paint work from 1st to 3rd floor in flats completed. • Electrical wiring work on 2nd to 8th floor completed. • SS balcony railing work fixing started. • 60%Stilt floor VDF flooring work completed. • Overhead tank MS ladder fixing work completed. • 100% RCC, Brick work, Internal plaster, SCI, POP Cornices, Wall tiles, Floor tiles and Wall putty work completed.
Current Month Activity	<ul style="list-style-type: none"> • 1st coat of paint work from 1st to 7th floor in flats completed. • Electrical wiring work on 2nd to 13th floor completed. • 1st to 6th floor SS balcony railing work completed. • 70%Stilt floor VDF flooring work completed. • Stilt to basement CI connection work completed. • Aluminum door window frame with glass fixing work completed. • 100% RCC, Brick work, Internal plaster, SCI, POP Cornices, Wall tiles, Floor tiles and Wall putty work completed.
Block B04 UpTo Last Month	<ul style="list-style-type: none"> • SS Balcony railing fixing work completed all floors. • Shaft louvers fixing work completed all floors. • 1st coat Paint work completed in flats and common passage at all floors. • Overhead tank MS ladder fixing work completed. • 3rd floor main frame fixing of aluminium door and windows work completed. • Internal Door shutter work from 1st to 6th floor completed. • Staircase Baroda Green fixing work from Stilt to 11th floor completed. • 100% RCC, Brick work, Internal plaster, SCI, POP Cornices, Floor tiles, Wall tiles and Wall putty work completed
Current Month Activity	<ul style="list-style-type: none"> • Up to 10th Internal door shutter fixing work completed. • All floor main frame fixing of aluminium door and windows work completed. Glass fixing work in progress. • All Floor Staircase Baroda Green fixing work completed. • Mumty room tile fixing work completed. • Stilt to basement CI connection work completed. • 100% RCC, Brick work, Internal plaster, SCI, POP Cornices, Floor tiles, Wall tiles and Wall putty work completed.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Block B05 UpTo Last Month	<ul style="list-style-type: none"> • 1st coat of Paint work completed in flat and common passage at all floors. • SS Balcony railing fixing work up to 5th floor completed. • Internal Door shutter work from 1st to 8th floor completed. • Overhead tank MS ladder fixing work completed. • All floors shaft louvers fixing work completed. • 50% Stilt floor VDF flooring work completed. • Stilt to basement CI connection work completed. • 100% RCC, Brick work, Internal plaster, SCI, POP Cornices, Wall tiles, Floor tiles and Wall putty work completed
Current Month Activity	<ul style="list-style-type: none"> • SS Balcony railing fixing work up to 13th floor completed. • Internal Door shutter work from 1st to 10th floor completed. • All floor Aluminium door window frame fixing work completed.80% Glass fixing work completed. • 70% Stilt floor VDF flooring work completed. • 90% 9th to 13th floor internal wiring work completed. • Stilt to basement CI connection work completed. • 100% RCC, Brick work, Internal plaster, SCI, POP Cornices, Wall tiles, Floor tiles and Wall putty work completed.
Block C13 UpTo Last Month	<ul style="list-style-type: none"> • 1st coat paint work completed common passage. • Overhead tank MS ladder fixing work completed. • Machine room MS railing fixing work completed. • Staircase Baroda green fixing work completed. • 1st coat paint work at 2nd to 3rd floor completed. • Electrical wiring work on 2nd to 3rd floor completed. • 50% Stilt floor VDF flooring work completed. • 100% RCC, Brick work, Internal plaster, SCI, POP Cornices, Wall putty, Floor Tiles, Wall Tiles, staircase railing work completed.
Current Month Activity	<ul style="list-style-type: none"> • 1st coat paint work at 1st to 6th floor completed. • 100% 2nd to 9th floor internal wiring work completed. • 100% Main door entrance door fixing work completed. • 60% Stilt floor VDF flooring work completed. • OHT tank water proofing work in progress. • Stilt to basement CI connection work completed. • 100% RCC, Brick work, Internal plaster, SCI, POP Cornices, Wall putty, Floor Tiles, Wall Tiles, staircase railing work completed.
Block C14 UpTo Last Month	<ul style="list-style-type: none"> • Overhead tank MS ladder fixing work completed. • Machine room railing work completed. • 1st coat paint work common passage work completed. • 1st coat paint work on 2nd to 6th floor completed. • Electrical wiring work completed at all floors. • Electrical MCB work completed all floors. • 30% Stilt floor VDF flooring work completed. • 100% RCC, Brick work, Internal plaster, SCI, POP Cornices, Wall putty, Wall Tiles, Floor tiles work completed.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Current Month Activity	<ul style="list-style-type: none"> • 1st coat paint work on 2nd to 12th floor completed. • 100% Main door entrance door fixing work completed. • 30% Stilt floor VDF flooring work completed. • OHT tank water proofing work in progress. • Stilt to basement CI connection work completed. • 100% RCC, Brick work, Internal plaster, SCI, POP Cornices, Wall putty, Wall Tiles, Floor tiles work completed.
Block C03 UpTo Last Month	<ul style="list-style-type: none"> • All flats internal tile fixing work completed. • Overhead tank MS ladder fixing work completed. • Machine room kota stone fixing work completed. • All floor second coat wall putty work completed. • Machine room staircase MS railing fixing work completed. • Lift shafts one coat OBD work completed. • Machine room OBD work completed. • 2nd coat wall putty work completed all floors. • Wall primer work completed at all flats. • Common passage floor tiles fixing work is completed. • 100% RCC, Brick work, Door frame, SCI, POP Cornice, Wall tiles work completed
Current Month Activity	<ul style="list-style-type: none"> • Aluminium door window frame fixing work in progress. • 100% plumbing shafts louvers fixing work completed. • Up to 7th floor SS railing fixing work completed. • 90% internal door fixing work completed. • 90% Main door teak wood fixing work completed. • 90% 1st coat internal paint of flats work completed. • 100% 2nd switch, wiring, and MCB DB work completed. • Common passage floor tiles fixing work is completed. • OHT tank water proofing work in progress. • 100% RCC, Brick work, Door frame, SCI, POP Cornice, Wall tiles work completed
Block C04 UpTo Last Month	<ul style="list-style-type: none"> • All floor tile fixing work completed. • All floor Indian WC fixing work completed. • Overhead tank MS ladder fixing work completed. • Machine room staircase MS railing fixing work completed. • Machine room OBD work completed. • Lift shaft OBD completed. • 1st coat putti work completed in staircase and common passage. • Floor tile fixing work completed in all floors. • Indian WC fixing work completed in all floors. • Wall Primer work completed in all floors. • Floor tile fixing work completed on 8th floor and common passage. • 2nd Coat putty work completed in all floors. • 100% RCC, Brick work, Door frame, SCI, POP Cornice, Wall tiles work completed



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Current Month Activity	<ul style="list-style-type: none"> • Aluminium door window frame fixing work in progress. • Up to 4th floor internal door fixing work completed. • Up to 4th floor Main door teak wood fixing work completed. • 100% plumbing shafts louvers fixing work completed. • SS railing making work completed. • 90% Internal primer work completed. • Machine room OBD work completed. • Lift shaft OBD completed. • All Floor tile fixing work completed and common passage. • OHT tank water proofing work in progress. • 100% RCC, Brick work, Door frame, SCI, POP Cornice, Wall tiles work completed
Block C05 UpTo Last Month	<ul style="list-style-type: none"> • Floor tile fixing work on 8th to 14th floor is completed. • Overhead tank MS ladder fixing work completed. • Mumty machine room internal plaster work completed. • Machine room One coat OBD completed. • External putty work completed in machine room. • Mumty machine room internal plaster work completed. • 1st coat putty work completed in staircase and common passage. • Terrace level Brick coba work completed. • Kitchen Counter work completed all floors. • POP cornice work completed in all floors. • 100% RCC, brick work, Internal plaster, Door frame, SCI work completed
Current Month Activity	<ul style="list-style-type: none"> • Plumbing shafts louvers fixing work in progress. • 75% Stilt floor VDF flooring work completed. • SS railing making in progress. • Second coat wall putty work completed. • All Floor tile fixing work completed. • Mumty machine room internal plaster work completed. • Machine room One coat OBD completed. • External putty work completed in machine room. • OHT tank water proofing work in progress. • 100% RCC, brick work, Internal plaster, Door frame, SCI work completed



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Non-Tower UpTo Last Month	<ul style="list-style-type: none"> • 99% Retaining Wall work completed. • 309 M Boundary wall columns, Tie beams casting and brick work completed. • 550 R/M RCC Drain work completed. • 200 Sqm PCC for basement flooring work completed. (15800/15900sqm) • 3000 Sqm VDF for basement flooring work completed. (14700/15806 sqm) • 95% SCI work in basement ceiling fixing work completed. • 70% Firefighting work in basement ceiling work completed. • ATT work in progress below PCC. • 95% Kota stone water proofing work completed.
Current Month Activity	<ul style="list-style-type: none"> • 99% Retaining Wall work completed. • 309 M Boundary wall columns, Tie beams casting and brick work, plaster work completed. • 309 M Boundary wall MS railing work completed. • 610 R/M RCC Drain work completed. • 200 Sqm PCC for basement flooring work completed. (15800/15900sqm) • 500 Sqm VDF for basement flooring work completed. (15200/15806 sqm) • 96% SCI work in basement ceiling fixing work completed. • 72% Fire fighting work in basement ceiling work completed. • 80% Domestic Water supply and Flushing Water supply work completed. • ATT work in progress below PCC. • 96% Kota stone water proofing work completed.
Sample Flat Type A, B & C Status	<ul style="list-style-type: none"> • Painting work of walls & Ceiling completed. • Tile fixing work completed. • Internal Electrical work completed. • Water supply & Drainage work completed.

(B) Status of Test Piles: -

Location	Status
Block A01, B04, B05, C03, C04, C05, C13 & C14	Routine test completed.



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

PHOTOGRAPHS OF PACKAGE-IV on 31ST OCTOBER -2019

BIRD EYE VIEW OF PROJECT.



Progress Report No. 42 (1st OCT-19–31st OCT-19)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT



Progress Report No. 42 (1st OCT-19–31st OCT-19)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

**BLOCK C03,C04,C05- EXTERNAL 1ST COAT PUTTY WORK
COMPLETED.**



Progress Report No. 42 (1st OCT-19–31st OCT-19)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

BASEMENT FIRE FIGHTING WORK IN PROGRESS.



Progress Report No. 42 (1st OCT-19–31st OCT-19)



MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT
BASEMENT SEWERAGE LINE WORK IN PROGRESS.



Progress Report No. 42 (1st OCT-19–31st OCT-19)



MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT
NON-TOWER WATERPROOFING WORK IN PROGRESS.



Progress Report No. 42 (1st OCT-19–31st OCT-19)



MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT
ALUMINIUM DOOR WINDOWS FIXING WORK COMPLETED
IN BLOCK-A01,B04,B05,C13,C14.



Progress Report No. 42 (1st OCT-19–31st OCT-19)



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

Comparative Progress of Site Works: -

PACKAGE-V	STATUS AS ON 31/10/2019
Up to Last Month Block B01	<ul style="list-style-type: none"> • Internal Painting on ceiling completed up to 9th floor lvl. • Internal wall Painting work completed up to 9th floor lvl. • Internal wiring work completed up to 10th floor lvl. • Balcony SS railing fixing work in wing-4 completed up to 12th floor lvl. • Plumbing Shafts Louvers fixing work completed from 9th floor to 12th floor lvl. •
Current Month Activity	<ul style="list-style-type: none"> • Internal Door shutters fixing completed up to 10th floor lvl. • Internal wall & ceiling painting completed in 11th floor lvl. • MCB & Switch sockets fixing completed up to 12th floor lvl.
Up to Last Month Block B02	<ul style="list-style-type: none"> • Diverter fixing completed up to 13th floor lvl. • Internal door shutters fixing completed up to 7th floor lvl. • Internal Birla putty work 2nd coat completed from 12th floor to 13th floor lvl. • Plumbing Shafts Louvers fixing work completed from 11th floor to 13th floor lvl. • Balcony SS Railing top rail fixing work in wings-1 & 4 is in progress. •
Current Month Activity	<ul style="list-style-type: none"> • Balcony SS Railing top rail fixing work in wings-1 & 4 completed up to 12th floor lvl. • Internal Door shutters fixing work completed up to 11th floor lvl.
Up to Last Month Block B03	<ul style="list-style-type: none"> • Balance 25% 11th floor Roof slab casted.(Total 100%). • 100% 10th floor columns casted. • 12th floor columns 75% casted.(Total 100%). • 12th floor Roof slab 50% casted. • Brick work in 10th floor lvl 95% completed. • Brick work in 11th floor lvl is in progress. • Door frames fixing work completed in 8th floor lvl. • Balance 70% Internal plaster at 5th floor lvl completed.(Total 95%).
Current Month Activity	<ul style="list-style-type: none"> • Balance 12th floor Roof slab 50% casted.(Total 100%). • 13th floor columns 75% casted. • Brick work in 11th floor lvl 60% completed. • Door frames fixing work completed in 9th floor lvl. • Internal plaster completed in 8th & 9th floor lvl. • Internal Plaster is in progress at 10th floor lvl.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Up to Last Month Block C15	<ul style="list-style-type: none"> • Vdf flooring in stilt floor lvl 90% completed. • Stilt floor Toilets wall and floor tiling work 80% completed. • IWC fixing work completed from 1st to 11th floor lvl. • Tiles flooring in Indian Toilet completed up to 11th floor lvl. • Tiles flooring in corridor area completed in 11th floor lvl. • Machine Room Kota stone flooring work 75% completed. • Staircase stone skirting fixing work completed. • Aluminium Door window frames fixing work completed up to 3rd floor lvl. • SS balcony Railing fixing work is in progress at 6th floor lvl.(Total35% completed).
Current Month Activity	<ul style="list-style-type: none"> • Aluminium Door window glass fixing work 30% completed.(Total 90%). • Balcony SS Railing Top Rail fixing work completed at 11th floor lvl. • Internal door shutters fixing work is in progress. • Diverter fixing work completed up to 11th floor lvl.
Up to Last Month Block C16	<ul style="list-style-type: none"> • Stilt floor Toilets wall & floor tiling work 55% completed.(Total 95%). • Aluminum Door windows glass fixing completed from 1st floor to 9th floor lvl.(Total 98% completed). • Entry Teak door shutters fixing work completed from 4th to 9th floor lvl. • Internal Birla putty 2nd coat 10% completed.(Total 95%). • Plumbing shaft Louvers fixing work 5% completed.(Total 95%). • Balcony SS Railing fixing work 5% completed.(Total 95%). • Internal wiring work completed up to 6th floor lvl. • Internal Electrical fittings Switch sockets fixing work completed up to 5th floor lvl.
Current Month Activity	<ul style="list-style-type: none"> • Internal painting work 1st coat completed up to 4th floor lvl. • Plumbing shaft Louvers fixing work 3% completed.(Total 98%). • Balcony SS Railing fixing work 3% completed.(Total 98%). • Internal wiring work completed from 7th floor to 9th floor lvl. • Internal Electrical fittings Switch sockets fixing work completed from 6th floor to 9th floor lvl.
Up to Last Month Non-Tower	<ul style="list-style-type: none"> • VDF flooring 3% completed. (Total 98%). • Ramps-1 & 2 Vdf flooring work completed. • Fire fighting sprinkler Piping fittings fixing work is in progress. • Basement Water supply piping work is in progress. • Vdf flooring groove cutting work completed. • Vdf flooring Groove filling work 60% completed.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

Current Month Activity	
	<ul style="list-style-type: none">• Fire fighting sprinkler Piping fittings fixing work is in progress.• Basement Water supply piping work is in progress.• Vdf flooring Groove filling work 65% completed. (Total 95%).• Expansion Joint Casting work and Joint filling with waterproofing chemical is completed of length 150mtrs.• APP water proofing work 500Sqm area completed.• External Sewer Pipe line work 70mtrs completed.• External Sewer Excavation work is in progress.

(B) Status of Test Piles: -

Location	Status
Block B01, B02, B03, C15 & C16	Routine test completed.



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

PHOTOGRAPHS OF PACKAGE-V on 31st OCT-2019

View of Blocks B-01,B-02 ,C-15 & C-16



Progress Report No. 42 (1st OCT-19–31st OCT-19)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

In Block B-03 12th floor Roof slab 75% casted.



Progress Report No. 42 (1st OCT-19–31st OCT-19)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

**Basement Soil,waste & Rain water piping completed.
Firefighting piping work is in progress.**



Progress Report No. 42 (1st OCT-19–31st OCT-19)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

In Block B-01 Balcony SS Railing & Glass fixing work 95% completed.



Progress Report No. 42 (1st OCT-19–31st OCT-19)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

In Block C-15 SS Riling fixing work 95% completed.



Progress Report No. 42 (1st OCT-19–31st OCT-19)



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

Comparative Progress of Site works: -

PACKAGE-VI	STATUS AS ON 31/10/2019
Up to Last Month Boundary Wall	<ul style="list-style-type: none"> • Excavation for Boundary wall foundation of length 240 mtrs completed.Total (380/454 Mtrs). • PCC for Boundary wall foundation of length 204 mtrs completed. Total (344/454).
Current Month Activity	<ul style="list-style-type: none"> • Excavation for Boundary wall foundation of length 40 mtrs completed.Total (420/454 Mtrs). • PCC for Boundary wall foundation of length 76 mtrs completed. Total (420/454). • Boundary wall up to Plinth beam of length 65 mtrs casted. (Total 275mtrs) • Boundary wall Brick work of length 75 mtrs completed. • Boundary wall Railing of length 50mtrs completed. • Main gate-2 & 3 foundation PCC completed.
Up to Last Month Shopping.	<ul style="list-style-type: none"> • Excavation of Shopping Building completed. • PCC of Shopping building completed.
Current Month Activity	<ul style="list-style-type: none"> • Shopping building both Lift pits casted. • Shopping building foundation Reinforcement work 95% completed.
Up to Last Month Nursing	<ul style="list-style-type: none"> • Excavation of Nursing home completed. • PCC of Nursing home completed.
Current Month Activity	<ul style="list-style-type: none"> • Nursing home lift pits foundation PCC completed. • Layout work is in Progress.
Up to Last Month School	<ul style="list-style-type: none"> •
Current Month Activity	<ul style="list-style-type: none"> • School excavation work completed. • School foundation PCC work 180 Sqm completed.(180/574 Sqm).
Up to Last Month Non Tower Area	<ul style="list-style-type: none"> • Non Tower Excavation 1700 Sqm completed. • PCC of Non Tower area 1650 Sqm completed.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

Current Month Activity	<ul style="list-style-type: none">• Non tower area Excavation work 1200 Sqm completed.(Total 2900 /7645 Sqm)• Non tower area foundation PCC work 400 Sqm completed.(Total 2050/7645 Sqm).• Retaining wall footing Reinforcement binding work of length 50 mtrs completed.• Non Tower footing Reinforcement work is in progress.
-------------------------------	--



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

PHOTOGRAPHS OF PACKAGE-VI on 31st OCT-2019

Boundary wall Brick work & Railing above plinth is in progress.



Progress Report No. 42 (1st OCT-19–31st OCT-19)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

Shopping complex foundation Reinforcement 95% completed.



Progress Report No. 42 (1st OCT-19–31st OCT-19)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

QUALITY CONTROL

**DURING CONSTRUCTION FOLLOWING QUALITY CONTROL TESTS
CONDUCTED AT SITE:**

S. No.	Materials	Source From	Test Date	Frequency	Tests Done
1	Coarse Sand	Bajpur		As per Requirement	Sieve Analysis & Silt content
2	Coarse Aggregate	Nangal		As per Requirement	Sieve Analysis & Impact Value
3	Fine Sand	Yamuna Nagar		As per Requirement	Sieve Analysis & Silt content
4	Bricks	Greater Noida		As per Requirement	Dimension, Water Absorption & Compressive strength
5	Wood			As per Requirement	Wood Moisture content
6	Cement			Third party testing is being done	
7	Steel			Third party testing is being done	
8	Piles Integrity			Third party testing is being done	
9	Soil Compaction			Third party testing is being done	
10	STP water			Third party testing is being done	
11	RCC Cubes are being tested and Register is being maintained.				
12	Slump test conducted at site to insure workability if concrete.				



CUBE COMPRESSIVE STRENGTH TESTING.



COARSE SAND SIEVE ANALYSIS TESTING.



BRICK COMPRESSIVE STRENGTH TESTING



20MM IMPACT VALUE TESTING



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

**ALUMINIUM DOOR AND WINDOW
MANUFACTURING BY SCHUCO AT SITE**



Progress Report No. 42 (1st OCT-19–31st OCT-19)



ALUMINIUM DOOR AND WINDOW
MANUFACTURING BY SCHUCO AT SITE



ALUMINIUM DOOR AND WINDOW
MANUFACTURING BY SCHUCO AT SITE

