

MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

30th Sept-2019

(A) Comparative Progress of Site works: -

PACKAGE-II	STATUS AS ON 30/09/2019
Up to Last Month Block D03	<ul style="list-style-type: none"> • Terrace GI water Supply Piping work 45% completed. (Total 75%). • Tiles flooring in Indian Toilet completed from 11th to 14th floor lvl.. • Balcony Tiles flooring completed from 10th to 14th floor lvl. • Aluminum Door window glass fixing work completed from 1st to 14th floor lvl. • Staircase-1 M.S. Railing completed from 3rd to 14th floor lvl. • Staircase -2 M.S. Railing completed from 14th to 10th floor lvl. • S.S. Balcony Railing fixing work completed up to 2nd floor lvl. • Internal Fire Hose drum fixing completed from 1st to 14th floor lvl. • Internal 2nd coat Birla putty work completed from 4th to 14th floor lvl. •
Current Month Activity	<ul style="list-style-type: none"> • Terrace GI water Supply Piping work 20% completed. (Total 95%). • Aluminum Door window DW-7 in Kitchen fixing completed up to 14th floor lvl. • Staircase-1 M.S. Railing completed from Basement to 3rd floor lvl. • Staircase -2 M.S. Railing completed from 1st to 10th floor lvl. • S.S. Balcony Railing fixing work completed from 3rd to 7th floor lvl. • Staircase-1 stone flooring fixing completed from stilt to 7th floor lvl. • Staircase-2 stone flooring fixing completed from 1st to 3rd floor lvl. • Tiles flooring in corridor completed from 1st to 14th floor lvl. • Internal 1st coat Painting work completed from 1st to 14th floor lvl. • Aluminium louvers in Plumbing shafts fixing work completed up to 5th floor lvl.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Up to Last Month Block D04	<ul style="list-style-type: none"> • Brick coba water proofing work in wing-1 finishing completed and in wings-2,3 & 4 in progress. • Tiles flooring in Living, Bed rooms,Balcony and Toilets completed from 12th to 14th floor lvl. • Tiles dado in Toilets & Kitchen completed from 12th to 14th floor lvl. • Internal 2nd coat Birla putty work completed in 1st floor lvl. • PCC for VD flooring completed in wings-2 & 3. • Basement Brick work 35% completed. • Internal Fire Hose drum fixing completed from 1st to 14th floor lvl. •
Current Month Activity	<ul style="list-style-type: none"> • Terrace floor Brick coba water proofing work 100% completed. • Internal 2nd coat Birla putty work completed from 1st to 7th floor lvl. • Aluminium door window frames fixing work completed from 1st to 5th floor lvl. • Basement Brick work 65% completed.(Total 100%). • Stilt floor Brick work 100% completed. • Terrace floor GI water supply piping work 90% completed.
Up to Last Month Block D05	<ul style="list-style-type: none"> • Parasol slab ,Mummtty and Machine Room internal Plaster work completed. • Projection slab above Machine Room Roof 30% casted.(Total 100%). • Toilets Water proofing completed from 7th to 12th floor lvl. • Tiles Dado work in Toilets & Kitchen completed up to 3rd floor lvl. • Tiles flooring work completed in 1st floor lvl. • Kitchen counter stone fixing work completed from 13th to 14th floor lvl. • Basement floor PCC work 100% completed. • Internal wet Riser piping fixing completed up to 14th floor lvl. • Internal Fire Hose drum fixing completed from 1st to 14th floor lvl. •
Current Month Activity	<ul style="list-style-type: none"> • Toilets Water proofing completed from 13th to 14th floor lvl. • Tiles Dado work in Toilets & Kitchen completed from 4th to 8th floor lvl. • Tiles flooring work completed from 2nd to 8th floor lvl. • Stilt floor Brick work 95% completed. • Terrace Brick coba water proofing work is in progress. • Terrace GI Water supply piping work is in Progress.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Up to Last Month Block D06	<ul style="list-style-type: none"> • Terrace Parasol 10% casted.(Total 85%). • Balcony RCC wall casted up to 4th floor lvl. • External Plaster 10% completed. (Total 50%). • External Birla putty 1st coat 10% completed.(Total 25%) • Basement floor PCC work 100% completed. • Internal Fire Hose drum fixing completed from 1st to 14th floor lvl.
Current Month Activity	<ul style="list-style-type: none"> • Over Head water tank RCC wall casted. • Balcony RCC wall casted from 5th to 14th floor lvl. • External Plaster 10% completed. (Total 60%). • Balcony water proofing work completed up to 9th floor lvl. • Internal Birla putty 1st coat completed up to 14th floor lvl. • Basement & Stilt floor Brick work completed.
Up to Last Month Block D07	<ul style="list-style-type: none"> • 100% 13th floor columns casted. • 100% 13th floor Roof slab casted. • 50% 14th floor columns casted. • Balance 50% Brick work in 9th floor lvl completed. • 10th floor lvl Brick work 80% completed.
Current Month Activity	<ul style="list-style-type: none"> • Balance 50% 14th floor columns casted. (Total 100%) • 14th floor Roof slab Reinforcement binding work in wings-1 & 4 completed. • Balance 50% Brick work in 9th floor lvl completed. • 11th & 12th floor lvl Brick work 90% completed. • Balcony RCC wall casted up to 6th floor lvl.
Up to Last Month Block D08	<ul style="list-style-type: none"> •
Current Month Activity	<ul style="list-style-type: none"> •
Up to Last Month Non-Tower	<ul style="list-style-type: none"> • Pile caps 30 nos casted. (Total 327/350). • PCC below VDF 500 Sqm completed. (Total 10820/16656Sqm). • Basement Ceiling Plaster 480 Sqm completed. (Total 10255/16656Sqm). • 20 Nos Circular columns plaster completed.(Total 148/290). • Basement Soil,waste and Rain water piping work 20% completed.(Total 50%). • Basement firefighting piping work is in progress.
Current Month Activity	<ul style="list-style-type: none"> • PCC below VDF 840 Sqm completed. (Total 11660/16656Sqm). • Basement Ceiling Plaster 550 Sqm completed. (Total 10805/16656Sqm). • 42 Nos Circular columns plaster completed.(Total 190/290). • Basement Soil,waste and Rain water piping work 15% completed.(Total 65%). • Vdf flooring 2936 Sqm completed. (Total 6386/16656). • Basement Firefighting piping work 2% completed.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Up to Last Month Retaining Wall	<ul style="list-style-type: none">•
Current Month Activity	<ul style="list-style-type: none">• Retaining wall 1st lift 40mtrs casted.• Retaining wall 2nd lift 15mtrs casted.



MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT
PHOTOGRAPHS OF PACKAGE-II on 30th SEPT-2019

Block D-03 Balcony SS Railing fixing completed up to 7th floor lvl.
In Block D-03 Aluminium door window frames with glass fixing completed.



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

In Block D-06 Machine Room Slab Reinforcement work is in progress & Block D-07 14th floor Roof slab 50% casted.



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

Block D-05 Brick coba waterproofing is in progress.



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

Block D-04 Aluminum Door window frames fixing is in progress.



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

In Block D-05 Brick Coba waterproofing is in progress.



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT
Sample flat entrance door fixed.




Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

Staircase stone flooring and M.S.railing work completed.

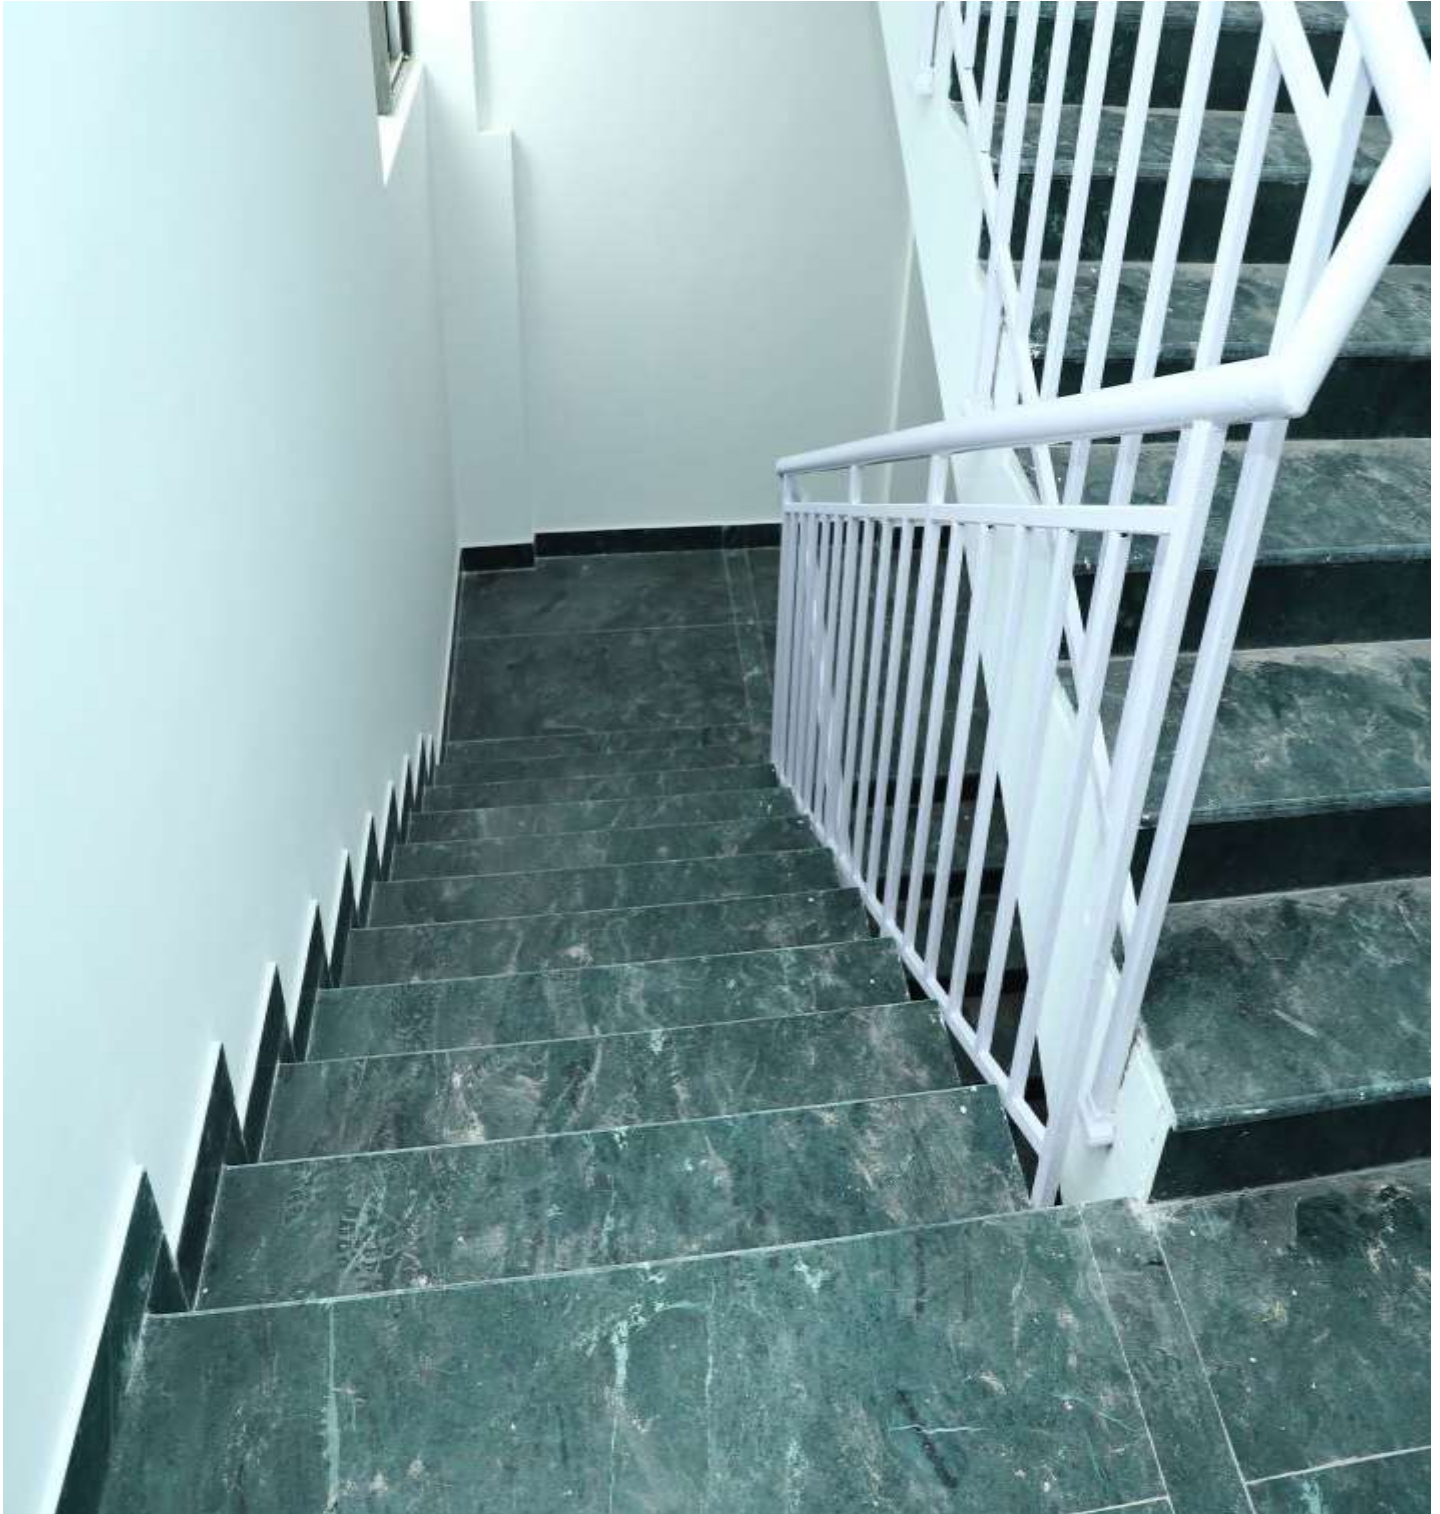


Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

Basement CI Piping (Soil, waste & Rain water) is in progress.

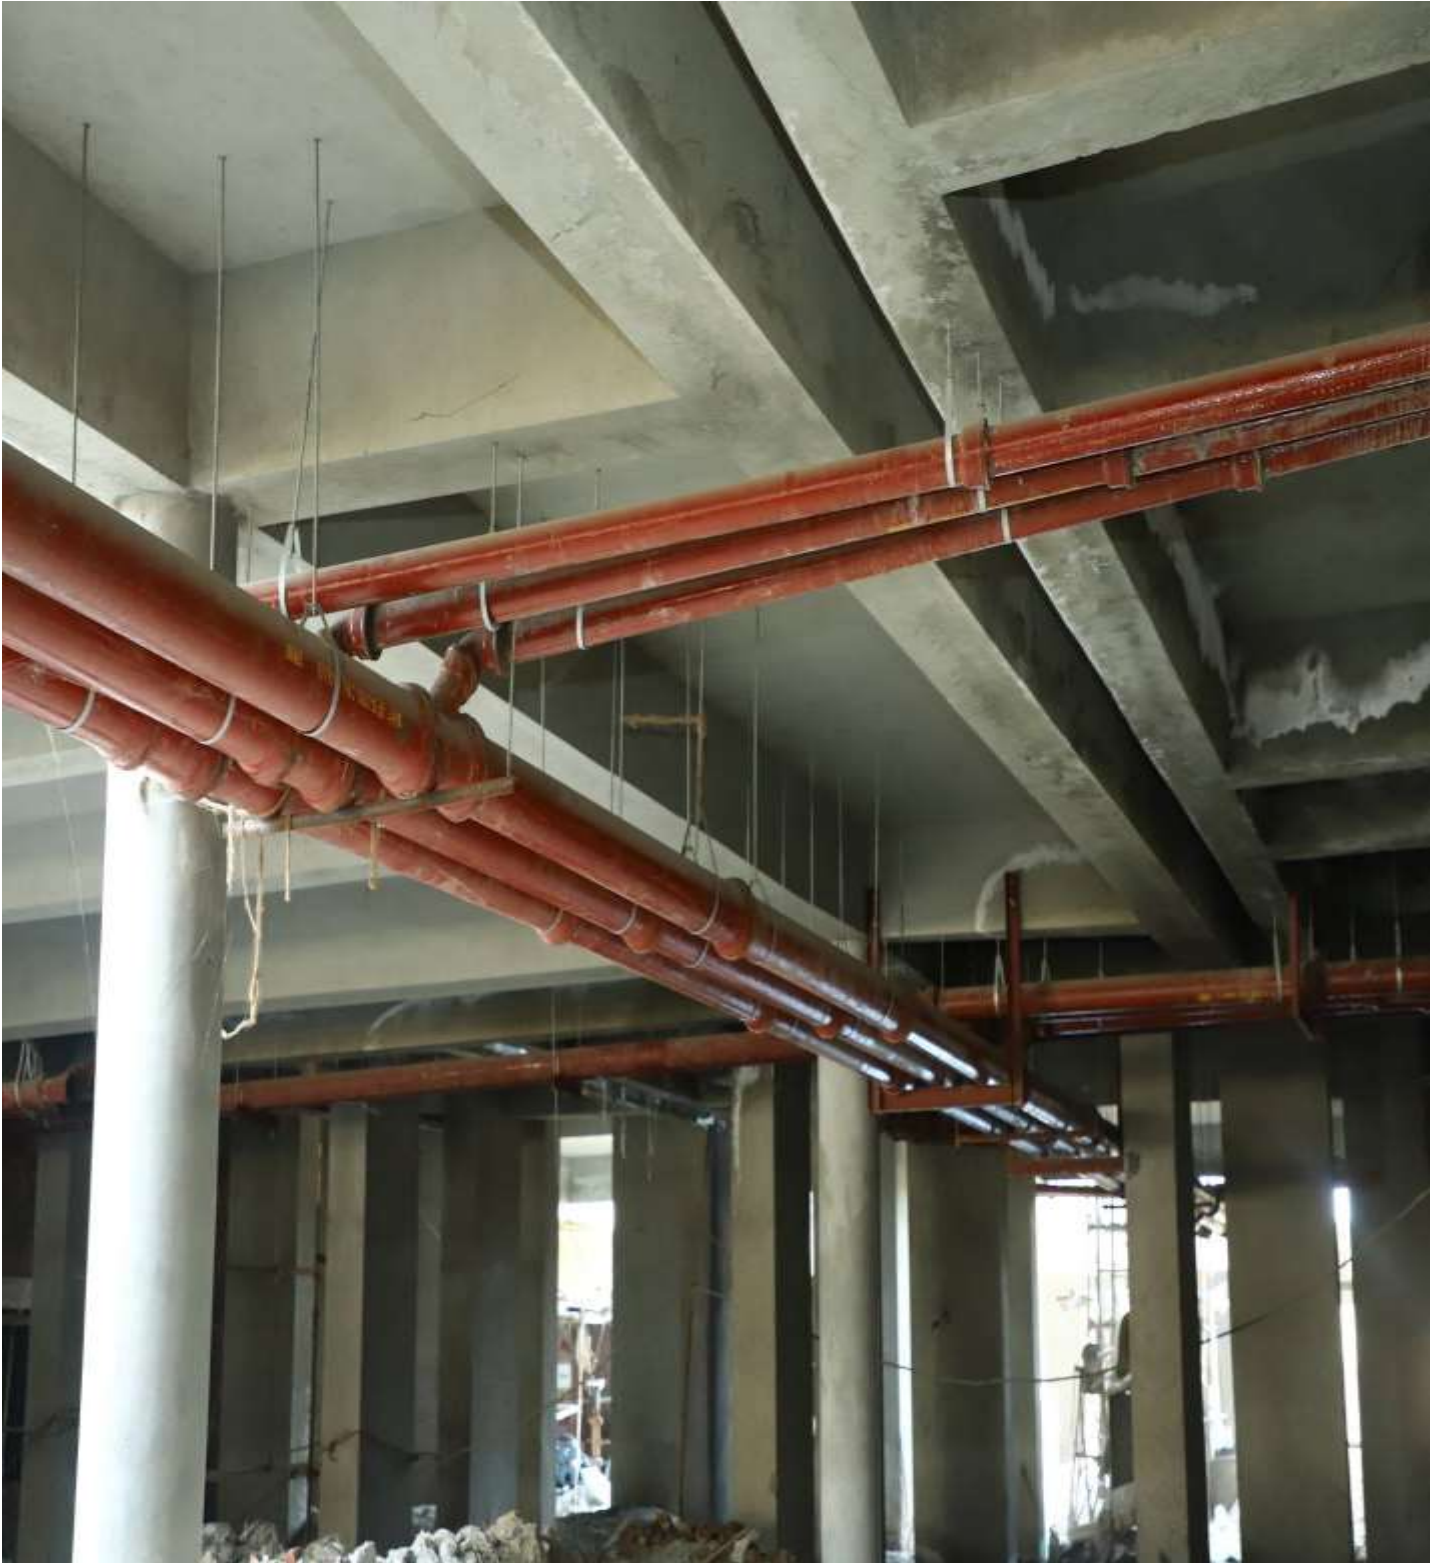

Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

Basement Firefighting Piping work is in progress.



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

PACKAGE-III	STATUS AS ON 30/09/2019
Up to Last Month Block C01	<ul style="list-style-type: none"> • Level 15(Terrace): 100% slab casting completed. <ul style="list-style-type: none"> ▪ Reinforcement of stub column of projection slab is on progress. ▪ Mumty column & slab casting completed. ▪ Machine room column shuttering and reinforcement is on progress. • Level 14: Brick work completed. • Level 13: Door frame completed. • Level 14: Door frame is on progress. • Level 11: Internal plaster completed. • Level 12: Internal plaster is on progress. • Level 13: Electrical wall conduit completed. • Level 14: Electrical wall conduit is on progress. • Level 13: Internal plumbing (CPVC) work completed. • Level 14: Internal plumbing (CPVC) work is on progress.
Current Month Activity	<ul style="list-style-type: none"> • Level 15(Terrace): 100% slab casting completed. <ul style="list-style-type: none"> ▪ Terrace projection column 100% & slab 50% casting completed & remaining reinforcement is on progress. ▪ Mumty column & slab casting completed. ▪ Overhead tank column & base slab casted completed & wall shuttering is on progress. • Level 14: Brick work completed. • Level 14: Door frame completed. • Level 11: Internal plaster completed. • Level 12: Internal plaster is on progress. • Level 13: Electrical wall conduit completed. • Level 14: Electrical wall conduit is on progress. • Level 13: Internal plumbing (CPVC) work completed. • Level 14: Internal plumbing (CPVC) work is on progress. • Level 01-03: POP cornice completed. • Level 04: POP cornice is on progress.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

<p>Up to Last Month</p> <p>Block C02</p>	<ul style="list-style-type: none"> • Level 15 (Terrace): 100% slab casting completed. <ul style="list-style-type: none"> ▪ Stub column of projection slab casting completed. ▪ Terrace elevation of parapet wall casting completed. ▪ Mumty slab casting completed. ▪ Machine room column casting completed. ▪ Over Head tank wall reinforcement work completed and shuttering work is on progress. • Level 14: Brick work 100% completed. • Level 14: Door frame completed. • Level 14: Internal plaster completed. • Level 14: Electrical wall conduit completed. • External plaster 75% completed. • Level 03 to 08: Water proofing completed. • Level 09: Water proofing is on progress. • Level 02: Wall tile (Toilet & Kitchen) completed. • Level 03: Wall tile (Toilet & Kitchen) is on progress. • Level 14: Internal plumbing (CPVC) work completed. • Level 14: External & internal plumbing (CI) work completed. • Level 01: POP cornice is on progress.
<p>Current Month Activity</p>	<ul style="list-style-type: none"> • Level 15 (Terrace): 100% slab casting completed. <ul style="list-style-type: none"> ▪ Terrace stub column & projection slab 100% casting completed. ▪ Mumty column & slab casting completed. ▪ Over Head tank base slab & wall casting completed. ▪ Machine room column casting completed & slab shuttering work is on progress. • Level 14: Brick work 100% completed. • Level 14: Door frame completed. • Level 14: Electrical wall conduit completed. • Level 14: Internal plaster completed. • External plaster 90% completed. • Level 01 to 08: Water proofing completed. • Level 09: Water proofing is on progress. • Level 01-05: Wall tile (Toilet & Kitchen) completed. • Level 06: Wall tile (Toilet & Kitchen) is on progress. • Level 14: Internal plumbing (CPVC) work completed. • Level 14: External & internal plumbing (CI) work completed. • Level 14: POP cornice completed.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

<p>Up to Last Month</p> <p>Block C06</p>	<ul style="list-style-type: none"> • Level 15(Terrace): 100% slab casting completed. <ul style="list-style-type: none"> ▪ Stub column of projection slab casting completed. ▪ Terrace elevation of parapet wall casting completed. ▪ Mumty slab 100% completed. ▪ Overhead tank base slab & wall casting completed. ▪ Machine room slab casting completed & machine room projection slab shuttering is on progress. • Level 14: Brick work completed. • Level 14: Door frame completed. • Level 14: Electrical wall conduit completed. • Level 14: Internal plaster completed. • External plaster 85% completed. • Level 12 &13: Water proofing completed. • Level 14: Water proofing is on progress. • Level 05 to 10: Wall tile (Toilet &Kitchen) completed. • Level 11: Wall tile (Toilet & kitchen) is on progress. • Level 14: Internal plumbing (CPVC) work completed. • Level 14: External & internal plumbing (CI) work completed. • Level 14: External vertical (GI) work completed. • Level 01-05: POP cornice completed.
<p>Current Month Activity</p>	<ul style="list-style-type: none"> • Level 15(Terrace): 100% slab casting completed. <ul style="list-style-type: none"> ▪ Terrace Stub column & projection slab casting completed. ▪ Mumty column & slab completed. ▪ Overhead tank base slab & wall casting completed. ▪ Machine room column & slab casting completed. ▪ Projection above machine room casting completed. • Level 14: Brick work completed. • Level 14: Door frame completed. • Level 14: Electrical wall conduit completed. • Level 14: Internal plaster completed. • External plaster 95% completed. • Level 14: Water proofing completed. • Level 11-14: Wall tile (Toilet &Kitchen) completed. • Level 14: Internal plumbing (CPVC) work completed. • Level 14: External & internal plumbing (CI) work completed. • Level 14: External vertical (GI) work completed. • Level 06-14: POP cornice completed. • Level 01-10: Wall putty completed. • Level 11: Wall putty is on progress.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

Up to Last Month

Block C07

- Level 15(Terrace): 100% slab casting completed.
 - Reinforcement of stub column of projection slab is on progress.
 - Mumty slab 100% completed.
 - Overhead tank base slab & Wall casting completed.
 - Machine room slab shuttering and reinforcement work is on progress.
- Level 14: Brick work 100% completed.
- Level 14: Door frame completed.
- Level 14: Internal plaster completed.
- External plaster 89% completed.
- Level 14: Electrical wall conduit completed.
- Level 13 & 14: Water proofing completed.
- Level 13 & 14: Wall tile (Toilet & Kitchen) completed.
- Level 01-05: Floor tile completed Except balcony.
- Level 06: Floor tile is on progress.
- Level 14: Internal plumbing (CPVC) work completed.
- Level 14: External & internal plumbing (CI) work completed.
- Level 14: External vertical (GI) work completed.
- Level 01-09: POP cornice completed.
- Level 10- POP cornice is on progress.



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

Current Activity	Month	
		<ul style="list-style-type: none">• Level 15(Terrace): 100% slab casting completed.<ul style="list-style-type: none">▪ Terrace Stub column casting completed & projection slab shuttering is on progress.▪ Mumty column & slab completed.▪ Overhead tank base slab & wall casting completed.▪ Machine room column & slab casting completed.▪ Projection above machine room reinforcement work is on progress.• Level 14: Brick work 100% completed.• Level 14: Door frame completed.• Level 14: Internal plaster completed.• External plaster 90% completed.• Level 14: Electrical wall conduit completed.• Level 14: Water proofing completed.• Level 14: Wall tile (Toilet & Kitchen) completed.• Level 06-10: Floor tile completed.• Level 11: Floor tile is on progress.• Level 14: Internal plumbing (CPVC) work completed.• Level 14: External & internal plumbing (CI) work completed.• Level 14: External vertical (GI) work completed.• Level 10-13: POP cornice completed.• Level 14: POP cornice is on progress.• Level 01-03: Wall putty is completed.• Level 04: Wall putty is on progress.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

<p>Up to Last Month</p> <p>Block C08</p>	<ul style="list-style-type: none"> • Level 15(Terrace): 100% slab casting completed. <ul style="list-style-type: none"> ▪ Stub column of projection slab casting completed. ▪ Terrace elevation of parapet wall casting completed. ▪ Mumty slab 100% completed. ▪ Overhead tank base slab & wall casting completed. ▪ Machine room slab casting completed. ▪ Projection above machine room casting completed. • Level 14: Brick work 100% completed. • Level 14: Door frame completed. • Level 14: Internal plaster completed. • External plaster 95% completed. • Level 14: Electrical wall conduit completed. • Level 01 to 14: Water proofing completed. • Level 14: Wall tile (Toilet & kitchen) completed. • Level 13: Floor tile completed. • Level 14: Floor tile is on progress. • Level 14: Internal plumbing (CPVC) work completed. • Level 14: External & internal plumbing (CI) work completed. • Level 14: External vertical (GI) work completed. • Level 01-07: POP cornice completed. • Level 08: POP cornice is on progress.
<p>Current Month</p> <p>Activity</p>	<ul style="list-style-type: none"> • Level 15(Terrace): 100% slab casting completed. <ul style="list-style-type: none"> ▪ Stub column of projection slab casting completed. ▪ Terrace elevation of parapet wall casting completed. ▪ Mumty slab 100% completed. ▪ Overhead tank base slab & wall casting completed. ▪ Machine room slab casting completed. ▪ Projection above machine room casting completed. • Level 14: Brick work 100% completed. • Level 14: Door frame completed. • Level 14: Internal plaster completed. • External plaster 95% completed. • Level 14: Electrical wall conduit completed. • Level 01 to 14: Water proofing completed. • Level 14: Wall tile (Toilet & kitchen) completed. • Level 13: Floor tile completed. • Level 14: Floor tile is on progress. • Level 14: Internal plumbing (CPVC) work completed. • Level 14: External & internal plumbing (CI) work completed. • Level 14: External vertical (GI) work completed. • Level 08-12: POP cornice completed. • Level 13: POP cornice is on progress. • Level 01-07: Wall putty completed. • Level 08: Wall putty is on progress.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

<p>Up to Last Month</p> <p>Block C09</p>	<ul style="list-style-type: none"> • Level 04: Remaining 50% column casting completed. • Level 05: 100% slab & 50% column casting completed. • Level 01: Brick work completed. • Level 02: Brick work is on progress.
<p>Current Month Activity</p>	<ul style="list-style-type: none"> • Level 05: Remaining 50% column casting completed. • Level 06: 100% Slab casting is on progress & column reinforcement is on progress. • Level 02-03: Brick work completed. • Level 04: Brick work is on progress.
<p>Up to Last Month</p> <p>Block C10</p>	<ul style="list-style-type: none"> • Level 00: 100% column casting completed. • Level 01: 100% slab casting & 50% column casting completed.
<p>Current Month Activity</p>	<ul style="list-style-type: none"> • Level 01: Remaining 50% column casting completed. • Level 02: 100% slab casting completed & column reinforcement work is on progress.
<p>Up to Last Month</p> <p>Block C11</p>	<ul style="list-style-type: none"> • Level 09: Remaining 50% slab & 100% column casting completed. • Level 04: Brick work 100% completed. • Level 05: Brick work is on progress. • Level 01-03: Door frame completed. • Level 04: Door frame is on progress. • Level 01-03: Electrical wall conduit completed • Level 04: Electrical wall conduit is on progress.
<p>Current Month Activity</p>	<ul style="list-style-type: none"> • Level 10: 100% slab & column casting completed. • Level 05: Brick work 100% completed. • Level 06: Brick work is on progress. • Level 04: Door frame completed. • Level 05: Door frame is on progress. • Level 03: Electrical wall conduit completed. • Level 04: Electrical wall conduit is on progress. • Level 01-02: Internal plaster completed. • Level 03: Internal plaster is on progress.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

<p>Up to Last Month</p> <p>Block C12</p>	<ul style="list-style-type: none"> • Level 15(Terrace): 100% slab casting completed. <ul style="list-style-type: none"> ▪ Mumty column casted & Slab shuttering is on progress. • Level 11: Brick work 100% completed. • Level 12: Brick work is on progress. • Level 10: Door frame completed. • Level 11: Door frame is on progress. • Level 08 & 09: Internal plaster completed. • Level 10: Internal plaster is on progress. • Level 09 & 10: Electrical wall conduit completed. • Level 11: Electrical wall conduit is on progress. • Level 08: Internal plumbing (CPVC) work completed. • Level 09: Internal plumbing (CPVC) work is on progress.
<p>Current Month</p> <p>Activity</p>	<ul style="list-style-type: none"> • Level 15(Terrace): 100% slab casting completed. <ul style="list-style-type: none"> ▪ Terrace projection column 100% reinforcement completed.. ▪ Mumty column & slab casting completed. ▪ Overhead tank column casting completed & base slab reinforcement work is on progress. • Level 12-13: Brick work 100% completed. • Level 13: Brick work is on progress. • Level 11-12: Door frame completed. • Level 13: Door frame is on progress. • Level 09-10: Internal plaster completed. • Level 11: Internal plaster is on progress. • Level 11-12: Electrical wall conduit completed. • Level 13: Electrical wall conduit is on progress. • Level 09: Internal plumbing (CPVC) work completed. • Level 10: Internal plumbing (CPVC) work is on progress.
<p>Up to Last Month</p> <p>UG Tank</p>	<ul style="list-style-type: none"> • U.G. Tank 100% slab casting completed & remaining slab shuttering is in progress.
<p>Current Month</p> <p>Activity</p>	<ul style="list-style-type: none"> • U.G. Tank 100% slab casting completed & remaining slab shuttering is in progress.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

Up to Last Month Non-Tower	<ul style="list-style-type: none">• Pile casting completed. (848/848) Nos.• Laying P.C.C completed. (Total 16867/18731) Sqm• Stitch slab casting completed. (Total 16658/18731) Sqm• Circular column casting completed. (Total 275/339) Nos.• Basement non-tower slab casting completed Total (10635/18731) Sqm• Retaining wall casting completed (275/294) m
Current Month Activity	<ul style="list-style-type: none">• Basement non-tower slab 982 sqm casting completed Total (11617/18731) Sqm• Retaining wall 2mtr casted (277/294) rmt• Laying P.C.C 390 m2 (17257/18731) m2• Circular column 19 nos. casting. (Total 294/339) Nos.



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

PHOTOGRAPHS OF PACKAGE-III on 30th Sept-2019

Block C-09 Level -06 column reinforcement is on progress.

Block C-10 Level -02 column reinforcement is on progress.

Block C-11 Level-11 slab shuttering is on progress.



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Block C-09 Level -06 column reinforcement is on progress.

Block C-10 Level -02 column reinforcement is on progress.

Block C-11 Level-11 slab shuttering is on progress.



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Block C-06 Above terrace machine room brick work is on progress.

Block C-07 Projection above machine room reinforcement is on progress.

Block C-08 Above terrace brick coba is on progress.



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Block C-01 Above terrace over head tank wall shuttering is on progress.
Block C-02 Above terrace machine room slab shuttering work is on progress.
Block C-12 Above terrace over head tank base slab reinforcement is on progress.



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

PACKAGE-IV	STATUS AS ON 30/09/2019
Block A01 UpTo Last Month	<ul style="list-style-type: none"> • 98% Above Terrace water supply distribution work completed. • First to Sixth floor Main door teak fixing work completed. • All floor Indian toilet WC fixing work completed. • All Indian Toilet floor tile fixing work completed. • All floor shaft louvers fixing work completed. • 90% Making and fixing of aluminum windows work completed. • Staircase MS railing fixing work completed. • Staircase Stone fixing work completed. • 100% RCC, Brick work, Internal plaster, SCI, POP Cornices, Wall tiles, Floor tiles and Wall putty work completed. • 95% External plaster work completed. • 90% External wall putty one coat work completed.
Current Month Activity	<ul style="list-style-type: none"> • Machine room Kota Stone fixing work completed. • Wall primer work completed with common passage. • 1st coat of paint work from 1st to 3rd floor in flats completed. • Electrical wiring work on 2nd to 8th floor completed. • SS balcony railing work fixing started. • 60% Stilt floor VDF flooring work completed. • Overhead tank MS ladder fixing work completed. • 100% RCC, Brick work, Internal plaster, SCI, POP Cornices, Wall tiles, Floor tiles and Wall putty work completed.
Block B04 UpTo Last Month	<ul style="list-style-type: none"> • 98% Above Terrace water supply distribution work completed. • Machine room kota stone fixing work completed. • All floor Indian toilet WC fixing work completed. • Second floor balcony SS railing fixing work completed. • Up to Sixth floor shaft Louvers fixing work completed. • All floor Staircase MS railing fixing work completed. • All floor Second coat wall putty work completed. • Primer on wall completed in all floors. • 100% RCC, Brick work, Internal plaster, SCI, POP Cornices, Floor tiles, Wall tiles and Wall putty work completed. • 95% External plaster work completed. • 95% External wall putty work completed.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Current Month Activity	<ul style="list-style-type: none"> • SS Balcony railing fixing work completed all floors. • Shaft louvers fixing work completed all floors. • 1st coat Paint work completed in flats and common passage at all floors. • Overhead tank MS ladder fixing work completed. • 3rd floor main frame fixing of aluminium door and windows work completed. • Internal Door shutter work from 1st to 6th floor completed. • Staircase Baroda Green fixing work from Stilt to 11th floor completed. • 100% RCC, Brick work, Internal plaster, SCI, POP Cornices, Floor tiles, Wall tiles and Wall putty work completed.
Block B05 UpTo Last Month	<ul style="list-style-type: none"> • All floor Staircase MS railing fixing work completed. • All floor Staircase Stone fixing work completed. • All floor Indian toilet WC fixing work completed. • Aluminum windows frame fixing work completed. • All Indian toilets floor tile fixing work completed. • 98% Above Terrace water supply distribution work completed. • All floor second coat wall putty work completed. • Primer on wall completed. • 100% RCC, Brick work, Internal plaster, SCI, POP Cornices, Wall tiles, Floor tiles and Wall putty work completed. • 95% External plaster work completed. • 95% External one coat wall putty work completed.
Current Month Activity	<ul style="list-style-type: none"> • 1st coat of Paint work completed in flat and common passage at all floors. • SS Balcony railing fixing work up to 5th floor completed. • Internal Door shutter work from 1st to 8th floor completed. • Overhead tank MS ladder fixing work completed. • All floors shaft louvers fixing work completed. • 50%Stilt floor VDF flooring work completed. • Stilt to basement CI connection work completed. • 100% RCC, Brick work, Internal plaster, SCI, POP Cornices, Wall tiles, Floor tiles and Wall putty work completed.
Block C13 UpTo Last Month	<ul style="list-style-type: none"> • All floor S.S Balcony railing work completed. • All floor shaft Louvers fixing work completed. • Primer on wall completed all floors. • All floor Indian toilet WC fixing work completed. • Ninth floor Main teak wood shutter fixing work in progress. • All floor Main door teak fixing work completed. • Aluminium door window making and fixing work completed. Without mesh doors. • 100% RCC, Brick work, Internal plaster, SCI, POP Cornices, Wall putty, Floor Tiles, Wall Tiles, staircase railing work completed. • External plaster work completed. • External one coat wall putty work completed.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Current Month Activity	<ul style="list-style-type: none"> • 1st coat paint work completed common passage. • Overhead tank MS ladder fixing work completed. • Machine room MS railing fixing work completed. • Staircase Baroda green fixing work completed. • 1st coat paint work at 2nd to 3rd floor completed. • Electrical wiring work on 2nd to 3rd floor completed. • 50%Stilt floor VDF flooring work completed. • 100% RCC, Brick work, Internal plaster, SCI, POP Cornices, Wall putty, Floor Tiles, Wall Tiles, staircase railing work completed.
Block C14 UpTo Last Month	<ul style="list-style-type: none"> • Ninth floor Main teak wood shutter fixing work in progress. • Primer on wall completed all floors. • Ninth Electrical wiring work completed. • All floor Indian toilet WC fixing work completed. • Machine room staircase work completed. • All floor shaft Louvers fixing work completed. • Aluminium door window making and fixing work completed. Without mesh doors. • 100% RCC, Brick work, Internal plaster, SCI, POP Cornices, Wall putty, Wall Tiles, Floor tiles work completed.
Current Month Activity	<ul style="list-style-type: none"> • Overhead tank MS ladder fixing work completed. • Machine room railing work completed. • 1st coat paint work common passage work completed. • 1st coat paint work on 2nd to 6th floor completed. • Electrical wiring work completed at all floors. • Electrical switches and MCB work completed all floors. • 30%Stilt floor VDF flooring work completed. • 100% RCC, Brick work, Internal plaster, SCI, POP Cornices, Wall putty, Wall Tiles, Floor tiles work completed.
Block C03 UpTo Last Month	<ul style="list-style-type: none"> • 100% RCC, Brick work, Door frame, SCI, POP Cornice, Wall tiles work completed. • Fourteen floor flat tile fixing work in progress. • Machine room kota stone fixing work in progress. • All floor Indian toilet WC fixing work completed. • Ninth floor second coat wall putty work completed. • 90% Terrace GI water supply ring work completed. • All floor staircase railing work completed. • External plaster above terrace machine room in progress. • 95% External plaster work completed. • 95% External one coat wall putty work completed.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Current Month Activity	<ul style="list-style-type: none"> • All flats internal tile fixing work completed. • Overhead tank MS ladder fixing work completed. • Machine room kota stone fixing work completed. • All floor second coat wall putty work completed. • Machine room staircase MS railing fixing work completed. • Lift shafts one coat OBD work completed. • Machine room white wash work completed. • 2nd coat wall putty work completed all floors. • Wall primer work completed at all flats. • Common passage floor tiles fixing work is completed. • 100% RCC, Brick work, Door frame, SCI, POP Cornice, Wall tiles work completed
Block C04 UpTo Last Month	<ul style="list-style-type: none"> • Thirteen floor tile fixing work in progress. • All floor wall tile fixing work completed. • Twelfth floor Indian WC fixing work in progress. • Staircase MS railing fixing work completed. • Machine room kota stone fixing work completed. • 90% Terrace GI water supply ring work completed. • 80% terrace coba work completed. • 100% RCC, Brick work, Door frame, SCI, POP Cornice, Wall tiles work completed. • 95% External plaster and one coat wall putty work completed.
Current Month Activity	<ul style="list-style-type: none"> • All floor tile fixing work completed. • All floor Indian WC fixing work completed. • Overhead tank MS ladder fixing work completed. • Machine room staircase MS railing fixing work completed. • Machine room whitewash work completed. • Lift shaft whitewash completed. • 1st coat putti work completed in staircase and common passage. • Floor tile fixing work completed in all floors. • Indian WC fixing work completed in all floors. • Wall Primer work completed in all floors. • Floor tile fixing work completed on 8th floor and common passage. • 2nd Coat putty work completed in all floors. • 100% RCC, Brick work, Door frame, SCI, POP Cornice, Wall tiles work completed
Block C05 UpTo Last Month	<ul style="list-style-type: none"> • 100% RCC, brick work, Internal plaster, Door frame, SCI work completed. • All floor toilets wall tile fixing work completed. • Mumty machine room internal plaster work in progress. • All floor one coat wall putty work completed. • 90% Terrace GI water supply ring work completed. • 90% External plaster work completed. • 80% terrace coba work completed.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Current Month Activity	<ul style="list-style-type: none"> • Floor tile fixing work on 8th to 14th floor is completed. • Overhead tank MS ladder fixing work completed. • Mumty machine room internal plaster work completed. • Machine room One coat OBD completed. • External putty work completed in machine room. • Mumty machine room internal plaster work completed. • 1st coat putty work completed in staircase and common passage. • Terrace level Brick coba work completed. • Kitchen Counter work completed all floors. • POP cornice work completed in all floors. • 100% RCC, brick work, Internal plaster, Door frame, SCI work completed
Non-Tower UpTo Last Month	<ul style="list-style-type: none"> • 150 sqm basement slab casting work completed near Ramp-03. • 99% Retaining Wall work completed. • 309 M Boundary wall columns, Tie beams casting and brick work completed. • 510 R/M RCC Drain work completed. • 200 Sqm PCC for basement flooring work completed. (15500/15900sqm) • 4200 Sqm VDF for basement flooring work completed. (11700/15806 sqm) • 90% SCI work in basement ceiling fixing work completed. • 50% Fire fighting work in basement ceiling work completed. • ATT work in progress below PCC. • 95% Kota stone water proofing work completed.
Current Month Activity	<ul style="list-style-type: none"> • 99% Retaining Wall work completed. • 309 M Boundary wall columns, Tie beams casting and brick work completed. • 550 R/M RCC Drain work completed. • 200 Sqm PCC for basement flooring work completed. (15800/15900sqm) • 3000 Sqm VDF for basement flooring work completed. (14700/15806 sqm) • 95% SCI work in basement ceiling fixing work completed. • 70% Firefighting work in basement ceiling work completed. • ATT work in progress below PCC. • 95% Kota stone water proofing work completed.
Sample Flat Type A, B & C Status	<ul style="list-style-type: none"> • Painting work of walls & Ceiling completed. • Tile fixing work completed. • Internal Electrical work completed. • Water supply & Drainage work completed.



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

PHOTOGRAPHS OF PACKAGE-IV on 30th SEPTEMBER -2019

BIRD EYE VIEW OF PROJECT.



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

STILT FLOOR VDF FLOORING




**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

**STAIRCASE MS RAILING AND BARODA GREEN
COMPLETED.**



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

CORIDOOR FLOOR TILE FIXING AND MAIN DOOR FIXING

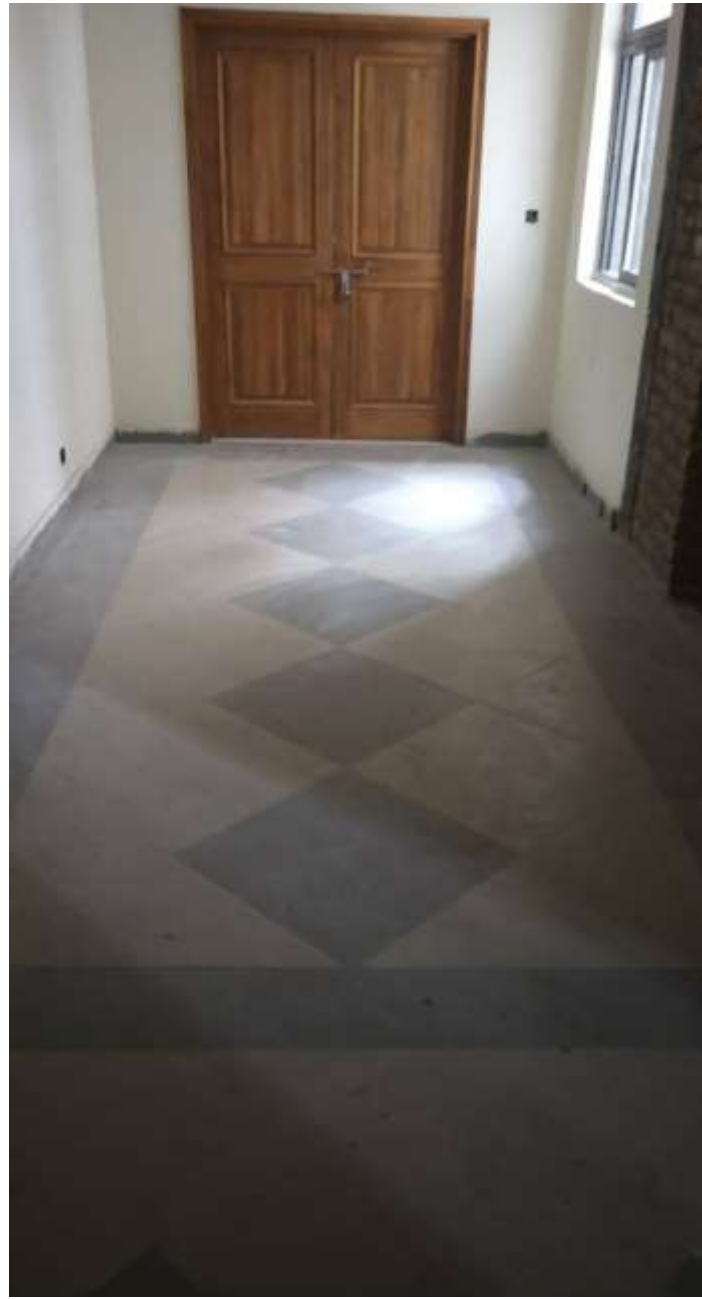

Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

ALUMINIUM DOOR WINDOW FIXING WORK IN PROGRESS.



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

ALUMINIUM DOOR WINDOWS FIXING WORK IN PROGRESS.



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

PACKAGE-V	STATUS AS ON 30/09/2019
Up to Last Month Block B01	<ul style="list-style-type: none"> • SS balcony Railing fixing in flats 5,6,7 & 8 completed from 2nd floor to 8th floor lvl. • IWC fixing work completed from 1st to 11th floor lvl. • Tiles flooring in Indian Toilet completed up to 11th floor lvl. • Aluminium Window frames fixing in wing-4 completed up to 11th floor lvl. • Internal Birla putty work 2nd coat completed up to 11th floor lvl. • Painting 1st coat completed in 1st floor lvl. • Internal door shutters fixing completed in 12th floor lvl. • Entry Door shutters fixing work completed up to 10th floor lvl. • Plumbing Shafts Louvers fixing work completed up to 8th floor lvl. • Internal wiring work completed up to 7th floor lvl. •
Current Month Activity	<ul style="list-style-type: none"> • Internal Painting on ceiling completed up to 9th floor lvl. • Internal wall Painting work completed up to 9th floor lvl. • Internal wiring work completed up to 10th floor lvl. • Balcony SS railing fixing work in wing-4 completed up to 12th floor lvl. • Plumbing Shafts Louvers fixing work completed from 9th floor to 12th floor lvl.
Up to Last Month Block B02	<ul style="list-style-type: none"> • IWC Orissa pan fixing completed from 10th to 13th floor lvl. • Indian toilet tiles flooring completed from 9th to 13th floor lvl. • SS Balcony Railing fixing completed in wings-1,2 & 3 up to 6th floor lvl. • Internal Birla putty work 2nd coat completed up to 11th floor lvl. • VDF flooring at stilt lvl wings -1 & 3 completed. • Plumbing Shafts Louvers fixing work completed up to 10th floor lvl. • Stilt floor Toilets wall & floor Tiling work 50% completed.
Current Month Activity	<ul style="list-style-type: none"> • Diverter fixing completed up to 13th floor lvl. • Internal door shutters fixing completed up to 7th floor lvl. • Internal Birla putty work 2nd coat completed from 12th floor to 13th floor lvl. • Plumbing Shafts Louvers fixing work completed from 11th floor to 13th floor lvl. • Balcony SS Railing top rail fixing work in wings-1 & 4 is in progress.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

<p>Up to Last Month</p> <p>Block B03</p>	<ul style="list-style-type: none"> • 75% 11th floor Roof slab casted. • 100% 10th floor columns casted. • 12th floor columns 25% casted. • Brick work in 9th floor lvl 95% completed. • Brick work in 10th floor lvl is in progress. • Door frames fixing work completed in 7th floor lvl. • Balance 40% Internal plaster at 3rd floor lvl completed. • Internal Plaster at 4th floor lvl 90% completed. • Internal Plaster at 5th floor lvl 25% completed. •
<p>Current Month</p> <p>Activity</p>	<ul style="list-style-type: none"> • Balance 25% 11th floor Roof slab casted.(Total 100%). • 100% 10th floor columns casted. • 12th floor columns 75% casted.(Total 100%). • 12th floor Roof slab 50% casted. • Brick work in 10th floor lvl 95% completed. • Brick work in 11th floor lvl is in progress. • Door frames fixing work completed in 8th floor lvl. • Balance 70% Internal plaster at 5th floor lvl completed.(Total 95%).
<p>Up to Last Month</p> <p>Block C15</p>	<ul style="list-style-type: none"> • Vdf flooring in stilt floor lvl 90% completed. • Stilt floor Toilets wall and floor tiling work 80% completed. • IWC fixing work completed from 1st to 11th floor lvl. • Tiles flooring in Indian Toilet completed up to 11th floor lvl. • Tiles flooring in corridor area completed in 11th floor lvl. • Machine Room Kota stone flooring work 75% completed. • Staircase stone skirting fixing work completed. • Aluminium Door window frames fixing work completed up to 3rd floor lvl. • SS balcony Railing fixing work is in progress at 6th floor lvl.(Total35% completed).
<p>Current Month</p> <p>Activity</p>	<ul style="list-style-type: none"> • Machine Room Kota stone flooring work 80% completed. • Aluminium Door window frames fixing work completed from 4th floor to 11th floor lvl. • Aluminium Door window glass fixing work 60% completed. • Balcony SS Railing Top Rail fixing work completed from 6th floor to 10th floor lvl.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

Up to Last Month Block C16	<ul style="list-style-type: none"> • IWC fixing work completed from 1st to 11th floor lvl.(Total 100%). • Tiles flooring in Indian Toilet completed up to 11th floor lvl. (Total 100%). • Stilt floor Toilets wall & floor tiling work 40% completed. • Aluminum Door windows glass fixing completed from 1st floor to 9th floor lvl.(Total 90% completed). • Entry Teak door shutters fixing work completed up to 3rd floor lvl. • Internal Birla putty 2nd coat 85% completed. • Plumbing shaft Louvers fixing work 90% completed. • Balcony SS Railing fixing work 90% completed. •
Current Month Activity	<ul style="list-style-type: none"> • Stilt floor Toilets wall & floor tiling work 55% completed.(Total 95%). • Aluminum Door windows glass fixing completed from 1st floor to 9th floor lvl.(Total 98% completed). • Entry Teak door shutters fixing work completed from 4th to 9th floor lvl. • Internal Birla putty 2nd coat 10% completed.(Total 95%). • Plumbing shaft Louvers fixing work 5% completed.(Total 95%). • Balcony SS Railing fixing work 5% completed.(Total 95%). • Internal wiring work completed up to 6th floor lvl. • Internal Electrical fittings Switch sockets fixing work completed up to 5th floor lvl.
Up to Last Month Non-Tower	<ul style="list-style-type: none"> • VDF flooring 5% completed. (Total 95%). • Ramps-1 & 2 Vdf flooring work completed. • Fire fighting sprinkler Piping fittings fixing work is in progress. • Vdf flooring groove cutting work is in progress.
Current Month Activity	<ul style="list-style-type: none"> • VDF flooring 3% completed. (Total 98%). • Ramps-1 & 2 Vdf flooring work completed. • Fire fighting sprinkler Piping fittings fixing work is in progress. • Basement Water supply piping work is in progress. • Vdf flooring groove cutting work completed. • Vdf flooring Groove filling work 60% completed.



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

PHOTOGRAPHS OF PACKAGE-V on 30th SEPT-2019

View of Blocks B-01,B-02 ,C-15 & C-16



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

In Block B-03 12th floor Roof slab 75% casted.



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

**Basement Soil,waste & Rain water piping completed.
Firefighting piping work is in progress.**



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

In Block C-16 Balcony SS Railing fixing work 95% completed.



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

In Block C-16 Aluminium Door windows frames with glass fixing 95% completed.



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

PACKAGE-VI	STATUS AS ON 30/09/2019
Up to Last Month Boundary Wall	<ul style="list-style-type: none">• Excavation for Boundary wall foundation of length 140 mtrs completed.Total (140/440 Mtrs).• PCC for Boundary wall foundation of length 140 mtrs completed. Total (140/440).• Excavation of Shopping Building is in Progress.• Boundary wall Raft Reinforcement work is in progress.• Layout Marking of Boundary wall is in progress.
Current Month Activity	<ul style="list-style-type: none">• Excavation for Boundary wall foundation of length 240 mtrs completed.Total (380/454 Mtrs).• PCC for Boundary wall foundation of length 204 mtrs completed. Total (344/454).• Excavation of Shopping Building & Nursing home completed.• PCC of Nursing & Shopping building completed.• Non Tower Excavation 1700 Sqm completed.• PCC of Non Tower area 1650 Sqm completed.



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

PHOTOGRAPHS OF PACKAGE-VI on 30th SEPT-2019

Boundary wall Columns casting above plinth is in progress.



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

PCC work of Shopping and Nursing is completed.



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

QUALITY CONTROL

**DURING CONSTRUCTION FOLLOWING QUALITY CONTROL TESTS
CONDUCTED AT SITE:**

S. No.	Materials	Source From	Test Date	Tests done	Result
1	Coarse Sand	Bajpur		Each truck	Sieve Analysis & Silt content
2	Coarse Aggregate	Nangal		Each truck	Sieve Analysis & Impact Value
3	Fine Sand	Yamuna Nagar		Each truck	Sieve Analysis & Silt content
4	Bricks	Greater Noida		Each truck	Dimension, Water Absorption & Compressive strength
5	Cement	Third party testing is being done			
6	Steel	Third party testing is being done			
7	Piles Integrity	Third party testing is being done			
8	Soil Compaction	Third party testing is being done			
9	STP water	Third party testing is being done			
10	RCC Cubes are being tested and Register is being maintained.				
11	Slump test conducted at site to insure workability if concrete.				



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

CUBE COMPRESSIVE STRENGTH TESTING.



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



COARSE SAND SIEVE ANALYSIS TESTING.



BRICK COMPRESSIVE STRENGTH TESTING



20MM IMPACT VALUE TESTING



MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT

ALUMINIUM DOOR AND WINDOW
MANUFACTURING AT SITE PROVIDE BY
SCHUCO.



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT



Progress Report No. 41 (1st SEPT-19–30th SEPT-19)

