

**CGEWHO – CHENNAI PHASE-III  
PROJECT**



**MONTHLY PROGRESS REPORT**

**STATUS AS ON : 31.08.2024**

**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

31.08.2024

BLOCK	STATUS AS ON 31 <sup>st</sup> AUGUST-2024
A1 BLOCK	<p>◆ <b>100% Completed Works</b></p> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (4 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank               <ul style="list-style-type: none"> <li>(a) Base Slab Concrete 2 out of 2</li> <li>(b) Tank Wall Concrete 2 out of 2</li> <li>(c) Top Cover slab Concrete 2 out of 2</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor</li> <li>▪ Electrical Conducting works in Tenth floor.</li> <li>▪ Fixing of Water supply pipe Lines (CPVC).</li> <li>▪ Fixing of Sanitary Lines (PVC).</li> <li>▪ Fixing of Vertical Plumbing Lines in Shaft.</li> <li>▪ Water Proofing Works               <ul style="list-style-type: none"> <li>a) Over Head Water Tanks ( 2 / 2 )</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles 100% completed (200/200)</li> <li>▪ Fixing of Toilet Wall Tiles 100% completed (200/200)</li> <li>▪ Laying Of Floor Tiles               <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathrooms 100% completed (200/200)</li> <li>b) Ceramic Tiles in Toilets 100% completed (200/200)</li> </ul> </li> <li>▪ Vitrified Tiles in Halls &amp; Bedrooms 100% completed (200/200).</li> <li>▪ Water Proofing Works.               <ul style="list-style-type: none"> <li>a) Over Head Water Tank 100% completed ( 2 / 2).</li> <li>b) Terrace Water Proofing Work 100% completed.</li> </ul> </li> <li>▪ Kitchen Finishing Works               <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados 100% completed (200/200).</li> <li>b) Laying of Granite Countertop 100% completed (200/200).</li> <li>c) Fixing of S.S Sink 100% completed (200/200)</li> </ul> </li> <li>▪ Electrical wire pulling work 100% completed (200/200).</li> <li>▪ Fixing of Modular Switches &amp; Sockets 100% completed. (200/200)</li> <li>▪ Fixing of Door Shutters 100% completed (1200/1200).</li> <li>▪ Fixing of IWC 100% completed (200/200)</li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

	<ul style="list-style-type: none"> <li>▪ Fixing of UPVC Windows 100% completed ( 800 /800 ).</li> <li>▪ Laying of Green marble for Staircase 100% completed.</li> <li>▪ Internal Painting               <ul style="list-style-type: none"> <li>a) 1<sup>st</sup> Coat – 100% completed (200/200)</li> </ul> </li> </ul>	
	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> AUGUST-2024</b>
	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ External Plastering 100% completed in all sides.</li> <li>▪ Fixing of Staircase Handrail 95% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Lift Materials 4 out of 4 received.               <ul style="list-style-type: none"> <li>a)Lift 1 – 50% completed.</li> <li>b)Lift 2 – Bulkhead fittings started.</li> </ul> </li> <li>▪ Fire fighting works 40% completed.</li> </ul> </li> <li>➤ <b>Model Flat</b> Finishing works 90% completed.</li> </ul>	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ External Plastering 100% completed in all sides.</li> <li>▪ Fixing of Staircase Handrail 95% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Lift Materials 4 out of 4 received.               <ul style="list-style-type: none"> <li>a) Lift 1 - 70% completed.</li> <li>b) Lift 2 - 70% completed.</li> <li>c) Lift 3 - Frame fixing started.</li> <li>d) Lift 4 - Bulkhead fitting completed.</li> </ul> </li> <li>▪ Fire fighting works 45% completed.</li> <li>▪ Fixing of Window Safety Grills 46% completed. (370 / 800).</li> </ul> </li> <li>➤ <b>Model Flat</b> Finishing works 95% completed.</li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

BLOCK	STATUS AS ON 31 <sup>st</sup> AUGUST-2024
A2 BLOCK	<p>◆ <b>100% Completed Works</b></p> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (4 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank <ul style="list-style-type: none"> <li>● Base Slab Concrete 2 out of 2</li> <li>● Tank Wall Concrete 2 out of 2</li> <li>● Top Cover slab Concrete 2 out of 2</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Electrical Conducting works upto Tenth floor.</li> <li>▪ Fixing of Water supply pipe Lines (CPVC).</li> <li>▪ Fixing of Sanitary Lines (PVC).</li> <li>▪ Fixing of Vertical Plumbing Lines in Shaft.</li> <li>▪ Water Proofing Work <ol style="list-style-type: none"> <li>a) Over Head Water Tank 100% completed (2 / 2 )</li> <li>b) Terrace Water proofing 100% completed.</li> </ol> </li> <li>▪ Fixing of Door Shutters 100% completed (1200/1200).</li> <li>▪ Kitchen Finishing Works <ol style="list-style-type: none"> <li>a) Fixing of Wall Dados 100% completed (200/200).</li> <li>b) Laying of Granite Countertop 100% completed (200/200).</li> <li>c) Fixing of S.S Sink 100% completed (200/200)</li> </ol> </li> <li>▪ Electrical wire pulling work 100% completed (200/200).</li> <li>▪ Fixing of Bathroom Wall Tiles 100% completed (200/200).</li> <li>▪ Fixing of Toilet Wall Tiles 100% completed (200/200).</li> <li>▪ Laying Of Floor Tiles <ol style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom 100% completed (200/200)</li> <li>b) Ceramic Tiles in Toilet 100% completed (200/200).</li> </ol> </li> <li>▪ Vitrified Tiles in Halls &amp; Bedrooms 100% completed. (200/200).</li> <li>▪ Fixing of IWC 100% completed (200/200).</li> <li>▪ Laying of Green marble for Staircase 100% completed.</li> <li>▪ Fixing of Modular Switches &amp; Sockets 100% completed (200/200).</li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31 <sup>st</sup> AUGUST-2024
	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ External plastering in all sides 95% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Lift Materials 4 out of 4 received                             <ul style="list-style-type: none"> <li>a) Lift 1 – 50% completed.</li> <li>b) Lift 2 – Bulkhead fittings started.</li> </ul> </li> <li>▪ Fire fighting works 40% completed.</li> <li>Fixing of Modular Switches &amp; Sockets 100% completed (200/200).</li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ External plastering in all sides 100% completed.</li> <li>▪ Fixing of UPVC Windows 100% completed ( 786 /800 )</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Lift Materials 4 out of 4 received                             <ul style="list-style-type: none"> <li>a) Lift 1 – 70% completed.</li> <li>b) Lift 2 – 60% completed.</li> <li>c) Lift 3 – 50% completed.</li> <li>d) Lift 4 - Bulkhead fittings completed</li> </ul> </li> <li>▪ Fire fighting works 45% completed.</li> <li>▪ Internal Painting                             <ul style="list-style-type: none"> <li>1<sup>st</sup> Coat – 30% completed (60/200)</li> </ul> </li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

BLOCK	STATUS AS ON 31 <sup>st</sup> AUGUST-2024
B1 BLOCK	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (3 out of 3) - Slab Concrete.</li> <li>▪ Over Head Water Tank                             <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (3 out of 3)</li> <li>(b) Wall Concrete (3 out of 3)</li> <li>(c) Top Cover slab (3 out of 3 )</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails</li> <li>▪ Fixing of Internal Plumbing Line                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ Fixing of Vertical Plumbing Line in Shafts                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles.</li> <li>▪ Laying Of Floor Tiles                             <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom</li> <li>b) Vitrified Tiles in Halls &amp; Bedrooms.</li> <li>c) Vitrified Tiles in Corridor.</li> </ul> </li> <li>▪ Fixing of UPVC Windows.</li> <li>▪ Fixing of UPVC French Door (without Mosquito mesh shutter)</li> <li>▪ Kitchen Finishing Works                             <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados.</li> <li>b) Laying of Granite Countertop.</li> <li>c) Fixing of S.S Sink.</li> </ul> </li> <li>▪ External Plastering in all sides.</li> <li>▪ Water Proofing Works.                             <ul style="list-style-type: none"> <li>a) Terrace floor Water proofing.</li> <li>b) Over Head Water Tank.</li> </ul> </li> <li>▪ Fixing of Door Shutters 100% completed (840/840).</li> <li>▪ Electrical wire pulling work 100% completed (120/120).</li> <li>▪ Fixing of Modular Switches &amp; Sockets 100% completed. (120/120)</li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

B1 BLOCK	<ul style="list-style-type: none"> <li>▪ Laying of Green marble for Staircase 100% completed.</li> <li>▪ Fixing of M.S Window Safety Grills 100% completed.</li> <li>▪ Fixing of IWC 100% completed (120/120)</li> <li>▪ Lift Cladding works 3 out of 3 100% completed.</li> <li>▪ Internal Painting               <ul style="list-style-type: none"> <li>a) 1<sup>st</sup> Coat – 100% completed (120/120)</li> </ul> </li> </ul>	
	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> AUGUST-2024</b>
	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Lift Installation works 3 out 3.</li> <li>▪ Application of Exterior Wall Primer</li> <li>▪ Firefighting works 95% completed.</li> <li>▪ Terrace Water supply Ring main works 95% completed.</li> <li>▪ Construction of Earth Pit chambers 95% completed.</li> <li>▪ Electrical Panel room- Trench works &amp; cable tray fixing works 90% completed.</li> </ul> </li> <li>▪ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ External Painting- Damp proof elasto               <ul style="list-style-type: none"> <li>a) South side - 90% completed.</li> <li>b) West side - 90% completed.</li> </ul> </li> <li>▪ Bathroom false ceiling work 99% completed ( 238 / 240 )</li> </ul> </li> <li>● <b>Model Flat</b> Finishing works 95% completed.</li> </ul>	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Lift Installation works 3 out 3.</li> <li>▪ Application of Exterior Wall Primer</li> <li>▪ Firefighting works 95% completed.</li> <li>▪ Terrace Water supply Ring main works 95% completed.</li> <li>▪ Construction of Earth Pit chambers 95% completed.</li> <li>▪ Electrical Panel room- Trench works &amp; cable tray fixing works 95% completed.</li> </ul> </li> <li>▪ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ External Painting- Damp proof elasto               <ul style="list-style-type: none"> <li>a) South side - 90% completed.</li> <li>b) West side - 90% completed.</li> </ul> </li> <li>▪ Bathroom false ceiling work 100% completed ( 240 / 240 ).</li> </ul> </li> <li>● <b>Model Flat</b> Finishing works 95% completed.</li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

BLOCK	STATUS AS ON 31 <sup>st</sup> AUGUST-2024	
B2 BLOCK	<p>◆ <b>100% Completed Works</b></p> <ul style="list-style-type: none"> <li>▪ Upto Terrace floor level slab R.C.C</li> <li>▪ Parapet Columns Concrete 100% completed</li> <li>▪ Block work upto Tenth floor.</li> <li>▪ Ceiling plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Ninth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Ninth floor completed.</li> </ul>	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31 <sup>st</sup> AUGUST-2024
	<p>◆ <b>Works On Progress</b></p> <ul style="list-style-type: none"> <li>▪ Wall Plastering <ul style="list-style-type: none"> <li>a) In Tenth floor 90% completed</li> </ul> </li> <li>▪ Electrical conducting works 93% completed. ( 112/120)</li> <li>▪ 1<sup>st</sup> Coat Wall Putty in Ninth floor 75% completed.</li> <li>▪ Fixing of Internal Water supply pipeline (CPVC) 93% completed ( 112 / 120)</li> <li>▪ Fixing of Internal Sanitary lines (PVC) 70% completed.( 84 / 120).</li> <li>▪ Fixing of Plumbing lines in Vertical Shafts 20% completed. ( 5 /24 )</li> <li>▪ External Plastering 65% completed.</li> <li>▪ Fixing of Bathroom Wall Tiles 8% completed ( 20 / 240).</li> <li>▪ Laying Of Floor Tiles <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom 8% completed ( 20 / 240).</li> </ul> </li> </ul>	<p>◆ <b>Works On Progress</b></p> <ul style="list-style-type: none"> <li>▪ Wall Plastering <ul style="list-style-type: none"> <li>a) In Tenth floor 100% completed</li> </ul> </li> <li>▪ Electrical conducting works 100% completed. ( 120/120)</li> <li>▪ 1<sup>st</sup> Coat Wall Putty in Tenth floor 15% completed.</li> <li>▪ Fixing of Internal Water supply pipeline (CPVC) 100% completed ( 120 / 120)</li> <li>▪ Fixing of Internal Sanitary lines (PVC) 83% completed.( 100 / 120).</li> <li>▪ Fixing of Plumbing lines in Vertical Shafts 54% completed. ( 13 /24 )</li> <li>▪ External Plastering 80% completed.</li> <li>▪ Fixing of Bathroom Wall Tiles 38% completed ( 90 / 240).</li> <li>▪ Laying Of Floor Tiles <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom 38% completed ( 90 / 240).</li> <li>b) Vitrified Tiles in Halls &amp; Bedrooms 15% completed (18/120)</li> </ul> </li> <li>▪ Fixing of UPVC Windows started (5/120).</li> <li>▪ Fixing of UPVC French Doors started (5/120).</li> </ul>





**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

BLOCK	STATUS AS ON 31 <sup>st</sup> AUGUST-2024
C1 BLOCK	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (4 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank                             <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (3 out of 3)</li> <li>(b) Wall Concrete (3 out of 3)</li> <li>(c) Top Cover slab (3 out of 3 )</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Internal Plumbing Line.                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ Fixing of Vertical Plumbing Line in Shafts                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles.</li> <li>▪ Laying Of Floor Tiles                             <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom</li> <li>b) Vitrified Tiles in Halls &amp; Bedrooms</li> <li>c) Vitrified Tiles in Corridor completed.</li> </ul> </li> <li>▪ Fixing of UPVC Windows.</li> <li>▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed.</li> <li>▪ External Plastering in all sides.</li> <li>▪ Water Proofing Works.                             <ul style="list-style-type: none"> <li>a) Over Head Water Tank</li> <li>b) Terrace floor Water proofing.</li> </ul> </li> <li>▪ Laying of Green marble for Staircase 100% completed.</li> <li>▪ Kitchen Finishing Works                             <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados.</li> <li>b) Laying of Granite Countertop.</li> <li>c) Fixing of S.S Sink.</li> </ul> </li> <li>▪ Lift Cladding works 4 out of 4.</li> <li>▪ Fixing of Door Shutters 100% completed (1080 / 1080)</li> </ul> </li> </ul>

**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

C1 BLOCK	<ul style="list-style-type: none"> <li>▪ Electrical wire pulling work 100% completed (120/120).</li> <li>▪ Fixing of Modular Switches &amp; Sockets 100% completed. (120/120)</li> <li>▪ Terrace Water supply Ring main works 100% completed.</li> <li>▪ Application of Exterior Wall Primer 100% completed.</li> <li>▪ Fixing of M.S Window Safety Grills 100% completed ( 480 / 480 )</li> <li>▪ Fixing of IWC 100% completed (120 / 120).</li> <li>▪ Bathroom false ceiling work 100% completed ( 360 / 360 ).</li> <li>▪ Internal Painting               <ul style="list-style-type: none"> <li>a) 1<sup>st</sup> Coat – 100% completed (120/120)</li> </ul> </li> </ul>	
	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> AUGUST-2024</b>
	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Fixing of Staircase Hand Rails (3 out of 3) 95% completed.</li> <li>▪ Lift Installation works 4 out 4.</li> <li>▪ Laying of External Sewerage lines 95% completed.</li> <li>▪ Laying of External water supply lines 95% completed.</li> <li>▪ Construction of Earth Pit chambers 95% completed.</li> <li>▪ Fire Fighting works 95% completed.</li> <li>▪ Electrical Panel room- Trench works &amp; cable tray fixing works 90% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ External Painting- Damp proof elasto 85% completed.</li> </ul> </li> <li>● <b>Model Flat</b> Finishing works 95% completed.</li> </ul>	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Fixing of Staircase Hand Rails (3 out of 3) 95% completed.</li> <li>▪ Lift Installation works 4 out 4.</li> <li>▪ Laying of External Sewerage lines 95% completed.</li> <li>▪ Laying of External water supply lines 95% completed.</li> <li>▪ Construction of Earth Pit chambers 95% completed.</li> <li>▪ Fire Fighting works 95% completed.</li> <li>▪ Electrical Panel room- Trench works &amp; cable tray fixing works 95% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ External Painting- Damp proof elasto 100% completed.</li> <li>▪ Fixing of EWC 60% completed (144 / 240).</li> </ul> </li> <li>● <b>Model Flat</b> Finishing works 95% completed.</li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

BLOCK	STATUS AS ON 31 <sup>st</sup> AUGUST-2024
C2 BLOCK	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (3 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank               <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (2 out of 3)</li> <li>(b) Wall Concrete (2 out of 3)</li> <li>(c) Top Cover slab (2 out of 3 )</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Fixing of Internal Plumbing Line               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ Fixing of Vertical Plumbing Line in Shafts               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> <li>▪ External Plastering in all sides.</li> <li>▪ Water Proofing Works.               <ul style="list-style-type: none"> <li>a) Over Head Water Tank 3 out of 3</li> <li>b) Terrace floor Water proofing 100% completed.</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles completed.</li> <li>▪ Laying Of Floor Tiles               <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom completed.</li> <li>b) Vitrified Tiles in Halls &amp; Bedrooms completed.</li> <li>c) Vitrified Tiles in Corridor completed.</li> </ul> </li> <li>▪ Kitchen Finishing Works               <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados 100% completed. ( 120 / 120 )</li> <li>b) Laying of Granite Countertop 100% completed. ( 120 / 120).</li> <li>c) Fixing of S.S Sink 100% completed. ( 120 / 120).</li> </ul> </li> <li>▪ Fixing of UPVC Window 100% completed. ( 600 / 600 )</li> <li>▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed. (240 /240)</li> <li>▪ Fixing of Main Door &amp; Internal Shutters 100% completed (1080 / 1080)</li> <li>▪ Laying of Green marble for Staircase 100% completed..</li> <li>▪ Electrical wire pulling 100% completed ( 120 /120).</li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

C2 BLOCK	<ul style="list-style-type: none"> <li>▪ Fixing of Modular Switches &amp; Sockets 100% completed. (120/120).</li> <li>▪ Lift Cladding work 100% completed.</li> <li>▪ Application of Exterior Wall Primer 100% completed.</li> <li>▪ Fixing of M.S Window Safety Grills 100% completed ( 480 / 480 )</li> <li>▪ Bathroom false ceiling work 100% completed ( 360 / 360 )</li> <li>▪ Fixing of IWC 100% completed (120 / 120)</li> <li>▪ Internal Painting               <ul style="list-style-type: none"> <li>a) 1<sup>st</sup> Coat – 100% completed (120/120)</li> </ul> </li> </ul>	
	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> AUGUST-2024</b>
	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails</li> <li>▪ Lift Installation works 4 out 4                   <ul style="list-style-type: none"> <li>a) Lift 1 &amp; 2 - 90% completed.</li> <li>b) Lift 3 &amp; 4 - 85% completed.</li> </ul> </li> <li>▪ Terrace Water supply Ring main works 95% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Fire fighting works 65% completed.</li> <li>▪ Laying of External Sewerage lines 90% completed.</li> <li>▪ Laying of External water supply lines 85% completed.</li> <li>▪ External Painting- Damp proof elasto 85% completed.</li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails</li> <li>▪ Lift Installation works 4 out 4                   <ul style="list-style-type: none"> <li>a) Lift 1, 2 &amp; 3 - 90% completed.</li> <li>b) Lift 4 - 85% completed.</li> </ul> </li> <li>▪ Terrace Water supply Ring main works 95% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Fire fighting works 90% completed.</li> <li>▪ Laying of External Sewerage lines 95% completed.</li> <li>▪ Laying of External water supply lines 90% completed.</li> <li>▪ External Painting- Damp proof elasto 95% completed.</li> <li>▪ Construction of Earth Pit chambers 95% completed.</li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

BLOCK	STATUS AS ON 31 <sup>st</sup> AUGUST-2024
C3 BLOCK	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (4 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank               <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (2 out of 3)</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Fixing of Internal Plumbing Line               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ Fixing of Vertical Plumbing Line in Shafts               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> <li>▪ External Plastering in all sides.</li> <li>▪ Water Proofing Works.               <ul style="list-style-type: none"> <li>a) Over Head Water Tank ( 2 / 2) completed.</li> <li>b) Terrace floor Water proofing 100% completed.</li> </ul> </li> <li>▪ Kitchen Finishing Works               <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados 100% completed (100/100)</li> <li>b) Laying of Granite Countertop 100% completed. (100/100).</li> <li>c) Fixing of S.S Sink 100% completed. (100/ 100).</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles 100% completed. ( 300 /300 )</li> <li>▪ Laying Of Floor Tiles               <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom 100% completed. ( 300 /300 )</li> <li>b) Vitrified Tiles in Halls &amp; Bedrooms 100% completed. ( 100 / 100 )</li> </ul> </li> <li>▪ Laying of Green marble for Staircase 100% completed.</li> <li>▪ Electrical wire pulling 100% completed ( 100 /100).</li> <li>▪ Fixing of UPVC Window 100% Completed. ( 500 / 500 ).</li> <li>▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed ( 200 / 200 ).</li> <li>▪ Fixing of Main Door &amp; Internal Shutters 100% completed (900 / 900).</li> <li>▪ Electrical Wire pulling 100% completed ( 100 /100).</li> <li>▪ Fixing of Modular Switches &amp; Sockets 100% completed. (100/100).</li> <li>▪ Application of Exterior Wall Primer 100% completed.</li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

C3 BLOCK	<ul style="list-style-type: none"> <li>▪ Fixing of M.S Window Safety Grills 100% completed ( 400 / 400 )</li> <li>▪ Fixing of IWC 100% completed (100 / 100)</li> <li>▪ Internal Painting               <ul style="list-style-type: none"> <li>a) 1<sup>st</sup> Coat – 100% completed (120/120)</li> </ul> </li> </ul>	
	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> AUGUST-2024</b>
	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails.</li> <li>▪ Lift Cladding work 4 out of 4 95% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Lift Installation works 4 out 4               <ul style="list-style-type: none"> <li>a) All 4 Lifts -85% completed.</li> </ul> </li> <li>▪ Fire fighting works 60% completed.</li> <li>▪ Laying of External Sewerage lines 70% completed.</li> <li>▪ Laying of External water supply lines 35% completed.</li> <li>▪ External Painting- Damp proof elasto 40% completed.</li> <li>▪ Bathroom false ceiling work 10% completed ( 30 / 300 )</li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails.</li> <li>▪ Lift Cladding work 4 out of 4 95% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Lift Installation works 4 out 4               <ul style="list-style-type: none"> <li>a) Lift1 &amp; 2 -90% completed.</li> <li>b) Lift 3 &amp; 4 – 90% completed.</li> </ul> </li> <li>▪ Fire fighting works 90% completed.</li> <li>▪ Laying of External Sewerage lines 85% completed.</li> <li>▪ Laying of External water supply lines 75% completed.</li> <li>▪ External Painting- Damp proof elasto 90% completed.</li> <li>▪ Bathroom false ceiling work 93% completed ( 279 / 300 )</li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

BLOCK	STATUS AS ON 31 <sup>st</sup> AUGUST-2024
D1 BLOCK	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (4 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank                             <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (3 out of 3)</li> <li>(b) Wall Concrete (3 out of 3)</li> <li>(c) Top Cover slab (3 out of 3)</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Water Proofing Works.                             <ul style="list-style-type: none"> <li>a) Over Head Water Tank 3 out of 3</li> <li>b) Terrace floor Water proofing 100% completed.</li> </ul> </li> <li>▪ Fixing of Internal Plumbing Line                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ Fixing of Vertical Plumbing Line in Shafts                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles 100% completed. ( 320 / 320 ).</li> <li>▪ Laying Of Floor Tiles                             <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom 100% completed. ( 320 / 320 )</li> <li>b) Vitrified Tiles in Halls &amp; Bedrooms 100% completed. ( 80 / 80).</li> </ul> </li> <li>▪ Kitchen Finishing Works                             <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados 100% completed. ( 80 / 80 )</li> <li>b) Laying of Granite Countertop 100% completed. ( 80 / 80).</li> <li>c) Fixing of S.S Sink 100% completed. ( 80 / 80).</li> </ul> </li> <li>▪ Fixing of Main Door &amp; Internal Shutters 100% completed ( 880 / 880 )</li> <li>▪ Electrical Wire pulling works 100% completed. (80/ 80).</li> <li>▪ Fixing of Modular Switches &amp; Sockets 100% completed. (80/80)</li> <li>▪ Fixing of UPVC Windows 100% completed. (400 / 400).</li> <li>▪ Fixing of UPVC French Door 100% competed.(without Mosquito mesh shutter) ( 160 / 160 )</li> <li>▪ Application of External Wall Primer- 100% completed.</li> <li>▪ Lift Cladding works 4 out of 4 - 100% completed.</li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

D1 BLOCK	<ul style="list-style-type: none"> <li>▪ Laying of Green marble for Staircase 100% completed.</li> <li>▪ Bathroom false ceiling work 100% completed ( 320 / 320 )</li> <li>▪ Fixing of IWC 100% completed (80 / 80)</li> <li>▪ External plastering in all sides 100% completed.</li> </ul>	
	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> AUGUST-2024</b>
	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ External Painting - Damp proof elasto 95% completed.</li> <li>▪ Fire fighting works 95% completed.</li> <li>▪ Laying of External Sewerage lines 95% completed</li> <li>▪ Laying of External Water supply lines 95% completed.</li> <li>▪ Laying of Storm Water drain pipes 95% completed.</li> <li>▪ Fixing of M.S Window Safety Grills 94% completed ( 302 / 320 )</li> <li>▪ Laying of Grano flooring in Stilt floor 95% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Lift Installation works                             <ol style="list-style-type: none"> <li>a) 3 Lifts - 90% completed.</li> <li>b) 4<sup>th</sup> Lift – 70% completed.</li> </ol> </li> <li>▪ Construction of Earth Pit chambers 85% completed.</li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ External Painting - Damp proof elasto 95% completed.</li> <li>▪ Fire fighting works 95% completed.</li> <li>▪ Laying of External Sewerage lines 95% completed</li> <li>▪ Laying of External Water supply lines 95% completed.</li> <li>▪ Laying of Storm Water drain pipes 95% completed.</li> <li>▪ Fixing of M.S Window Safety Grills 94% completed ( 302 / 320 )</li> <li>▪ Laying of Grano flooring in Stilt floor 95% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Lift Installation works                             <ol style="list-style-type: none"> <li>a) 3 Lifts - 90% completed.</li> <li>b) 4<sup>th</sup> Lift – 70% completed.</li> </ol> </li> <li>▪ Construction of Earth Pit chambers 90% completed.</li> </ul> </li> </ul>





**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

BLOCK	STATUS AS ON 31 <sup>st</sup> AUGUST-2024
D2 BLOCK	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (3 out of 3) - Slab Concrete.</li> <li>▪ Over Head Water Tank               <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (3 out of 3)</li> <li>(b) Wall Concrete (3 out of 3)</li> <li>(c) Top Cover slab (3 out of 3 )</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails</li> <li>▪ Fixing of Internal Plumbing Line               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ Fixing of Vertical Plumbing Line in Shafts               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles.</li> <li>▪ Laying Of Floor Tiles               <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom</li> <li>b) Vitrified Tiles in Halls &amp; Bedrooms.</li> <li>c) Vitrified Tiles in Corridor.</li> </ul> </li> <li>▪ Fixing of UPVC Windows.</li> <li>▪ Fixing of Main Door &amp; Internal Shutters.</li> <li>▪ Kitchen Finishing Works               <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados.</li> <li>b) Laying of Granite Countertop.</li> <li>c) Fixing of S.S Sink.</li> </ul> </li> <li>▪ External Plastering in all sides.</li> <li>▪ Water Proofing Works.               <ul style="list-style-type: none"> <li>a) Terrace floor Water proofing.</li> <li>b) Over Head Water Tank</li> </ul> </li> <li>▪ Laying of Green marble for Staircase.</li> <li>▪ Fixing of UPVC French Door (without Mosquito mesh shutter).</li> <li>▪ Electrical Wire pulling works 100% completed (80/ 80).</li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

D2 BLOCK	<ul style="list-style-type: none"> <li>▪ Fixing of Modular Switches &amp; Sockets 100% completed. (80/80).</li> <li>▪ Fire Fighting Works 100% completed.</li> <li>▪ Fixing of M.S Window Safety Grills 100% completed. (320 / 320).</li> <li>▪ Lift Cladding works 4 out of 4 – 100% completed.</li> <li>▪ Application of Exterior Wall Primer-100% completed.</li> <li>▪ Fixing of IWC 100% completed (80 / 80)</li> <li>▪ Bathroom false ceiling work 100% completed ( 320 / 320 )</li> </ul>	
	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> AUGUST-2024</b>
	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Lift Installation works 4 out 4.</li> <li>▪ Laying of External Sewerage lines 95% completed.</li> <li>▪ Laying of External Water supply lines 95% completed.</li> <li>▪ Laying of Storm Water drain pipes 95% completed.</li> <li>▪ Fire Fighting Works 95% completed.</li> <li>▪ Construction of Earth Pit chambers 95% completed.</li> <li>▪ External Painting - Damp proof elasto 95% completed.</li> <li>▪ Electrical Panel room- Trench works &amp; cable tray fixing works 95% completed.</li> <li>▪ Fixing of M.S Window Safety Grills 94% completed ( 303 / 320 )</li> <li>▪ Laying of Grano flooring in Stilt floor 95% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Lift Commissioning works for 4 Lifts</li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Lift Installation works 4 out 4.</li> <li>▪ Laying of External Sewerage lines 95% completed.</li> <li>▪ Laying of External Water supply lines 95% completed.</li> <li>▪ Laying of Storm Water drain pipes 95% completed.</li> <li>▪ Fire Fighting Works 95% completed.</li> <li>▪ Construction of Earth Pit chambers 95% completed.</li> <li>▪ External Painting - Damp proof elasto 95% completed.</li> <li>▪ Electrical Panel room- Trench works &amp; cable tray fixing works 95% completed.</li> <li>▪ Fixing of M.S Window Safety Grills 94% completed ( 303 / 320 )</li> <li>▪ Laying of Grano flooring in Stilt floor 95% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Lift Commissioning works for 4 Lifts</li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

BLOCK	STATUS AS ON 31 <sup>st</sup> AUGUST-2024
D3 BLOCK	<p>◆ <b>100% Completed Works</b></p> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (4 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank               <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (3 out of 3)</li> <li>(b) Wall Concrete (3 out of 3)</li> <li>(c) Top Cover slab (3 out of 3 )</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Tenth floor</li> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails</li> <li>▪ Fixing of Internal Plumbing Line               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ Fixing of Vertical Plumbing Line in Shafts               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> <li>▪ External Plastering in all sides.</li> <li>▪ Water Proofing Works.               <ul style="list-style-type: none"> <li>a) Over Head Water Tank 1 out of 3</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles 100% completed. ( 320 / 320 )</li> <li>▪ Kitchen Finishing Works               <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados 100% completed. ( 80 / 80 )</li> <li>b) Laying of Granite Countertop 100% completed. ( 80 / 80).</li> </ul> </li> <li>▪ Fixing of S.S Sink 100% completed. ( 80 / 80).</li> <li>▪ Laying Of Floor Tiles               <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom 100% completed. (320 / 320)</li> <li>b) Vitrified Tiles in Halls &amp; Bedrooms 100% completed. ( 80 / 80 )</li> <li>c) Vitrified Tiles in Corridor 100% completed.</li> </ul> </li> <li>▪ Fixing of Main Door &amp; Internal Shutters 100% completed (880 / 880)</li> <li>▪ Water Proofing Works.               <ul style="list-style-type: none"> <li>a) Terrace floor Water proofing 100% completed.</li> <li>b) Over Head Water Tank 3 out of 3 completed.</li> </ul> </li> <li>▪ Fixing of UPVC Windows 100% completed. ( 400 / 400 )</li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

	<ul style="list-style-type: none"> <li>▪ Electrical Wire pulling works 100% completed (80/ 80).</li> <li>▪ Fixing of Modular Switches &amp; Sockets 100% completed. (80/80).</li> <li>▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed ( 160 / 160).</li> <li>▪ Laying of Green marble for Staircase 100% completed.</li> <li>▪ Lift Cladding works 4 out of 4 - 100% completed.</li> <li>▪ Application of Exterior Wall Primer 100% completed.</li> <li>▪ Fixing of IWC 100% completed (80 / 80)</li> <li>▪ Bathroom false ceiling work 100% completed ( 320 / 320 )</li> </ul>	
D3 BLOCK	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> AUGUST-2024</b>
	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Laying of External Sewerage lines 95% completed.</li> <li>▪ Laying of External water supply lines 95% completed.</li> <li>▪ Laying of Storm Water drain pipes 95% completed.</li> <li>▪ Firefighting works 95% completed.</li> <li>▪ Fixing of M.S Window Safety Grills 90% completed (285/320).</li> <li>▪ External Painting - Damp proof elasto 95% completed.</li> <li>▪ Laying of Grano flooring in Stilt floor 100% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Lift Installation works - 4 out of 4 –               <ul style="list-style-type: none"> <li>a) 3 Lifts - 90% completed.</li> <li>b) 4<sup>th</sup> Lift - 75% completed.</li> </ul> </li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Laying of External Sewerage lines 95% completed.</li> <li>▪ Laying of External water supply lines 95% completed.</li> <li>▪ Laying of Storm Water drain pipes 95% completed.</li> <li>▪ Firefighting works 95% completed.</li> <li>▪ Fixing of M.S Window Safety Grills 90% completed (285/320).</li> <li>▪ External Painting - Damp proof elasto 95% completed.</li> <li>▪ Laying of Grano flooring in Stilt floor 100% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Lift Installation works - 4 out of 4 –               <ul style="list-style-type: none"> <li>a) 3 Lifts - 90% completed.</li> <li>b) 4<sup>th</sup> Lift - 80% completed.</li> </ul> </li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

BLOCK	STATUS AS ON 31 <sup>st</sup> AUGUST-2024	
COMMUNITY HALL	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (2 out of 2) - Slab Concrete.</li> <li>▪ Over Head Water Tank                             <ul style="list-style-type: none"> <li>(a) Base Slab Concrete</li> <li>(b) Tank Wall Concrete</li> <li>(c) Top Cover slab Concrete.</li> </ul> </li> <li>▪ Block work upto Fourth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Fourth floor.</li> <li>▪ Wall plastering upto Fourth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Fourth floor.</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Fourth floor.</li> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails</li> <li>▪ Fixing of Internal Plumbing Line                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ Fixing of Vertical Plumbing Line in Shafts                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles.</li> <li>▪ Laying Of Floor Tiles                             <ul style="list-style-type: none"> <li>a) Vitrified Floor Tiles in Hall &amp; rooms</li> <li>b) Ceramic Floor Tiles in Bathrooms.</li> <li>c) Kota Stone in Staircase &amp; Lobby</li> </ul> </li> <li>▪ Fixing of UPVC Windows.</li> <li>▪ Fixing of Wooden flush Door for rooms.</li> <li>▪ Fixing of Fire Safety Door for Hall Main Entrance</li> <li>▪ External Plastering in all sides.</li> <li>▪ Water Proofing Works.                             <ul style="list-style-type: none"> <li>a) Terrace floor Water proofing.</li> <li>b) Over Head Water Tank.</li> </ul> </li> </ul> </li> </ul>	
	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> AUGUST-2024</b>
	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Lift Installation works 4 out 4.</li> <li>▪ Lift Cladding works 4 out of 4</li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Lift Installation works 4 out 4 100% completed</li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

COMMUNITY HALL	<ul style="list-style-type: none"> <li>▪ Application of Exterior Wall Primer.- 95% completed</li> <li>▪ Fire fighting works – Installation of Pipelines 95% completed.</li> <li>▪ Electrical Wire &amp; cables pulling work 95% completed.</li> <li>▪ Fixing of Modular Switches &amp; Sockets 95% completed.</li> <li>▪ Excavation for laying of Firefighting Hydrant pipes 95% completed.</li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Fixing of Sanitary fixtures 40% completed.</li> <li>▪ Application of Exterior Wall Damp proof Paint 50% completed.</li> <li>▪ Lift commissioning works.</li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>▪ Lift Cladding works 4 out of 4 – 100% completed.</li> <li>▪ Application of Exterior Wall Primer.- 100% completed</li> <li>▪ Fire fighting works – Installation of Pipelines 95% completed.</li> <li>▪ Electrical Wire &amp; cables pulling work 95% completed.</li> <li>▪ Fixing of Modular Switches &amp; Sockets 95% completed.</li> <li>▪ Excavation for laying of Firefighting Hydrant pipes 95% completed.</li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Fixing of Sanitary fixtures 40% completed.</li> <li>▪ Application of Exterior Wall Damp proof Paint 50% completed.</li> <li>▪ Lift commissioning works.                             <ul style="list-style-type: none"> <li>a) Lift 1 – High Speed completed.</li> <li>b) Lift 2 – Slow Speed completed</li> </ul> </li> </ul> </li> </ul>
----------------	---	---

EXTERNAL DEVELOPMENT WORKS	<b>STATUS AS ON 31<sup>st</sup> AUGUST-2024</b>
	<ul style="list-style-type: none"> <li>➤ <b>Underground Sump-1 (Near B-Block)</b> <ul style="list-style-type: none"> <li>▪ Base Slab R.C.C 100% completed.</li> <li>▪ Sump Wall - R.C.C 100% completed.</li> <li>▪ Top slab R.C.C 100% completed.</li> <li>▪ Outer Wall Waterproof plastering – 100% completed.</li> <li>▪ Inner Wall Waterproof plastering – 100% completed.</li> <li>▪ Pump room Inner plastering – 100% completed.</li> </ul> </li> <li>➤ <b>Underground Sump-2 (Near D-Block)</b> <ul style="list-style-type: none"> <li>▪ Base Slab - R.C.C 100% completed.</li> <li>▪ Sump Wall - R.C.C 100% completed.</li> <li>▪ Top slab R.C.C 100% completed.</li> <li>▪ Outer Wall Waterproof plastering – 100% completed.</li> <li>▪ Inner Wall Waterproof plastering 100% completed.</li> <li>▪ Pump room Inner plastering 100% completed.</li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

---

	<ul style="list-style-type: none"><li>➤ <b>Sewage Treatment Plant-2 (Near D-Block)</b><ul style="list-style-type: none"><li>▪ Base slab – R.C.C 100% completed.</li><li>▪ STP Wall – R.C.C 100% completed.</li><li>▪ STP Top Slab – R.C.C 100% completed.</li><li>▪ STP Pump Room completed.</li><li>▪ Outer wall Waterproof plastering 100% completed.</li><li>▪ Inner Wall Waterproof plastering 100% completed.</li><li>▪ Installation of STP 85% completed.</li></ul></li><li>➤ <b>Sewage Treatment Plant-1 (Near C3-Block)</b><ul style="list-style-type: none"><li>▪ Base slab RCC completed.</li><li>▪ STP Wall Reinforcement 100% completed.</li><li>▪ STP Wall Concrete 90% completed.</li><li>▪ Top Slab reinforcement 45% completed.</li></ul></li><li>➤ <b>Laying of External Sewer lines</b><ul style="list-style-type: none"><li>▪ Type D All Blocks – 100% completed.</li><li>▪ C1 Block - 95% completed</li><li>▪ C2 Block - 90% completed.</li><li>▪ C3 Block - 70% completed.</li><li>▪ B1 Block - 35% completed.</li><li>▪ A1 Block - 85% completed.</li><li>▪ A2 Block - 85% completed.</li></ul></li><li>➤ <b>Laying of External Water Supply lines</b><ul style="list-style-type: none"><li>▪ Type D All Blocks – 95% completed.</li><li>▪ C1 Block – 95% completed</li><li>▪ C2 Block – 85% completed.</li><li>▪ C3 Block – 35% completed.</li><li>▪ B1 Block – 25% completed.</li><li>▪ A1 Block - 70% completed.</li><li>▪ A2 Block – 70% completed.</li></ul></li><li>➤ <b>Laying of Storm Water Drainage.</b><ul style="list-style-type: none"><li>▪ Type D All Blocks – 95% completed.</li><li>▪ C1 Block – 70% completed.</li><li>▪ C2 Block – 80% completed.</li><li>▪ C3 Block – 70% completed.</li><li>▪ A1 Block – 75% completed.</li><li>▪ A2 Block – 75% completed.</li></ul></li></ul>
--	--

# PROGRESS REPORT CGEWHO – CHENNAI PHASE-III PROJECT

---

## PHOTOGRAPHS OF WORK PROGRESS AS ON 31<sup>st</sup> AUGUST 2024

**Community Hall:** 2<sup>nd</sup> Lift Commissioning works on progress. Fire fighting pumps connection works on progress





# PROGRESS REPORT CGEWHO – CHENNAI PHASE-III PROJECT

---

**Block A1:** Lift Cladding works & Window grill fixing on progress.



# PROGRESS REPORT CGEWHO – CHENNAI PHASE-III PROJECT

---

**Block A2** : False ceiling works & Firefighting works on progress.



# PROGRESS REPORT


## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Block B1:** Clearing if Stilt floor for Grano flooring on progress.



**Block B2 :** Vitrified Tiling works & External Plumbing works in shafts on progress.

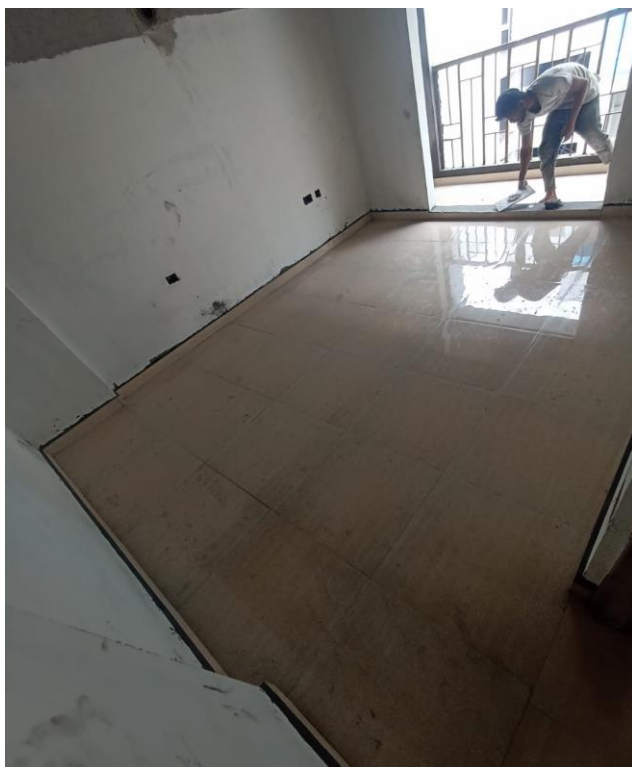

# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Block C1:** Fixing of Manholes Cover frames & Grano flooring in Stilt floor on progress.



# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

**Block C2:** Fixing of Manholes Cover frames & Grano flooring in Stilt floor on progress.



# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Block C3:** Cleaning work and shifting of store materials for grano flooring.



# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Block D1:** Removal of Debris at stilts and levelling work for Road on progress.



# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

**Block D2:** Preparation of Sub-Grade for Road on progress





# PROGRESS REPORT CGEWHO – CHENNAI PHASE-III PROJECT

---

**Block D3:** Removal & levelling of Earth for Road work on progress.



# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Sewage Treatment Plant 1 (Near C Block).** STP Top Slab Concrete 35% completed. Reinforcement works for balance Top slab on progress.



**External Electrification Works:** Fixing of Poles for Transformers & Transmission Lines on Progress



# PROGRESS REPORT CGEWHO – CHENNAI PHASE-III PROJECT

---



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

---

**QUALITY CONTROL**

**DURING CONSTRUCTION FOLLOWING QUALITY CONTROL TESTS CONDUCTED AT SITE:**

Sl.No.	Materials	Source from	Test Done	Result
1	M-Sand	Arcot (T.K), Ranipet (Dist) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2.	P- Sand	Uthiramerur, Kanchipuram (DT) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2	Coarse Aggregate (20mm)	Sriperambathur, Kanchipuram (Dt), Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
3	Coarse Aggregate (12mm)	Sriperambathur, Kanchipuram (Dt) Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
4	Cement	Third party testing is being done.		
5	Steel	Third party testing is being done.		
6	Pile Integrity	Third party testing is being done.		
7	Soil Compaction	Third party testing is being done.		
8	RCC cubes are being tested and Register is being maintained.			
9	Slump test conducted at site to insure workability of concrete.			
