

**CGEWHO – CHENNAI PHASE-III
PROJECT**



MONTHLY PROGRESS REPORT

STATUS AS ON : 30.09.2024

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

30.09.2024

BLOCK	STATUS AS ON 30 th SEPTEMBER-2024
A1 BLOCK	<p>◆ 100% Completed Works</p> <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete 2 out of 2 (b) Tank Wall Concrete 2 out of 2 (c) Top Cover slab Concrete 2 out of 2 ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor ▪ Electrical Conducting works in Tenth floor. ▪ Fixing of Water supply pipe Lines (CPVC). ▪ Fixing of Sanitary Lines (PVC). ▪ Fixing of Vertical Plumbing Lines in Shaft. ▪ Water Proofing Works <ul style="list-style-type: none"> a) Over Head Water Tanks (2 / 2) ▪ Fixing of Bathroom Wall Tiles 100% completed (200/200) ▪ Fixing of Toilet Wall Tiles 100% completed (200/200) ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathrooms 100% completed (200/200) b) Ceramic Tiles in Toilets 100% completed (200/200) ▪ Vitrified Tiles in Halls & Bedrooms 100% completed (200/200). ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 100% completed (2 / 2). b) Terrace Water Proofing Work 100% completed. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed (200/200). b) Laying of Granite Countertop 100% completed (200/200). c) Fixing of S.S Sink 100% completed (200/200) ▪ Electrical wire pulling work 100% completed (200/200). ▪ Fixing of Modular Switches & Sockets 100% completed. (200/200) ▪ Fixing of Door Shutters 100% completed (1200/1200). ▪ Fixing of IWC 100% completed (200/200)



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Fixing of UPVC Windows 100% completed (800 /800). ▪ Laying of Green marble for Staircase 100% completed. ▪ Internal Painting <ul style="list-style-type: none"> a) 1st Coat – 100% completed (200/200) ▪ External Plastering 100% completed in all sides. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th SEPTEMBER-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Handrail 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Materials 4 out of 4 received. <ul style="list-style-type: none"> a) Lift 1 - 70% completed. b) Lift 2 - 70% completed. c) Lift 3 - Frame fixing started. d) Lift 4 - Bulkhead fitting completed. ▪ Fire fighting works 45% completed. ▪ Fixing of Window Safety Grills 46% completed. (370 / 800). ➤ Model Flat Finishing works 95% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Handrail 95% completed. ▪ Over Head Tank Ring Main connection works 90% completed. ▪ Fixing of Window Safety Grills 100% completed. (800 / 800). ▪ Bathroom & Toilet False ceiling work 100% completed. ▪ Stilt floor – Grano flooring work 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Materials 4 out of 4 received. <ul style="list-style-type: none"> a) Lift 1 - 70% completed. b) Lift 2 - 70% completed. c) Lift 3 – 20% completed. d) Lift 4 - Bulkhead fitting completed. ▪ Fire fighting works 50% completed. ▪ Lift Cladding work 35% completed. ➤ Model Flat Finishing works 95% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 30 th SEPTEMBER-2024
A2 BLOCK	<p>◆ 100% Completed Works</p> <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> • Base Slab Concrete 2 out of 2 • Tank Wall Concrete 2 out of 2 • Top Cover slab Concrete 2 out of 2 ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ Electrical Conducting works upto Tenth floor. ▪ Fixing of Water supply pipe Lines (CPVC). ▪ Fixing of Sanitary Lines (PVC). ▪ Fixing of Vertical Plumbing Lines in Shaft. ▪ Water Proofing Work <ol style="list-style-type: none"> a) Over Head Water Tank 100% completed (2 / 2) b) Terrace Water proofing 100% completed. ▪ Fixing of Door Shutters 100% completed (1200/1200). ▪ Kitchen Finishing Works <ol style="list-style-type: none"> a) Fixing of Wall Dados 100% completed (200/200). b) Laying of Granite Countertop 100% completed (200/200). c) Fixing of S.S Sink 100% completed (200/200) ▪ Electrical wire pulling work 100% completed (200/200). ▪ Fixing of Bathroom Wall Tiles 100% completed (200/200). ▪ Fixing of Toilet Wall Tiles 100% completed (200/200). ▪ Laying Of Floor Tiles <ol style="list-style-type: none"> a) Ceramic Tiles in Bathroom 100% completed (200/200) b) Ceramic Tiles in Toilet 100% completed (200/200). ▪ Vitrified Tiles in Halls & Bedrooms 100% completed. (200/200). ▪ Fixing of IWC 100% completed (200/200). ▪ Laying of Green marble for Staircase 100% completed. ▪ Fixing of Modular Switches & Sockets 100% completed (200/200). ▪ External plastering in all sides 100% completed. ▪ Fixing of UPVC Windows 100% completed (800 /800).



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30 th SEPTEMBER-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Materials 4 out of 4 received <ul style="list-style-type: none"> a) Lift 1 – 70% completed. b) Lift 2 – 60% completed. c) Lift 3 – 50% completed. d) Lift 4 - Bulkhead fittings completed ▪ Fire fighting works 45% completed. ▪ Internal Painting <ul style="list-style-type: none"> 1st Coat – 30% completed (60/200) 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Over Head Tank Ring Main connection works 95% completed. ▪ Bathroom & Toilet False ceiling work 97% completed. (390 / 400) ▪ Stilt floor – Grano flooring work 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Materials 4 out of 4 received <ul style="list-style-type: none"> a) Lift 1 – 70% completed. b) Lift 2 – 70% completed. c) Lift 3 – 70% completed. d) Lift 4 - Bulkhead fittings completed ▪ Fire fighting works 50% completed. ▪ Internal Painting <ul style="list-style-type: none"> 1st Coat –83% completed (165/200) ▪ Fixing of Window Safety Grills 10% completed. (80 / 800).



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 30 th SEPTEMBER-2024
B1 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 3) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom b) Vitrified Tiles in Halls & Bedrooms. c) Vitrified Tiles in Corridor. ▪ Fixing of UPVC Windows. ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados. b) Laying of Granite Countertop. c) Fixing of S.S Sink. ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. b) Over Head Water Tank. ▪ Fixing of Door Shutters 100% completed (840/840). ▪ Electrical wire pulling work 100% completed (120/120). ▪ Fixing of Modular Switches & Sockets 100% completed. (120/120)



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

B1 BLOCK	<ul style="list-style-type: none"> ▪ Laying of Green marble for Staircase 100% completed. ▪ Fixing of M.S Window Safety Grills 100% completed. ▪ Fixing of IWC 100% completed (120/120) ▪ Lift Cladding works 3 out of 3 100% completed. ▪ Internal Painting <ul style="list-style-type: none"> a) 1st Coat – 100% completed (120/120) ▪ Bathroom false ceiling work 100% completed (240 / 240). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th SEPTEMBER-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 3 out 3. ▪ Application of Exterior Wall Primer ▪ Firefighting works 95% completed. ▪ Terrace Water supply Ring main works 95% completed. ▪ Construction of Earth Pit chambers 95% completed. ▪ Electrical Panel room- Trench works & cable tray fixing works 95% completed. ▪ Works On Progress <ul style="list-style-type: none"> ▪ External Painting- Damp proof elasto paint <ul style="list-style-type: none"> a) South side - 90% completed. b) West side - 90% completed. ● Model Flat Finishing works 95% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 3 out 3. ▪ Application of Exterior Wall Primer ▪ Firefighting works 95% completed. ▪ Terrace Water supply Ring main works 95% completed. ▪ Construction of Earth Pit chambers 95% completed. ▪ Electrical Panel room- Trench works & cable tray fixing works 95% completed. ▪ Works On Progress <ul style="list-style-type: none"> ▪ External Painting- Damp proof elasto paint <ul style="list-style-type: none"> a) South side - 90% completed. b) West side - 90% completed. ▪ Stilt floor Electrical work on progress. ● Model Flat Finishing works 95% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 30 th SEPTEMBER-2024	
B2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 3) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor. ▪ Ceiling plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor completed. ▪ Electrical conducting works 100% completed. (120/120) ▪ Fixing of Internal Water supply pipeline (CPVC) 100% completed (120 / 120) 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30 th SEPTEMBER-2024
	<ul style="list-style-type: none"> ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of Internal Sanitary lines (PVC) 83% completed.(100 / 120). ▪ Fixing of Plumbing lines in Vertical Shafts 54% completed. (13 /24) ▪ External Plastering 80% completed. ▪ Fixing of Bathroom Wall Tiles 38% completed (90 / 240). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 38% completed (90 / 240). b) Vitrified Tiles in Halls & Bedrooms 15% completed (18/120) ▪ Fixing of UPVC Windows started (5/480). ▪ Fixing of UPVC French Doors started (5/240). 	<ul style="list-style-type: none"> ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of Internal Sanitary lines (PVC) 100% completed.(120 / 120). ▪ Fixing of Plumbing lines in Vertical Shafts 83% completed. (20 /24) ▪ External Plastering 85% completed. ▪ Fixing of Bathroom Wall Tiles 50% completed (120 / 240). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 50% completed (120 / 240). b) Vitrified Tiles in Halls & Bedrooms 41% completed (50/120) ▪ Fixing of UPVC Windows 58% completed. (280/480). ▪ Fixing of UPVC French Doors started (10/240). ▪ Fixing of Flush door shutters 66% completed (560 / 840) ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Laying of Granite Countertop 50% completed (60 / 120). ▪ Water Proofing works <ul style="list-style-type: none"> a) Over Head Water Tank – 66% completed (2 / 3)



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 30 th SEPTEMBER-2024
C1 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Internal Plumbing Line. <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom b) Vitrified Tiles in Halls & Bedrooms c) Vitrified Tiles in Corridor completed. ▪ Fixing of UPVC Windows. ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed. ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank b) Terrace floor Water proofing. ▪ Laying of Green marble for Staircase 100% completed. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados. b) Laying of Granite Countertop. c) Fixing of S.S Sink. ▪ Lift Cladding works 4 out of 4. ▪ Fixing of Door Shutters 100% completed (1080 / 1080)

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

C1 BLOCK	<ul style="list-style-type: none"> ▪ Electrical wire pulling work 100% completed (120/120). ▪ Fixing of Modular Switches & Sockets 100% completed. (120/120) ▪ Terrace Water supply Ring main works 100% completed. ▪ Application of Exterior Wall Primer 100% completed. ▪ Fixing of M.S Window Safety Grills 100% completed (480 / 480) ▪ Fixing of IWC 100% completed (120 / 120). ▪ Bathroom False ceiling work 100% completed (360 / 360). ▪ Internal Painting <ul style="list-style-type: none"> a) 1st Coat – 100% completed (120/120) ▪ External Painting- Damp proof elasto 100% completed. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th SEPTEMBER-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Staircase Hand Rails (3 out of 3) 95% completed. ▪ Lift Installation works 4 out 4. ▪ Laying of External Sewerage lines 95% completed. ▪ Laying of External water supply lines 95% completed. ▪ Construction of Earth Pit chambers 95% completed. ▪ Fire Fighting works 95% completed. ▪ Electrical Panel room- Trench works & cable tray fixing works 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of EWC 60% completed (144 / 240). ● Model Flat Finishing works 95% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Staircase Hand Rails (3 out of 3) 95% completed. ▪ Lift Installation works 4 out 4. ▪ Laying of External Sewerage lines 95% completed. ▪ Laying of External water supply lines 95% completed. ▪ Construction of Earth Pit chambers 95% completed. ▪ Fire Fighting works 95% completed. ▪ Electrical Panel room- Trench works & cable tray fixing works 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of EWC 60% completed (144 / 240). ▪ Stilt Floor – Grano flooring works 100% completed. ▪ Fixing of Main Door Lock & other Door Hardware fittings on progress. ● Model Flat Finishing works 95% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 30 th SEPTEMBER-2024
C2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (2 out of 3) (b) Wall Concrete (2 out of 3) (c) Top Cover slab (2 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 3 out of 3 b) Terrace floor Water proofing 100% completed. ▪ Fixing of Bathroom Wall Tiles completed. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom completed. b) Vitrified Tiles in Halls & Bedrooms completed. c) Vitrified Tiles in Corridor completed. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed. (120 / 120) b) Laying of Granite Countertop 100% completed. (120 / 120). c) Fixing of S.S Sink 100% completed. (120 / 120). ▪ Fixing of UPVC Window 100% completed. (600 / 600) ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed. (240 /240) ▪ Fixing of Main Door & Internal Shutters 100% completed (1080 / 1080) ▪ Laying of Green marble for Staircase 100% completed.. ▪ Electrical wire pulling 100% completed (120 /120).



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

C2 BLOCK	<ul style="list-style-type: none"> ▪ Fixing of Modular Switches & Sockets 100% completed. (120/120). ▪ Lift Cladding work 100% completed. ▪ Application of Exterior Wall Primer 100% completed. ▪ Fixing of M.S Window Safety Grills 100% completed (480 / 480) ▪ Bathroom False ceiling work 100% completed (360 / 360) ▪ Fixing of IWC 100% completed (120 / 120) ▪ Internal Painting <ul style="list-style-type: none"> a) 1st Coat – 100% completed (120/120) 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th SEPTEMBER-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Lift Installation works 4 out 4 <ul style="list-style-type: none"> a) Lift 1, 2 & 3 - 90% completed. b) Lift 4 - 85% completed. ▪ Terrace Water supply Ring main works 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fire fighting works 90% completed. ▪ Laying of External Sewerage lines 95% completed. ▪ Laying of External water supply lines 90% completed. ▪ External Painting- Damp proof elasto 95% completed. ▪ Construction of Earth Pit chambers 95% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Lift Installation works 4 out 4 <ul style="list-style-type: none"> a) Lift 1, 2 & 3 - 90% completed. b) Lift 4 - 85% completed. ▪ Terrace Water supply Ring main works 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fire fighting works 90% completed. ▪ Laying of External Sewerage lines 95% completed. ▪ Laying of External water supply lines 90% completed. ▪ External Painting- Damp proof elasto 95% completed. ▪ Construction of Earth Pit chambers 95% completed. ▪ Stilt Floor – Grano flooring works 100% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 30 th SEPTEMBER-2024
C3 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (2 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank (2 / 2) completed. b) Terrace floor Water proofing 100% completed. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed (100/100) b) Laying of Granite Countertop 100% completed. (100/100). c) Fixing of S.S Sink 100% completed. (100/ 100). ▪ Fixing of Bathroom Wall Tiles 100% completed. (300 /300) ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 100% completed. (300 /300) b) Vitrified Tiles in Halls & Bedrooms 100% completed. (100 / 100) ▪ Laying of Green marble for Staircase 100% completed. ▪ Electrical wire pulling 100% completed (100 /100). ▪ Fixing of UPVC Window 100% Completed. (500 / 500). ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed (200 / 200). ▪ Fixing of Main Door & Internal Shutters 100% completed (900 / 900). ▪ Electrical Wire pulling 100% completed (100 /100). ▪ Fixing of Modular Switches & Sockets 100% completed. (100/100). ▪ Application of Exterior Wall Primer 100% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

C3 BLOCK	<ul style="list-style-type: none"> ▪ Fixing of M.S Window Safety Grills 100% completed (400 / 400) ▪ Fixing of IWC 100% completed (100 / 100) ▪ Internal Painting <ul style="list-style-type: none"> a) 1st Coat – 100% completed (120/120) 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th SEPTEMBER-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails. ▪ Lift Cladding work 4 out of 4 - 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4 <ul style="list-style-type: none"> a) Lift1 & 2 -90% completed. b) Lift 3 & 4 – 85% completed. ▪ Fire fighting works 65% completed. ▪ Laying of External Sewerage lines 85% completed. ▪ Laying of External water supply lines 75% completed. ▪ External Painting- Damp proof elasto 90% completed. ▪ Bathroom false ceiling work 93% completed (279 / 300) 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails. ▪ Lift Cladding work 4 out of 4 - 95% completed. ▪ External Painting- Damp proof elasto 95% completed. ▪ Bathroom false ceiling work 100% completed (300 / 300) ▪ Lift Installation works 4 out 4 <ul style="list-style-type: none"> a) Lift1 & 2 -90% completed. b) Lift 3 & 4 – 85% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fire fighting works 90% completed. ▪ Laying of External Sewerage lines 90% completed. ▪ Laying of External water supply lines 90% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 30 th SEPTEMBER-2024
D1 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 3 out of 3 b) Terrace floor Water proofing 100% completed. ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles 100% completed. (320 / 320). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 100% completed. (320 / 320) b) Vitrified Tiles in Halls & Bedrooms 100% completed. (80 / 80). ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed. (80 / 80) b) Laying of Granite Countertop 100% completed. (80 / 80). c) Fixing of S.S Sink 100% completed. (80 / 80). ▪ Fixing of Main Door & Internal Shutters 100% completed (880 / 880) ▪ Electrical Wire pulling works 100% completed. (80/ 80). ▪ Fixing of Modular Switches & Sockets 100% completed. (80/80) ▪ Fixing of UPVC Windows 100% completed. (400 / 400). ▪ Fixing of UPVC French Door 100% competed.(without Mosquito mesh shutter) (160 / 160) ▪ Application of External Wall Primer- 100% completed. ▪ Lift Cladding works 4 out of 4 - 100% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

D1 BLOCK	<ul style="list-style-type: none"> ▪ Laying of Green marble for Staircase 100% completed. ▪ Bathroom false ceiling work 100% completed (320 / 320) ▪ Fixing of IWC 100% completed (80 / 80) ▪ External plastering in all sides 100% completed. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th SEPTEMBER-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External Painting - Damp proof elasto 95% completed. ▪ Fire fighting works 95% completed. ▪ Laying of External Sewerage lines 95% completed ▪ Laying of External Water supply lines 95% completed. ▪ Laying of Storm Water drain pipes 95% completed. ▪ Fixing of M.S Window Safety Grills 94% completed (302 / 320) ▪ Laying of Grano flooring in Stilt floor 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works <ol style="list-style-type: none"> a) 3 Lifts - 90% completed. b) 4th Lift – 70% completed. ▪ Construction of Earth Pit chambers 90% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External Painting - Damp proof elasto 100% completed. ▪ Fire fighting works 95% completed. ▪ Laying of External Sewerage lines 95% completed ▪ Laying of External Water supply lines 95% completed. ▪ Laying of Storm Water drain pipes 95% completed. ▪ Fixing of M.S Window Safety Grills 95% completed (305 / 320) ▪ Laying of Grano flooring in Stilt floor 95% completed. ▪ Fixing of EWC 100% completed (240 / 240) ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works <ol style="list-style-type: none"> a) 3 Lifts - 90% completed. b) 4th Lift – 75% completed. ▪ Construction of Earth Pit chambers 95% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 30 th SEPTEMBER-2024
D2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 3) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom b) Vitrified Tiles in Halls & Bedrooms. c) Vitrified Tiles in Corridor. ▪ Fixing of UPVC Windows. ▪ Fixing of Main Door & Internal Shutters. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados. b) Laying of Granite Countertop. c) Fixing of S.S Sink. ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. b) Over Head Water Tank ▪ Laying of Green marble for Staircase. ▪ Fixing of UPVC French Door (without Mosquito mesh shutter). ▪ Electrical Wire pulling works 100% completed (80/ 80).



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

D2 BLOCK	<ul style="list-style-type: none"> ▪ Fixing of Modular Switches & Sockets 100% completed. (80/80). ▪ Fire Fighting Works 100% completed. ▪ Fixing of M.S Window Safety Grills 100% completed. (320 / 320). ▪ Lift Cladding works 4 out of 4 – 100% completed. ▪ Application of Exterior Wall Primer-100% completed. ▪ Fixing of IWC 100% completed (80 / 80) ▪ Bathroom false ceiling work 100% completed (320 / 320) 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th SEPTEMBER-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Laying of External Sewerage lines 95% completed. ▪ Laying of External Water supply lines 95% completed. ▪ Laying of Storm Water drain pipes 95% completed. ▪ Fire Fighting Works 95% completed. ▪ Construction of Earth Pit chambers 95% completed. ▪ External Painting - Damp proof elasto 95% completed. ▪ Electrical Panel room- Trench works & cable tray fixing works 95% completed. ▪ Fixing of M.S Window Safety Grills 94% completed (303 / 320) ▪ Laying of Grano flooring in Stilt floor 95% completed. ◆ Works On Progress Lift Commissioning works for 4 Lifts 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Laying of External Sewerage lines 95% completed. ▪ Laying of External Water supply lines 95% completed. ▪ Laying of Storm Water drain pipes 95% completed. ▪ Fire Fighting Works 95% completed. ▪ Construction of Earth Pit chambers 100% completed. ▪ External Painting - Damp proof elasto 95% completed. ▪ Electrical Panel room- Trench works & cable tray fixing works 95% completed. ▪ Fixing of M.S Window Safety Grills 95% completed (305 / 320) ▪ Laying of Grano flooring in Stilt floor 100% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Commissioning works <ul style="list-style-type: none"> a) All 4 Lifts Slow Speed commissioning completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 30 th SEPTEMBER-2024
D3 BLOCK	<p>◆ 100% Completed Works</p> <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 1 out of 3 ▪ Fixing of Bathroom Wall Tiles 100% completed. (320 / 320) ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed. (80 / 80) b) Laying of Granite Countertop 100% completed. (80 / 80). ▪ Fixing of S.S Sink 100% completed. (80 / 80). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 100% completed. (320 / 320) b) Vitrified Tiles in Halls & Bedrooms 100% completed. (80 / 80) c) Vitrified Tiles in Corridor 100% completed. ▪ Fixing of Main Door & Internal Shutters 100% completed (880 / 880) ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 100% completed. b) Over Head Water Tank 3 out of 3 completed. ▪ Fixing of UPVC Windows 100% completed. (400 / 400)



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Electrical Wire pulling works 100% completed (80/ 80). ▪ Fixing of Modular Switches & Sockets 100% completed. (80/80). ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed (160 / 160). ▪ Laying of Green marble for Staircase 100% completed. ▪ Lift Cladding works 4 out of 4 - 100% completed. ▪ Application of Exterior Wall Primer 100% completed. ▪ Fixing of IWC 100% completed (80 / 80) ▪ Bathroom false ceiling work 100% completed (320 / 320). ▪ Laying of Grano flooring in Stilt floor 100% completed. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th SEPTEMBER-2024
D3 BLOCK	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Laying of External Sewerage lines 95% completed. ▪ Laying of External water supply lines 95% completed. ▪ Laying of Storm Water drain pipes 95% completed. ▪ Firefighting works 95% completed. ▪.Fixing of M.S Window Safety Grills 90% completed (285/320). ▪ External Painting - Damp proof elasto 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works - 4 out of 4 – <ul style="list-style-type: none"> a) 3 Lifts - 90% completed. b) 4th Lift - 80% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Laying of External Sewerage lines 95% completed. ▪ Laying of External water supply lines 95% completed. ▪ Laying of Storm Water drain pipes 95% completed. ▪ Firefighting works 95% completed. ▪ Fixing of M.S Window Safety Grills 94% completed (300/320). ▪ External Painting - Damp proof elasto 100% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works - 4 out of 4 – <ul style="list-style-type: none"> c) 3 Lifts - 90% completed. d) 4th Lift - 80% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 30 th SEPTEMBER-2024
COMMUNITY HALL	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (2 out of 2) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (b) Tank Wall Concrete (c) Top Cover slab Concrete. ▪ Block work upto Fourth floor & Parapet wall. ▪ Ceiling Plastering upto Fourth floor. ▪ Wall plastering upto Fourth floor. ▪ 1st Coat Wall Putty upto Fourth floor. ▪ 2nd Coat Wall Putty upto Fourth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Vitrified Floor Tiles in Hall & rooms b) Ceramic Floor Tiles in Bathrooms. c) Kota Stone in Staircase & Lobby ▪ Fixing of UPVC Windows. ▪ Fixing of Wooden flush Door for rooms. ▪ Fixing of Fire Safety Door for Hall Main Entrance ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. b) Over Head Water Tank. ▪ Lift Installation works 4 out 4 100% completed. ▪ Lift Cladding works 4 out of 4 – 100% completed. ▪ Application of Exterior Wall Primer.-100% completed

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30 th SEPTEMBER-2024
COMMUNITY HALL	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fire fighting works – Installation of Pipelines 95% completed. ▪ Electrical Wire & cables pulling work 95% completed. ▪ Fixing of Modular Switches & Sockets 95% completed. ▪ Excavation for laying of Firefighting Hydrant pipes 95% completed. <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Fixing of Sanitary fixtures 40% completed. ▪ Application of Exterior Wall Damp proof Paint 50% completed. ▪ Lift commissioning works. <ul style="list-style-type: none"> a) Lift 1 – High Speed completed. b) Lift 2 – Slow Speed completed. 	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fire fighting works – Installation of Pipelines 95% completed. ▪ Electrical Wire & cables pulling work 95% completed. ▪ Fixing of Modular Switches & Sockets 95% completed. ▪ Excavation for laying of Firefighting Hydrant pipes 95% completed. ▪ Stilt floor – Grano flooring 95% completed. <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Fixing of Sanitary fixtures 50% completed. ▪ Application of Exterior Wall Damp proof Paint 70% completed. ▪ Lift commissioning works. <ul style="list-style-type: none"> a) Lift 1 – High Speed completed. b) Lift 2 – Slow Speed completed.

	STATUS AS ON 30 th SEPTEMBER-2024
EXTERNAL DEVELOPMENT WORKS	<ul style="list-style-type: none"> ➤ Underground Sump-1 (Near B-Block) <ul style="list-style-type: none"> ▪ Base Slab R.C.C 100% completed. ▪ Sump Wall - R.C.C 100% completed. ▪ Top slab R.C.C 100% completed. ▪ Outer Wall Waterproof plastering – 100% completed. ▪ Inner Wall Waterproof plastering – 100% completed. ▪ Fixing of Ladder in Pump room completed. ➤ Underground Sump-2 (Near D-Block) <ul style="list-style-type: none"> ▪ Base Slab - R.C.C 100% completed. ▪ Sump Wall - R.C.C 100% completed. ▪ Top slab R.C.C 100% completed. ▪ Outer Wall Waterproof plastering – 100% completed. ▪ Inner Wall Waterproof plastering 100% completed. ▪ Fixing of Ladder in Pump room completed.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none">➤ Sewage Treatment Plant-2 (Near D-Block)<ul style="list-style-type: none">▪ Base slab – R.C.C 100% completed.▪ STP Wall – R.C.C 100% completed.▪ STP Top Slab – R.C.C 100% completed.▪ STP Pump Room completed.▪ Outer wall Waterproof plastering 100% completed.▪ Inner Wall Waterproof plastering 100% completed.▪ Installation of STP 90% completed. ➤ Sewage Treatment Plant-1 (Near C3-Block)<ul style="list-style-type: none">▪ Base slab RCC completed.▪ STP Wall Concrete 90% completed.▪ STP Top Slab Concrete 90% completed.▪ STP Pump room Top slab Shuttering on progress.▪ Internal Waterproof plastering 10% completed. ➤ Laying of External Sewer lines<ul style="list-style-type: none">▪ Type D All Blocks – 100% completed.▪ C1 Block - 95% completed▪ C2 Block - 90% completed.▪ C3 Block - 90% completed.▪ B1 Block - 35% completed.▪ A1 Block - 90% completed.▪ A2 Block - 90% completed. ➤ Laying of External Water Supply lines<ul style="list-style-type: none">▪ Type D All Blocks – 95% completed.▪ C1 Block – 95% completed▪ C2 Block – 90% completed.▪ C3 Block – 90% completed.▪ B1 Block – 25% completed.▪ A1 Block - 85% completed.▪ A2 Block – 85% completed. ➤ Laying of Storm Water Drainage.<ul style="list-style-type: none">▪ Type D All Blocks – 95% completed.▪ C1 Block – 85% completed.▪ C2 Block – 85% completed.▪ C3 Block – 85% completed.▪ A1 Block – 85% completed.▪ A2 Block – 85% completed. ➤ External Electrification works.<ul style="list-style-type: none">▪ Total 8 Nos Transformers received out of 10 Nos.▪ Type D All Blocks – Fixing of Pole structure for Transformers 100%
--	--

PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

	<p>completed. Fixing of Single poles 90% completed.</p> <ul style="list-style-type: none">▪ Type A,B & C – Fixing of Pole structure for Transformers 100% completed. Fixing of Single poles 90% completed.▪ Installation of Over Head Power line<ul style="list-style-type: none">a) In Type –D block – 85% completed.b) In Type – B Block – 75% completed. <p>➤ Laying of Roads.</p> <ul style="list-style-type: none">▪ Formation of Sub-Grade<ul style="list-style-type: none">a) Around Type D All Blocks – 95% completed.b) Around Type A1 Block – 50% completed.c) Around Community Hall – 75% completed.▪ Laying of Granular Sub Base<ul style="list-style-type: none">a) Around Type D All Blocks – 85% completed.
--	--

PHOTOGRAPHS OF WORK PROGRESS AS ON 30th SEPTEMBER 2024

Community Hall: Fire fighting- External Hydrant pipes connection works on progress. Preparation for final coat of External Painting as per New proposed colour pattern on progress.



Proposed New Colour for Community Hall

PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block A1: Lift Installation works & External Painting final coat on progress.



PROGRESS REPORT CGEWHO – CHENNAI PHASE-III PROJECT

Block A2 : Door shutters Painting works & External Painting final coat on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block B1: Stilt floor electrical wire pulling & fixing of light points on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block B2 : Bathroom Wall Tiling works & Fire fighting works in One shaft on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block C1: Fixing of Hardware fittings in Door shutters & fixing of Ladders in O.H.T on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block C2: Fixing of Manholes Cover frames, Grano flooring in Stilt floor & Installation of Fire Hydrant Pipes in Terrace on progress.



PROGRESS REPORT CGEWHO – CHENNAI PHASE-III PROJECT

Block C3: Stilt Grano flooring work, fixing of frames & cover slabs for chambers, fixing of ladders in O.H.T & laying of Earthing wires for Lifts on progress



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block D1: Fixing of Main Door Lock & Other Door Hardware fittings on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block D2: Groove cutting work in Stilt floor on progress



Block D3: Fixing of EWC in Bathrooms on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Sewage Treatment Plant 1 (Near C Block). STP Pump room Top Slab Shuttering & reinforcement works on progress.



Under Ground Sump 1 (Opp to B1 Block). Fixing of Ladder inside Pump room completed.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Under Ground Sump 2 (Near D1 Block). Installation of Pumps in Sump on progress.



External Sewerage Lines : Excavation for Road crossing in C3 Block & Excavation in between B1 & B2 block for laying of Eco-drain pipes on Progress



Crossing in C3- Block



In Between B1 & B2 Block

PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT


External Electrification Works : Supply of Transformers & Poles, installation of Over Head Power cables on progress



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Road Works : Laying of Granular Sub-base around D1, D2 & D3 blocks & Rolling completed.

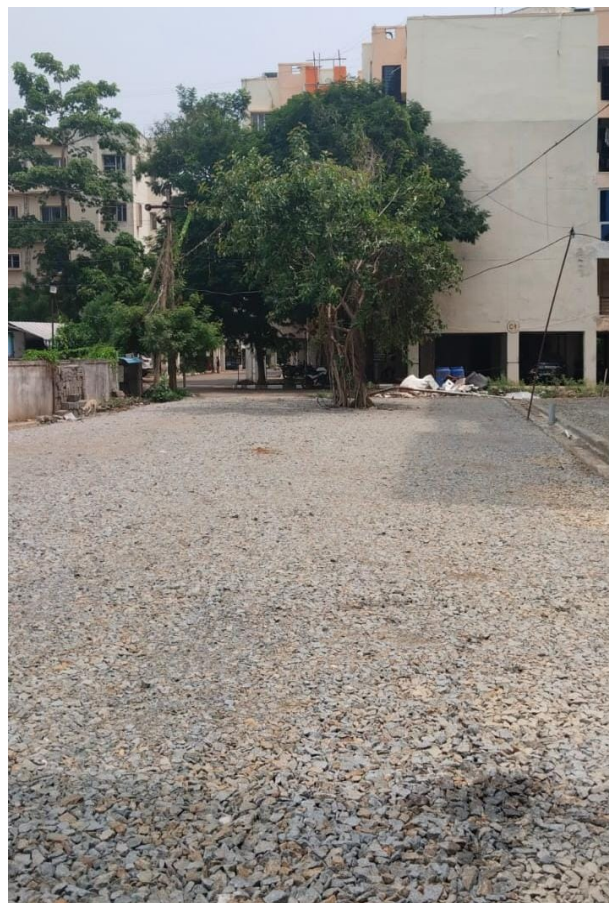

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

QUALITY CONTROL

DURING CONSTRUCTION FOLLOWING QUALITY CONTROL TESTS CONDUCTED AT SITE:

Sl.No.	Materials	Source from	Test Done	Result
1	M-Sand	Arcot (T.K), Ranipet (Dist) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2.	P- Sand	Uthiramerur, Kanchipuram (DT) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2	Coarse Aggregate (20mm)	Sriperambathur, Kanchipuram (Dt), Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
3	Coarse Aggregate (12mm)	Sriperambathur, Kanchipuram (Dt) Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
4	Cement	Third party testing is being done.		
5	Steel	Third party testing is being done.		
6	Pile Integrity	Third party testing is being done.		
7	Soil Compaction	Third party testing is being done.		
8	RCC cubes are being tested and Register is being maintained.			
9	Slump test conducted at site to insure workability of concrete.			
