

**CGEWHO – CHENNAI PHASE-III  
PROJECT**



**MONTHLY PROGRESS REPORT**

**STATUS AS ON : 30.11.2024**

**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

30.11.2024

BLOCK	STATUS AS ON 30 <sup>th</sup> NOVEMBER-2024
A1 BLOCK	<p>◆ <b>100% Completed Works</b></p> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (4 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank               <ul style="list-style-type: none"> <li>(a) Base Slab Concrete 2 out of 2</li> <li>(b) Tank Wall Concrete 2 out of 2</li> <li>(c) Top Cover slab Concrete 2 out of 2</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor</li> <li>▪ Electrical Conducting works in Tenth floor.</li> <li>▪ Fixing of Water supply pipe Lines (CPVC).</li> <li>▪ Fixing of Sanitary Lines (PVC).</li> <li>▪ External Plastering 100% completed in all sides.</li> <li>▪ Fixing of Vertical Plumbing Lines in Shaft.</li> <li>▪ Fixing of Bathroom Wall Tiles 100% completed (200/200)</li> <li>▪ Fixing of Toilet Wall Tiles 100% completed (200/200)</li> <li>▪ Laying Of Floor Tiles               <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathrooms 100% completed (200/200)</li> <li>b) Ceramic Tiles in Toilets 100% completed (200/200)</li> </ul> </li> <li>▪ Vitrified Tiles in Halls &amp; Bedrooms 100% completed (200/200).</li> <li>▪ Fixing of UPVC Windows &amp; Ventilators 100% completed ( 800 /800 ).</li> <li>▪ Fixing of Door Shutters 100% completed (1200/1200).</li> <li>▪ Kitchen Finishing Works               <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados 100% completed (200/200).</li> <li>b) Laying of Granite Countertop 100% completed (200/200).</li> <li>c) Fixing of S.S Sink 100% completed (200/200)</li> </ul> </li> <li>▪ Water Proofing Works.               <ul style="list-style-type: none"> <li>a) Over Head Water Tank 100% completed ( 2 / 2).</li> <li>b) Terrace Water Proofing Work 100% completed.</li> </ul> </li> <li>▪ Laying of Green marble for Staircase 100% completed.</li> <li>▪ Electrical wire pulling work 100% completed (200/200).</li> <li>▪ Fixing of Modular Switches &amp; Sockets 100% completed. (200/200)</li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

	<ul style="list-style-type: none"> <li>▪ Fixing of Window Safety Grills 100% completed. (800 / 800).</li> <li>▪ Bathroom &amp; Toilet False ceiling work 100% completed.</li> <li>▪ Fixing of IWC 100% completed (200/200)</li> <li>▪ Internal Painting               <ul style="list-style-type: none"> <li>a) 1<sup>st</sup> Coat – 100% completed (200/200)</li> </ul> </li> <li>▪ Stilt floor – Grano flooring work completed.</li> <li>▪ Fixing of Door Hardware fittings.</li> <li>▪ Electrical Panel &amp; Cable tray fixing works completed.</li> <li>▪ Firefighting works completed (Application for NOC submitted, Inspection scheduled on 5<sup>th</sup> Dec 2024).</li> </ul>	
	<b>WORKS ON PROGRESS</b>	<b>WORKS TO BE DONE</b>
	<ul style="list-style-type: none"> <li>▪ Balcony Handrail painting works 50% completed.</li> <li>▪ Staircase Handrail finishing works 50% completed.</li> <li>▪ Over Head Tank Ring Main connection works 95% completed.</li> <li>▪ Lift Erection works (Total 4 Lifts)               <ul style="list-style-type: none"> <li>a) Lift 1 - 70% completed.</li> <li>b) Lift 2 - 70% completed.</li> <li>c) Lift 3 - 70% completed.</li> <li>d) Lift 4 - 40% completed.</li> </ul> </li> <li>▪ Lift Cladding work 70% completed.</li> <li>▪ Fixing of Main Door lock 30% completed (60\200).</li> <li>▪ Conducting work for lightening arrester on progress.</li> </ul>	<ul style="list-style-type: none"> <li>▪ Fixing of Wash basins</li> <li>▪ Fixing of Plumbing CP fittings.</li> <li>▪ Internal Painting 2<sup>nd</sup> Coating</li> <li>▪ Lift Commissioning works.</li> <li>▪ Fixing of EB meters.</li> <li>▪ Fixing of Electrical fittings in common areas.</li> <li>▪ Installation of lightening arrester.</li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

BLOCK	STATUS AS ON 30 <sup>th</sup> NOVEMBER-2024
A2 BLOCK	<p>◆ <b>100% Completed Works</b></p> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (4 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank               <ul style="list-style-type: none"> <li>(a) Base Slab Concrete 2 out of 2</li> <li>(b) Tank Wall Concrete 2 out of 2</li> <li>(c) Top Cover slab Concrete 2 out of 2</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor</li> <li>▪ Electrical Conducting works in Tenth floor.</li> <li>▪ Fixing of Water supply pipe Lines (CPVC).</li> <li>▪ Fixing of Sanitary Lines (PVC).</li> <li>▪ External Plastering 100% completed in all sides.</li> <li>▪ Fixing of Vertical Plumbing Lines in Shaft.</li> <li>▪ Fixing of Bathroom Wall Tiles 100% completed (200/200)</li> <li>▪ Fixing of Toilet Wall Tiles 100% completed (200/200)</li> <li>▪ Laying Of Floor Tiles               <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathrooms 100% completed (200/200)</li> <li>b) Ceramic Tiles in Toilets 100% completed (200/200)</li> </ul> </li> <li>▪ Vitrified Tiles in Halls &amp; Bedrooms 100% completed (200/200).</li> <li>▪ Fixing of UPVC Windows &amp; Ventilators 100% completed ( 800 /800 ).</li> <li>▪ Fixing of Door Shutters 100% completed (1200/1200).</li> <li>▪ Kitchen Finishing Works               <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados 100% completed (200/200).</li> <li>b) Laying of Granite Countertop 100% completed (200/200).</li> <li>c) Fixing of S.S Sink 100% completed (200/200)</li> </ul> </li> <li>▪ Water Proofing Works.               <ul style="list-style-type: none"> <li>a) Over Head Water Tank 100% completed ( 2 / 2).</li> <li>b) Terrace Water Proofing Work 100% completed.</li> </ul> </li> <li>▪ Laying of Green marble for Staircase 100% completed.</li> <li>▪ Electrical wire pulling work 100% completed (200/200).</li> <li>▪ Fixing of Modular Switches &amp; Sockets 100% completed. (200/200)</li> <li>▪ Bathroom &amp; Toilet False ceiling work 100% completed.</li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

	<ul style="list-style-type: none"> <li>▪ Fixing of IWC 100% completed (200/200)</li> <li>▪ Internal Painting               <ul style="list-style-type: none"> <li>a) 1<sup>st</sup> Coat – 100% completed (200/200)</li> </ul> </li> <li>▪ Stilt floor – Grano flooring work completed.</li> <li>▪ Fixing of Door Hardware fittings.</li> <li>▪ Electrical Panel &amp; Cable tray fixing works completed.</li> <li>▪ Firefighting works completed (Application for NOC submitted, Inspection scheduled on 5<sup>th</sup> Dec 2024).</li> </ul>	
	<b>WORKS ON PROGRESS</b>	<b>WORKS TO BE DONE</b>
	<ul style="list-style-type: none"> <li>▪ Fixing of Window Safety Grills 90% completed. (780 / 800).</li> <li>▪ Balcony Handrail painting works 50% completed.</li> <li>▪ Staircase Handrail finishing works 50% completed.</li> <li>▪ Over Head Tank Ring Main connection works 95% completed.</li> <li>▪ Lift Erection works (Total 4 Lifts)               <ul style="list-style-type: none"> <li>a) Lift 1 - 70% completed.</li> <li>b) Lift 2 - 70% completed.</li> <li>c) Lift 3 – 70% completed.</li> <li>d) Lift 4 – 45% completed.</li> </ul> </li> <li>▪ Lift Cladding work 70% completed.</li> <li>▪ Fixing of Main Door lock 70% completed (140 \ 200)</li> </ul>	<ul style="list-style-type: none"> <li>▪ Fixing of Wash basins</li> <li>▪ Fixing of Plumbing CP fittings.</li> <li>▪ Internal Painting 2<sup>nd</sup> Coating</li> <li>▪ Lift Commissioning works.</li> <li>▪ Fixing of EB meters.</li> <li>▪ Fixing of Electrical fittings in common areas.</li> <li>▪ Installation of lightning arrester.</li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

BLOCK	STATUS AS ON 30 <sup>th</sup> NOVEMBER-2024
B1 BLOCK	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (3 out of 3) - Slab Concrete.</li> <li>▪ Over Head Water Tank               <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (3 out of 3)</li> <li>(b) Wall Concrete (3 out of 3)</li> <li>(c) Top Cover slab (3 out of 3 )</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Fixing of Internal Plumbing Line               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ External Plastering in all sides.</li> <li>▪ Fixing of Vertical Plumbing Line in Shafts               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles.</li> <li>▪ Laying Of Floor Tiles               <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom</li> <li>b) Vitrified Tiles in Halls &amp; Bedrooms.</li> <li>c) Vitrified Tiles in Corridor.</li> </ul> </li> <li>▪ Fixing of UPVC Windows.</li> <li>▪ Fixing of UPVC French Door (without Mosquito mesh shutter)</li> <li>▪ Fixing of Door Shutters 100% completed (840/840).</li> <li>▪ Kitchen Finishing Works               <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados.</li> <li>b) Laying of Granite Countertop.</li> <li>c) Fixing of S.S Sink.</li> </ul> </li> <li>▪ Water Proofing Works.               <ul style="list-style-type: none"> <li>a) Terrace floor Water proofing.</li> <li>b) Over Head Water Tank.</li> </ul> </li> <li>▪ Laying of Green marble for Staircase 100% completed.</li> <li>▪ Electrical wire pulling work 100% completed (120/120).</li> <li>▪ Fixing of Modular Switches &amp; Sockets 100% completed. (120/120)</li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

B1 BLOCK	<ul style="list-style-type: none"> <li>▪ Fixing of M.S Window Safety Grills 100% completed.</li> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails.</li> <li>▪ Bathroom false ceiling work 100% completed ( 240 / 240 ).</li> <li>▪ Fixing of IWC 100% completed (120/120)</li> <li>▪ Fixing of EWC 100% completed (120/120)</li> <li>▪ Lift Cladding works 3 out of 3 100% completed.</li> <li>▪ Internal Painting               <ul style="list-style-type: none"> <li>a) 1<sup>st</sup> Coat – 100% completed (120/120)</li> </ul> </li> <li>▪ Over Head Tank Ring Main Connection works 100% completed.</li> <li>▪ Application of Exterior Wall Primer</li> <li>▪ Electrical Panel &amp; cable tray fixing works completed.</li> <li>▪ Construction of Earth Pit chambers completed.</li> <li>▪ Fixing of Door Hardware fittings.</li> <li>▪ Stilt Grano flooring completed.</li> <li>▪ Fixing of Main Door lock 100% completed ( 120 / 120 )</li> <li>▪ Over Head Tank Ring Main connection works.</li> </ul>	
	<b>WORKS ON PROGRESS</b>	<b>WORKS TO BE DONE</b>
	<ul style="list-style-type: none"> <li>▪ Lift Installation works 90% completed. ( 3 out 3 ).</li> <li>▪ Firefighting works 95% completed.</li> <li>▪ External Painting- Damp proof elasto paint overall 90% completed.</li> </ul>	<ul style="list-style-type: none"> <li>▪ Fixing of Wash basins</li> <li>▪ Fixing of Plumbing CP fittings.</li> <li>▪ Internal Painting 2<sup>nd</sup> Coating</li> <li>▪ Lift Commissioning works.</li> <li>▪ Fixing of EB meters.</li> <li>▪ Fixing of Electrical fittings in common areas.</li> <li>▪ Installation of lightening arrester.</li> </ul>
<b>BLOCK</b>	<b>STATUS AS ON 30<sup>th</sup> NOVEMBER-2024</b>	
B2 BLOCK	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (3 out of 3) - Slab Concrete.</li> <li>▪ Over Head Water Tank               <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (3 out of 3)</li> <li>(b) Wall Concrete (3 out of 3)</li> <li>(c) Top Cover slab (3 out of 3)</li> </ul> </li> </ul> </li> </ul>	



# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

B2 BLOCK	<ul style="list-style-type: none"> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Fixing of Internal Plumbing Line               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ Fixing of Vertical Plumbing Line in Shafts               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> <li>▪ Water Proofing Works.               <ul style="list-style-type: none"> <li>a) Over Head Water Tank.</li> </ul> </li> </ul>	
	<b>WORKS ON PROGRESS</b>	<b>WORKS TO BE DONE</b>
B2 BLOCK	<ul style="list-style-type: none"> <li>▪ 2<sup>nd</sup> Coat Wall Putty 40% completed (48 / 120).</li> <li>▪ External Plastering 92% completed.</li> <li>▪ Fixing of Bathroom Wall Tiles 87% completed ( 210 / 240).</li> <li>▪ Laying Of Floor Tiles               <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom 87% completed (210 / 240).</li> <li>b) Vitrified Tiles in Halls &amp; Bedrooms 87% completed (105/120)</li> </ul> </li> <li>▪ Fixing of UPVC Windows 58% completed. (350/480).</li> <li>▪ Fixing of UPVC French Doors 24% completed (100/240).</li> <li>▪ Fixing of Flush door shutters 83% completed ( 700 / 840 )</li> <li>▪ Kitchen Finishing Works               <ul style="list-style-type: none"> <li>a) Laying of Granite Countertop 95% completed (114 / 120 ).</li> <li>b) Fixing of Kitchen wall Dados 71% completed (86/120).</li> <li>c) Fixing of S.S Sink 95% completed (114/120)</li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>▪ Lift Installation works ( Lift Materials received - 3 out of 3 ).</li> <li>▪ Lift Cladding works.</li> <li>▪ Laying of Staircase Green marble.</li> <li>▪ Internal Electrification works               <ul style="list-style-type: none"> <li>a) Electrical wire pulling work.</li> <li>b) Fixing of Modular Switches &amp; Sockets.</li> </ul> </li> <li>▪ Fixing of Window safety grills (Fabrication on process)</li> <li>▪ Overhead Tank -Ring main works</li> <li>▪ Fixing of EWC</li> <li>▪ Fixing of Wash basins.</li> <li>▪ Stilt Grano flooring</li> <li>▪ Fixing of Door Hardware fittings.</li> <li>▪ Fixing of Main Door lock</li> <li>▪ Fixing of Plumbing CP fittings.</li> <li>▪ Internal Painting 2<sup>nd</sup> Coating</li> <li>▪ Lift Commissioning works.</li> <li>▪ Fixing of EB meters.</li> <li>▪ Fixing of Electrical fittings in common areas.</li> <li>▪ Installation of lightening arrester.</li> </ul>





**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

	<ul style="list-style-type: none"> <li>▪ Terrace Water Proofing works 30% completed.</li> <li>▪ Firefighting works 25% completed.</li> <li>▪ Bathroom false ceiling work 75% completed (180/240).</li> </ul>	
<b>BLOCK</b>	<b>STATUS AS ON 30<sup>th</sup> NOVEMBER-2024</b>	
C1 BLOCK	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (4 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank                             <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (3 out of 3)</li> <li>(b) Wall Concrete (3 out of 3)</li> <li>(c) Top Cover slab (3 out of 3 )</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Fixing of Internal Plumbing Line                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ External Plastering in all sides.</li> <li>▪ Fixing of Vertical Plumbing Line in Shafts                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles.</li> <li>▪ Laying Of Floor Tiles                             <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom</li> <li>b) Vitrified Tiles in Halls &amp; Bedrooms.</li> <li>c) Vitrified Tiles in Corridor.</li> </ul> </li> <li>▪ Fixing of UPVC Windows.</li> <li>▪ Fixing of UPVC French Door (without Mosquito mesh shutter)</li> <li>▪ Fixing of Door Shutters 100% completed (1080/1080).</li> <li>▪ Kitchen Finishing Works                             <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados.</li> <li>b) Laying of Granite Countertop.</li> <li>c) Fixing of S.S Sink.</li> </ul> </li> </ul> </li> </ul>	



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

C1 BLOCK	<ul style="list-style-type: none"> <li>▪ Water Proofing Works.               <ul style="list-style-type: none"> <li>a) Terrace floor Water proofing.</li> <li>b) Over Head Water Tank.</li> </ul> </li> <li>▪ Laying of Green marble for Staircase 100% completed.</li> <li>▪ Electrical wire pulling work 100% completed (120/120).</li> <li>▪ Fixing of Modular Switches &amp; Sockets 100% completed. (120/120)</li> <li>▪ Fixing of M.S Window Safety Grills 100% completed.</li> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails.</li> <li>▪ Bathroom false ceiling work 100% completed (360 / 360).</li> <li>▪ Fixing of IWC 100% completed (120/120)</li> <li>▪ Fixing of EWC 100% completed (240/240)</li> <li>▪ Lift Cladding works 4 out of 4 100% completed.</li> <li>▪ Internal Painting               <ul style="list-style-type: none"> <li>a) 1<sup>st</sup> Coat – 100% completed (120/120)</li> </ul> </li> <li>▪ External Damp proof elasto painting completed.</li> <li>▪ Over Head Tank Ring Main Connection works completed.</li> <li>▪ Fixing of Door Hardware Fittings completed.</li> <li>▪ Fixing of Main Door Lock completed.</li> <li>▪ Plumbing shaft top covering completed.</li> <li>▪ Stilt Grano flooring works completed.</li> <li>▪ Electrical Panel &amp; Cable tray fixing works completed.</li> <li>▪ Construction of Earth Pit chambers completed.</li> <li>▪ Firefighting works completed (Application for NOC submitted, Inspection scheduled on 5<sup>th</sup> Dec 2024).</li> </ul>	
	<b>WORKS ON PROGRESS</b>	<b>WORKS TO BE DONE</b>
	<ul style="list-style-type: none"> <li>▪ Lift Installation works 90% completed. ( 3 out 3 ).</li> <li>▪ Fixing of Wash basins 70% completed ( 252/360).</li> </ul>	<ul style="list-style-type: none"> <li>▪ Internal Painting 2<sup>nd</sup> Coating</li> <li>▪ Fixing of Plumbing CP fittings.</li> <li>▪ Lift Commissioning works.</li> <li>▪ Fixing of EB meters.</li> <li>▪ Fixing of Electrical fittings in common areas.</li> <li>▪ Installation of lightening arrester.</li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

BLOCK	STATUS AS ON 30 <sup>th</sup> NOVEMBER-2024
C2 BLOCK	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (4 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank               <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (3 out of 3)</li> <li>(b) Wall Concrete (3 out of 3)</li> <li>(c) Top Cover slab (3 out of 3 )</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Fixing of Internal Plumbing Line               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ External Plastering in all sides.</li> <li>▪ Fixing of Vertical Plumbing Line in Shafts               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles.</li> <li>▪ Laying Of Floor Tiles               <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom</li> <li>b) Vitrified Tiles in Halls &amp; Bedrooms.</li> <li>c) Vitrified Tiles in Corridor.</li> </ul> </li> <li>▪ Fixing of UPVC Windows.</li> <li>▪ Fixing of UPVC French Door (without Mosquito mesh shutter)</li> <li>▪ Fixing of Door Shutters 100% completed (1080/1080).</li> <li>▪ Kitchen Finishing Works               <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados.</li> <li>b) Laying of Granite Countertop.</li> <li>c) Fixing of S.S Sink.</li> </ul> </li> <li>▪ Water Proofing Works.               <ul style="list-style-type: none"> <li>a) Terrace floor Water proofing.</li> <li>b) Over Head Water Tank.</li> </ul> </li> <li>▪ Laying of Green marble for Staircase 100% completed.</li> <li>▪ Electrical wire pulling work 100% completed (120/120).</li> <li>▪ Fixing of Modular Switches &amp; Sockets 100% completed. (120/120)</li> </ul> </li> </ul>

**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

C2 BLOCK	<ul style="list-style-type: none"> <li>▪ Fixing of M.S Window Safety Grills 100% completed.</li> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails.</li> <li>▪ Bathroom false ceiling work 100% completed (360 / 360).</li> <li>▪ Fixing of IWC 100% completed (120/120)</li> <li>▪ Fixing of EWC 100% completed (240/240)</li> <li>▪ Lift Cladding works 4 out of 4 100% completed.</li> <li>▪ Internal Painting                             <ul style="list-style-type: none"> <li>a) 1<sup>st</sup> Coat – 100% completed (120/120)</li> </ul> </li> <li>▪ Over Head Tank Ring Main Connection works completed.</li> <li>▪ Fixing of Door Hardware Fittings completed.</li> <li>▪ Fixing of Main Door Lock completed.</li> <li>▪ Plumbing shaft top covering completed.</li> <li>▪ Stilt Grano flooring works completed.</li> <li>▪ Electrical Panel &amp; Cable tray fixing works completed.</li> <li>▪ Construction of Earth Pit chambers completed.</li> <li>▪ Firefighting works completed (Application for NOC submitted, Inspection scheduled on 5<sup>th</sup> Dec 2024).</li> </ul>	
	<b>WORKS ON PROGRESS</b>	<b>WORKS TO BE DONE</b>
	<ul style="list-style-type: none"> <li>▪ Lift Installation works 90% completed. ( 3 out 3 ).</li> </ul>	<ul style="list-style-type: none"> <li>▪ Fixing of Wash basins.</li> <li>▪ Internal Painting 2<sup>nd</sup> Coating</li> <li>▪ Fixing of Plumbing CP fittings.</li> <li>▪ Lift Commissioning works.</li> <li>▪ Fixing of EB meters.</li> <li>▪ Fixing of Electrical fittings in common areas.</li> <li>▪ Installation of lightening arrester.</li> </ul>
<b>BLOCK</b>	<b>STATUS AS ON 30<sup>th</sup> NOVEMBER-2024</b>	
C3 BLOCK	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (4 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank                                     <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (3 out of 3)</li> <li>(b) Wall Concrete (3 out of 3)</li> <li>(c) Top Cover slab (3 out of 3 )</li> </ul> </li> </ul> </li> </ul>	



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

---

C3 BLOCK	<ul style="list-style-type: none"><li>▪ Block work upto Tenth floor &amp; Parapet wall.</li><li>▪ Ceiling Plastering upto Tenth floor.</li><li>▪ Wall plastering upto Tenth floor.</li><li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li><li>▪ 2<sup>nd</sup> Coat Wall Putty upto Tenth floor.</li><li>▪ Fixing of Internal Plumbing Line<ul style="list-style-type: none"><li>a) Water supply pipe Lines (CPVC).</li><li>b) Sanitary Lines (PVC)</li></ul></li><li>▪ External Plastering in all sides.</li><li>▪ Fixing of Vertical Plumbing Line in Shafts<ul style="list-style-type: none"><li>a) Water supply pipe Lines (G.I).</li><li>b) Sanitary Lines (PVC).</li></ul></li><li>▪ Fixing of Bathroom Wall Tiles.</li><li>▪ Laying Of Floor Tiles<ul style="list-style-type: none"><li>a) Ceramic Tiles in Bathroom</li><li>b) Vitrified Tiles in Halls &amp; Bedrooms.</li><li>c) Vitrified Tiles in Corridor.</li></ul></li><li>▪ Fixing of UPVC Windows.</li><li>▪ Fixing of UPVC French Door (without Mosquito mesh shutter)</li><li>▪ Fixing of Door Shutters 100% completed (900/900).</li><li>▪ Kitchen Finishing Works<ul style="list-style-type: none"><li>a) Fixing of Wall Dados.</li><li>b) Laying of Granite Countertop.</li><li>c) Fixing of S.S Sink.</li></ul></li><li>▪ Water Proofing Works.<ul style="list-style-type: none"><li>a) Terrace floor Water proofing.</li><li>b) Over Head Water Tank.</li></ul></li><li>▪ Laying of Green marble for Staircase 100% completed.</li><li>▪ Electrical wire pulling work 100% completed (100/100).</li><li>▪ Fixing of Modular Switches &amp; Sockets 100% completed. (100/100)</li><li>▪ Fixing of M.S Window Safety Grills 100% completed.</li><li>▪ Fixing of Balcony Handrail.</li><li>▪ Fixing of Staircase Hand Rails.</li><li>▪ Bathroom false ceiling work 100% completed (300 / 300).</li><li>▪ Fixing of IWC 100% completed (100/100)</li><li>▪ Lift Cladding works 4 out of 4 100% completed.</li><li>▪ Internal Painting<ul style="list-style-type: none"><li>a) 1<sup>st</sup> Coat – 100% completed (120/120)</li></ul></li></ul>
----------	--



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

C3 BLOCK	<ul style="list-style-type: none"> <li>▪ Over Head Tank Ring Main Connection works completed.</li> <li>▪ Fixing of Door Hardware Fittings completed.</li> <li>▪ Fixing of Main Door Lock completed.</li> <li>▪ Plumbing shaft top covering completed.</li> <li>▪ Stilt Grano flooring works completed.</li> <li>▪ Electrical Panel &amp; Cable tray fixing works completed.</li> <li>▪ Construction of Earth Pit chambers completed.</li> <li>▪ Firefighting works completed (Application for NOC submitted, Inspection scheduled on 5<sup>th</sup> Dec 2024).</li> </ul>	
	<b>WORKS ON PROGRESS</b>	<b>WORKS TO BE DONE</b>
	<ul style="list-style-type: none"> <li>▪ Lift Installation works               <ul style="list-style-type: none"> <li>a) 3 Lifts - 90% completed.</li> <li>b) 4<sup>th</sup> Lift - 85% completed.</li> </ul> </li> <li>▪ Fixing of EWC 90% completed (180/200)</li> </ul>	<ul style="list-style-type: none"> <li>▪ Fixing of Wash basins.</li> <li>▪ Internal Painting 2<sup>nd</sup> Coating</li> <li>▪ Fixing of Plumbing CP fittings.</li> <li>▪ Lift Commissioning works.</li> <li>▪ Fixing of EB meters.</li> <li>▪ Fixing of Electrical fittings in common areas.</li> <li>▪ Installation of lightening arrester.</li> </ul>
<b>BLOCK</b>	<b>STATUS AS ON 30<sup>th</sup> NOVEMBER-2024</b>	
D1 BLOCK	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (4 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank                   <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (3 out of 3)</li> <li>(b) Wall Concrete (3 out of 3)</li> <li>(c) Top Cover slab (3 out of 3 )</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Fixing of Internal Plumbing Line                   <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ External Plastering in all sides.</li> <li>▪ Fixing of Vertical Plumbing Line in Shafts</li> </ul> </li> </ul>	



# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

D1 BLOCK	<ul style="list-style-type: none"><li>a) Water supply pipe Lines (G.I).</li><li>b) Sanitary Lines (PVC).</li><li>▪ Fixing of Bathroom Wall Tiles.</li><li>▪ Laying Of Floor Tiles<ul style="list-style-type: none"><li>a) Ceramic Tiles in Bathroom</li><li>b) Vitrified Tiles in Halls &amp; Bedrooms.</li><li>c) Vitrified Tiles in Corridor.</li></ul></li><li>▪ Fixing of UPVC Windows.</li><li>▪ Fixing of UPVC French Door (without Mosquito mesh shutter)</li><li>▪ Fixing of Door Shutters 100% completed (900/900).</li><li>▪ Kitchen Finishing Works<ul style="list-style-type: none"><li>a) Fixing of Wall Dados.</li><li>b) Laying of Granite Countertop.</li><li>c) Fixing of S.S Sink.</li></ul></li><li>▪ Water Proofing Works.<ul style="list-style-type: none"><li>a) Terrace floor Water proofing.</li><li>b) Over Head Water Tank.</li></ul></li><li>▪ Laying of Green marble for Staircase 100% completed.</li><li>▪ Electrical wire pulling work 100% completed (80/80).</li><li>▪ Fixing of Modular Switches &amp; Sockets 100% completed. (80/80)</li><li>▪ Fixing of M.S Window Safety Grills 100% completed.</li><li>▪ Fixing of Balcony Handrail.</li><li>▪ Fixing of Staircase Hand Rails.</li><li>▪ Bathroom false ceiling work 100% completed (320 / 320).</li><li>▪ Fixing of IWC 100% completed (80/800)</li><li>▪ Fixing of EWC 100% completed (240/240)</li><li>▪ Lift Cladding works 4 out of 4 100% completed.</li><li>▪ Internal Painting<ul style="list-style-type: none"><li>b) 1<sup>st</sup> Coat – 100% completed (80/80)</li></ul></li><li>▪ Over Head Tank Ring Main Connection works completed.</li><li>▪ Fixing of Door Hardware Fittings completed.</li><li>▪ Fixing of Main Door Lock completed.</li><li>▪ Stilt flooring works completed.</li><li>▪ Electrical Panel &amp; Cable tray fixing works completed.</li><li>▪ Construction of Earth Pit chambers completed.</li><li>▪ Firefighting works completed. ( NOC from Fire Department obtained)</li></ul>
----------	--

**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

	WORKS ON PROGRESS	WORKS TO BE DONE
	<ul style="list-style-type: none"> <li>▪ Lift Installation works               <ul style="list-style-type: none"> <li>a) 3 Lifts - 90% completed.</li> <li>b) 4<sup>th</sup> Lift - 85% completed.</li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>▪ Fixing of Wash basins.</li> <li>▪ Internal Painting 2<sup>nd</sup> Coating</li> <li>▪ Fixing of Plumbing CP fittings.</li> <li>▪ Lift Commissioning works.</li> <li>▪ Fixing of EB meters.</li> <li>▪ Fixing of Electrical fittings in common areas.</li> <li>▪ Installation of lightening arrester.</li> </ul>
BLOCK	STATUS AS ON 30 <sup>th</sup> NOVEMBER-2024	
D2 BLOCK	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ <b>Terrace floor level</b> slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (4 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank               <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (3 out of 3)</li> <li>(b) Wall Concrete (3 out of 3)</li> <li>(c) Top Cover slab (3 out of 3 )</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Fixing of Internal Plumbing Line               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ External Plastering in all sides.</li> <li>▪ Fixing of Vertical Plumbing Line in Shafts               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles.</li> <li>▪ Laying Of Floor Tiles               <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom</li> <li>b) Vitrified Tiles in Halls &amp; Bedrooms.</li> <li>c) Vitrified Tiles in Corridor.</li> </ul> </li> <li>▪ Fixing of UPVC Windows.</li> <li>▪ Fixing of UPVC French Door (without Mosquito mesh shutter)</li> <li>▪ Fixing of Door Shutters 100% completed (900/900).</li> </ul> </li> </ul>	





# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

D2 BLOCK	<ul style="list-style-type: none"> <li>▪ Kitchen Finishing Works               <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados.</li> <li>b) Laying of Granite Countertop.</li> <li>c) Fixing of S.S Sink.</li> </ul> </li> <li>▪ Water Proofing Works.               <ul style="list-style-type: none"> <li>a) Terrace floor Water proofing.</li> <li>b) Over Head Water Tank.</li> </ul> </li> <li>▪ Laying of Green marble for Staircase 100% completed.</li> <li>▪ Electrical wire pulling work 100% completed (80/80).</li> <li>▪ Fixing of Modular Switches &amp; Sockets 100% completed. (80/80)</li> <li>▪ Fixing of M.S Window Safety Grills 100% completed.</li> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails.</li> <li>▪ Bathroom false ceiling work 100% completed (320 / 320).</li> <li>▪ Fixing of IWC 100% completed (80/800)</li> <li>▪ Fixing of EWC 100% completed (240/240)</li> <li>▪ Fixing of Wash basins 100% completed (240/240)</li> <li>▪ Lift Erection works 4 out of 4 completed.</li> <li>▪ Lift Cladding works 4 out of 4 100% completed.</li> <li>▪ Internal Painting               <ul style="list-style-type: none"> <li>a) 1<sup>st</sup> Coat – 100% completed (80/80)</li> </ul> </li> <li>▪ Over Head Tank Ring Main Connection works completed.</li> <li>▪ Fixing of Door Hardware Fittings completed.</li> <li>▪ Fixing of Main Door Lock completed.</li> <li>▪ Stilt flooring works completed.</li> <li>▪ Lift Slow speed commissioning 4 out of 4 completed.</li> <li>▪ Electrical Panel &amp; Cable tray fixing works completed.</li> <li>▪ Construction of Earth Pit chambers completed.</li> <li>▪ Firefighting works completed. ( NOC from Fire Department obtained).</li> </ul>	
	<b>WORKS ON PROGRESS</b>	<b>WORKS TO BE DONE</b>
	<ul style="list-style-type: none"> <li>▪ Final snag list checking &amp; cleaning.</li> <li>▪ Cabling work for lightening arrester on progress.</li> </ul>	<ul style="list-style-type: none"> <li>▪ Internal Painting 2<sup>nd</sup> Coating</li> <li>▪ Fixing of Plumbing CP fittings.</li> <li>▪ Lift Commissioning works (High Speed).</li> <li>▪ Fixing of EB meters.</li> <li>▪ Fixing of Electrical fittings in common areas.</li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

BLOCK	STATUS AS ON 30 <sup>th</sup> NOVEMBER-2024
D3 BLOCK	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (4 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank                             <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (3 out of 3)</li> <li>(b) Wall Concrete (3 out of 3)</li> <li>(c) Top Cover slab (3 out of 3 )</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Fixing of Internal Plumbing Line                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ External Plastering in all sides.</li> <li>▪ Fixing of Vertical Plumbing Line in Shafts                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles.</li> <li>▪ Laying Of Floor Tiles                             <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom</li> <li>b) Vitrified Tiles in Halls &amp; Bedrooms.</li> <li>c) Vitrified Tiles in Corridor.</li> </ul> </li> <li>▪ Fixing of UPVC Windows.</li> <li>▪ Fixing of UPVC French Door (without Mosquito mesh shutter)</li> <li>▪ Fixing of Door Shutters 100% completed (900/900).</li> <li>▪ Kitchen Finishing Works                             <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados.</li> <li>b) Laying of Granite Countertop.</li> <li>c) Fixing of S.S Sink.</li> </ul> </li> <li>▪ Water Proofing Works.                             <ul style="list-style-type: none"> <li>a) Terrace floor Water proofing.</li> <li>b) Over Head Water Tank.</li> </ul> </li> <li>▪ Laying of Green marble for Staircase 100% completed.</li> <li>▪ Electrical wire pulling work 100% completed (80/80).</li> <li>▪ Fixing of Modular Switches &amp; Sockets 100% completed. (80/80)</li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

D3 BLOCK	<ul style="list-style-type: none"> <li>▪ Fixing of M.S Window Safety Grills 100% completed.</li> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails.</li> <li>▪ Bathroom false ceiling work 100% completed (320 / 320).</li> <li>▪ Fixing of IWC 100% completed (80/800)</li> <li>▪ Fixing of EWC 100% completed (240/240)</li> <li>▪ Lift Cladding works 4 out of 4 100% completed.</li> <li>▪ Internal Painting               <ul style="list-style-type: none"> <li>a) 1<sup>st</sup> Coat – 100% completed (80/80)</li> </ul> </li> <li>▪ Over Head Tank Ring Main Connection works completed.</li> <li>▪ Fixing of Door Hardware Fittings completed.</li> <li>▪ Fixing of Main Door Lock completed.</li> <li>▪ Stilt flooring works completed.</li> <li>▪ Electrical Panel &amp; Cable tray fixing works completed.</li> <li>▪ Construction of Earth Pit chambers completed.</li> <li>▪ Firefighting works completed. ( NOC from Fire Department obtained)</li> </ul>	
	<b>WORKS ON PROGRESS</b>	<b>WORKS TO BE DONE</b>
	<ul style="list-style-type: none"> <li>▪ Lift Installation works               <ul style="list-style-type: none"> <li>a) 3 Lifts - 90% completed.</li> <li>b) 4<sup>th</sup> Lift - 85% completed.</li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>▪ Fixing of Wash basins.</li> <li>▪ Internal Painting 2<sup>nd</sup> Coating</li> <li>▪ Fixing of Plumbing CP fittings.</li> <li>▪ Lift Commissioning works.</li> <li>▪ Fixing of EB meters.</li> <li>▪ Fixing of Electrical fittings in common areas.</li> <li>▪ Installation of lightening arrester.</li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

BLOCK	STATUS AS ON 30 <sup>th</sup> NOVEMBER-2024
COMMUNITY HALL	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (2 out of 2) - Slab Concrete.</li> <li>▪ Over Head Water Tank                             <ul style="list-style-type: none"> <li>(a) Base Slab Concrete</li> <li>(b) Tank Wall Concrete</li> <li>(c) Top Cover slab Concrete.</li> </ul> </li> <li>▪ Block work upto Fourth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Fourth floor.</li> <li>▪ Wall plastering upto Fourth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Fourth floor.</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Fourth floor.</li> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails</li> <li>▪ Fixing of Internal Plumbing Line                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ Fixing of Vertical Plumbing Line in Shafts                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles.</li> <li>▪ Laying Of Floor Tiles                             <ul style="list-style-type: none"> <li>a) Vitrified Floor Tiles in Main Hall &amp; other rooms</li> <li>b) Ceramic Floor Tiles in Bathrooms.</li> <li>c) Kota Stone in Staircase &amp; Lobby</li> </ul> </li> <li>▪ Fixing of UPVC Windows.</li> <li>▪ Fixing of Wooden flush Door for rooms.</li> <li>▪ Fixing of Fire Safety Door for Hall Main Entrance</li> <li>▪ External Plastering in all sides.</li> <li>▪ Water Proofing Works.                             <ul style="list-style-type: none"> <li>a) Terrace floor Water proofing.</li> <li>b) Over Head Water Tank.</li> </ul> </li> <li>▪ Lift Installation works 2 out 2 100% completed.</li> <li>▪ Lift Cladding works 2 out of 2 – 100% completed.</li> <li>▪ Application of Exterior Wall Primer.-100% completed.</li> <li>▪ External Damp proof elasto painting completed.</li> <li>▪ Firefighting works all completed. ( NOC from Fire Department obtained)</li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

	<b>WORKS ON PROGRESS</b>	<b>WORKS TO BE DONE</b>
COMMUNITY HALL	<ul style="list-style-type: none"> <li>▪ Lift commissioning works.               <ul style="list-style-type: none"> <li>a) Lift 1 - High Speed completed.</li> <li>b) Lift 2 - Slow Speed completed</li> </ul> </li> <li>▪ External painting final coat on progress.</li> </ul>	<ul style="list-style-type: none"> <li>▪ Fixing of Wash basins &amp; urinals</li> <li>▪ Internal Painting 2<sup>nd</sup> Coating.</li> <li>▪ Fixing of Plumbing CP fittings.</li> <li>▪ Lift -2 High speed Commissioning.</li> <li>▪ Fixing of EB meters.</li> <li>▪ Fixing of Electrical fittings in Hall, rooms &amp; common areas.</li> </ul>

	<b>STATUS AS ON 30<sup>th</sup> NOVEMBER-2024</b>
EXTERNAL DEVELOPMENT WORKS	<ul style="list-style-type: none"> <li>➤ <b>Underground Sump-1 (Near B-Block)</b> <ul style="list-style-type: none"> <li>▪ All R.C.C works 100% completed.</li> <li>▪ Outer Wall Waterproof plastering – 100% completed.</li> <li>▪ Inner Wall Waterproof plastering – 100% completed.</li> <li>▪ Fixing of Ladder in Pump room completed.</li> <li>▪ Foundation for Pumps completed.</li> <li>▪ WTP Materials received.</li> </ul> </li> <li>➤ <b>Underground Sump-2 (Near D-Block)</b> <ul style="list-style-type: none"> <li>▪ All R.C.C works 100% completed.</li> <li>▪ Outer Wall Waterproof plastering – 100% completed.</li> <li>▪ Inner Wall Waterproof plastering 100% completed.</li> <li>▪ Fixing of Ladder in Pump room completed.</li> <li>▪ Fixing &amp; installation of Pumps completed.</li> <li>▪ WTP Materials received.</li> </ul> </li> <li>➤ <b>Sewage Treatment Plant-2 (Near D-Block)</b> <ul style="list-style-type: none"> <li>▪ All R.C.C works 100% completed.</li> <li>▪ STP Pump Room completed.</li> <li>▪ Outer wall Waterproof plastering 100% completed.</li> <li>▪ Inner Wall Waterproof plastering 100% completed.</li> <li>▪ Installation of STP 90% completed.</li> </ul> </li> <li>➤ <b>Sewage Treatment Plant-1 (Near C3-Block)</b> <ul style="list-style-type: none"> <li>▪ All R.C.C works 100% completed.</li> <li>▪ Pump room block work &amp; plastering completed.</li> <li>▪ Internal Waterproof plastering 60% completed.</li> <li>▪ STP components received.</li> </ul> </li> </ul>



# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

EXTERNAL DEVELOPMENT WORKS	<ul style="list-style-type: none"><li>➤ <b>Laying of External Sewer lines</b><ul style="list-style-type: none"><li>▪ Type 'D' All Blocks – 100% completed.</li><li>▪ Type 'C' All Blocks – 95% completed.</li><li>▪ Type 'A' All Blocks – 95% completed.</li><li>▪ B1 Block - 95% completed.</li><li>▪ B2 Block - 25% completed.</li></ul></li><li>➤ <b>Laying of External Water Supply lines</b><ul style="list-style-type: none"><li>▪ Type 'D' All Blocks – 95% completed.</li><li>▪ Type 'C' All Blocks – 95% completed.</li><li>▪ Type 'A' All Blocks – 95% completed.</li><li>▪ B1 Block - 50% completed.</li></ul></li><li>➤ <b>Laying of Storm Water Drainage.</b><ul style="list-style-type: none"><li>▪ Type 'D' All Blocks – 95% completed.</li><li>▪ Type 'C' All Blocks – 90% completed.</li><li>▪ Type 'A' All Blocks – 90% completed.</li><li>▪ B1 Block – Excavation 50% completed.</li><li>▪ B2 Block – Excavation 10% completed.</li></ul></li><li>➤ <b>External Electrification works.</b><ul style="list-style-type: none"><li>▪ Total 8 Nos Transformers received out of 10 Nos.</li><li>▪ Type 'D' All Blocks – Fixing of Pole structure for Transformers 100% completed. Fixing of Single poles 90% completed.</li><li>▪ Type 'A', 'B' &amp; 'C' all Blocks – Fixing of Pole structure for Transformers 100% completed. Fixing of Single poles 90% completed.</li><li>▪ Installation of Over Head Power line<ul style="list-style-type: none"><li>a) In Type - D block &amp; Community – 90% completed.</li><li>b) In Type – A, B &amp; C Blocks – 90% completed.</li></ul></li><li>▪ Foundation platform for Diesel Generators completed. Erection of DGs completed.</li></ul></li><li>➤ <b>Laying of Roads.</b><ul style="list-style-type: none"><li>▪ Formation of Sub-Grade<ul style="list-style-type: none"><li>a) Around Type D All Blocks – 100% completed.</li><li>b) Around Type C1 Block – 100% completed.</li><li>c) Around Type C2 Block – 100% completed</li><li>d) Around Type C3 Block – 90% completed</li><li>e) Around Type A1 Block – 100% completed.</li><li>f) Around Type A2 Block – 100% completed.</li><li>g) Around Community Hall – 95% completed.</li></ul></li><li>▪ Laying of Granular Sub Base (GSB)<ul style="list-style-type: none"><li>a) Around Type D All Blocks – 100% completed.</li><li>b) Around Type C1 Block – 85% completed.</li></ul></li></ul></li></ul>
----------------------------------	--

# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

	<ul style="list-style-type: none"><li>c) Around Type C2 Block – 90% completed</li><li>d) Around Type C3 Block – 65% completed</li><li>e) Around Type A1 Block – 85% completed.</li><li>f) Around Type A2 Block – 95% completed.</li> <li>▪ Laying of Wet Mix Macadam (WMM)<ul style="list-style-type: none"><li>a) Around Type D All Blocks – 80% completed.</li></ul></li></ul>
--	--

### PHOTOGRAPHS OF WORK PROGRESS AS ON 30<sup>th</sup> NOVEMBER 2024

**Community Hall:** External Damp proof Elasto Painting completed.



# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Block A1:** Conducting for Lightening arresstor & PCC around blocks on progress.



**Block A2 :** Lift installation works & Main Door Lock fixing works on progress.





# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Block B1:** Stilt floor Grano flooring completed.



**Block B2 :** Terrace Waterproofing works on progress. Vitrified floor tiling work on progress.



# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Block C1:** Fixing of Wash basins on progress. Erection of D.G Set on progress.



**Block C2:** Erection of D.G Set on progress.



# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Block C3:** Laying of PCC in Stilts on progress. Erection of D.G Set on progress.



**Block D1:** Fixing of Wash basins in bathrooms on progress.



# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Block D2:** Cabling work for Lightning arrestor on progress.



**Block D3:** Laying of Granular Sub-base (GSB) around the block on progress.



# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Sewage Treatment Plant 1 (Near C Block). STP Pump room external plastering work on progress. STP components received at Site.**




**Under Ground Sump 1 ( Opp to B1 Block). Water Treatment Plant Components received at Site.**



# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

**Under Ground Sump 2 (Near D1 Block). Water Treatment Plant Components received at Site.**

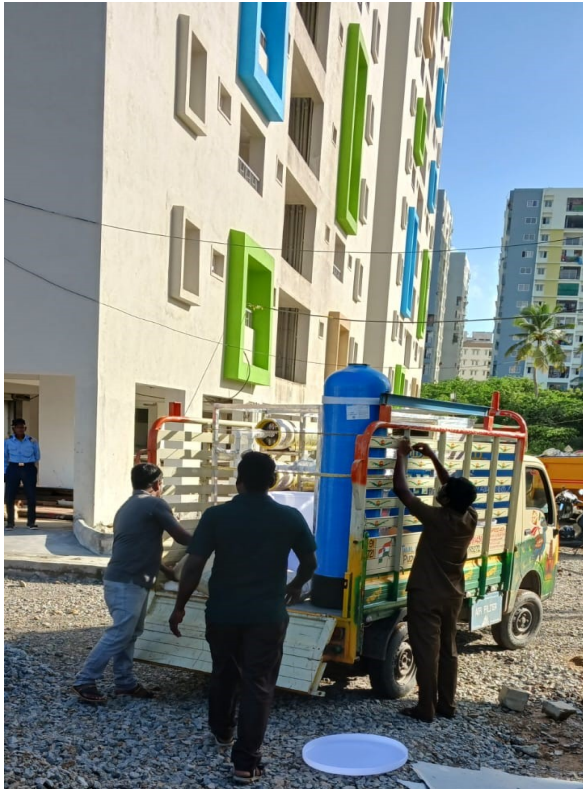

**External Electrification Works :** Erection of Diesel Generators completed. Preparation for fixing of Pillar box on progress



# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Road Works :** Laying of Wet Mix Macadam around D1, D2 & D3 & Rolling on progress.



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

**QUALITY CONTROL**

**DURING CONSTRUCTION FOLLOWING QUALITY CONTROL TESTS CONDUCTED AT SITE:**

Sl.No.	Materials	Source from	Test Done	Result
1	M-Sand	Arcot (T.K), Ranipet (Dist) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2.	P- Sand	Uthiramerur, Kanchipuram (DT) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2	Coarse Aggregate (20mm)	Sriperambathur, Kanchipuram (Dt), Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
3	Coarse Aggregate (12mm)	Sriperambathur, Kanchipuram (Dt) Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
4	Cement	Third party testing is being done.		
5	Steel	Third party testing is being done.		
6	Pile Integrity	Third party testing is being done.		
7	Soil Compaction	Third party testing is being done.		
8	RCC cubes are being tested and Register is being maintained.			
9	Slump test conducted at site to insure workability of concrete.			
