

**CGEWHO – CHENNAI PHASE-III
PROJECT**



MONTHLY PROGRESS REPORT

STATUS AS ON : 31.01.2024

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

31.01.2024

BLOCK	STATUS AS ON 31 st JANUARY-2024	
A1 BLOCK	<p>◆ 100% Completed Works</p> <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete 2 out of 2 (b) Tank Wall Concrete 2 out of 2 (c) Top Cover slab Concrete 2 out of 2 ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor ▪ Electrical Conducting works in Tenth floor. ▪ Fixing of Water supply pipe Lines (CPVC) –100% completed (200 / 200). ▪ Fixing of Sanitary Lines (PVC) – 100% completed (200/ 200). ▪ Fixing of Vertical Plumbing Lines in Shaft 100% completed. (200/200). ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank (2 / 2). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31 st JANUARY-2024
	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External Plastering 95% completed in all sides. ▪ Fixing of Vertical Plumbing Lines in Shaft 90% completed. (180/200). ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank (1 / 2). <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Fixing of Staircase Handrail 85% completed. ▪ Fixing of Bathroom Wall Tiles 33% completed (66/200). ▪ Fixing of Toilet Wall Tiles 12% completed (24/200). ▪ Laying Of Floor Tiles 	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External Plastering 95% completed in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace Water Proofing 10% completed. <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Fixing of Staircase Handrail 90% completed. ▪ Fixing of Bathroom Wall Tiles 71% completed (143/200). ▪ Fixing of Toilet Wall Tiles 71% completed (143/200). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathrooms 71% completed (143/200)



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> a) Ceramic Tiles in Bathrooms 33% completed (66/200) b) Ceramic Tiles in Toilets 12% completed (24/200) ▪ Vitrified Tiles in Halls & Bedrooms 25% completed (50/200). ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 15% completed (30/200). b) Laying of Granite Countertop 48% completed (96/200). ▪ Fixing of Door Shutters on progress (42/1200). ▪ Lift Materials 4 out of 4 received. Shaft work on progress. ◆ Model Flat Finishing works 90% completed. 	<ul style="list-style-type: none"> b) Ceramic Tiles in Toilets 71% completed (143/200) ▪ Vitrified Tiles in Halls & Bedrooms 71% completed (143/200). ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 63% completed (126/200). b) Laying of Granite Countertop 63% completed (126/200). c) Fixing of S.S Sink 63% completed (126/200) ▪ Fixing of Door Shutters 40% completed (480/1200). ▪ Fixing of UPVC Windows 20% completed (175 /800) ▪ Lift Materials 4 out of 4 received. Shaft work on progress. ◆ Model Flat Finishing works 90% completed.
BLOCK	STATUS AS ON 31st JANUARY-2024	
A2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete 2 out of 2 (b) Tank Wall Concrete 2 out of 2 (c) Top Cover slab Concrete 2 out of 2 ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ Electrical Conducting works upto Tenth floor. ▪ Fixing of Water supply pipe Lines (CPVC) –100% completed (200 / 200). ▪ Fixing of Sanitary Lines (PVC) – 100% completed (200/ 200). ▪ Fixing of Vertical Plumbing Lines in Shaft 100% completed (200/200). 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31 st JANUARY-2024
<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. ▪ Fixing of Sanitary Lines (PVC) – 95% completed (190/ 200). <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Fixing of Vertical Plumbing Lines in Shaft 60% completed (120/200). ▪ Fixing of Bathroom Wall Tiles started (6/200). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom started (6/200) ▪ Vitrified Tiles in Halls & Bedrooms started (3/200). ▪ Lift Materials 4 out of 4 received. Shaft work on progress. 	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Fixing of Bathroom Wall Tiles 20% completed (40/200). ▪ Fixing of Toilet Wall Tiles 20% completed (40/200). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 20% completed (40/200) b) Ceramic Tiles in Toilet 20% completed (40/200) ▪ Vitrified Tiles in Halls & Bedrooms 20% completed. (40/200). ▪ Fixing of Door Shutters 20% completed (240/1200). ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 20% completed (40/200). b) Laying of Granite Countertop 20% completed (40/200). c) Fixing of S.S Sink 20% completed (40/200) ▪ Water Proofing Work <ul style="list-style-type: none"> a) Over Head Water Tank 50% completed (1 / 2) b) Terrace Water proofing 10% completed. ▪ Lift Materials 4 out of 4 received. Shaft work on progress.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 31 st JANUARY-2024
B1 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 3) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom b) Vitrified Tiles in Halls & Bedrooms. c) Vitrified Tiles in Corridor. ▪ Fixing of UPVC Windows. ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados. b) Laying of Granite Countertop. c) Fixing of S.S Sink. ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. b) Over Head Water Tank.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BI BLOCK	<ul style="list-style-type: none"> ▪ Fixing of Door Shutters 100% completed (840/840). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st JANUARY-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 3 out 3. ▪ Lift Cladding works 3 out of 3. ▪ Fixing of Door Shutters 97% completed (820/840). ▪ Laying of Green marble for Staircase. ▪ Application of Exterior Wall Primer ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of M.S Window Safety Grills 60% completed. ▪ Electrical wire pulling work 51% completed (62/120). ▪ Firefighting works 50% completed. ● Model Flat Finishing works 95% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 3 out 3. ▪ Lift Cladding works 3 out of 3. ▪ Laying of Green marble for Staircase. ▪ Application of Exterior Wall Primer ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of M.S Window Safety Grills 75% completed. ▪ Electrical wire pulling work 93% completed (112/120). ▪ Firefighting works 60% completed. ● Model Flat Finishing works 95% completed.
BLOCK	STATUS AS ON 31st JANUARY-2024	
B2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Upto Ninth floor level slab R.C.C ▪ Block work upto Seventh floor. ▪ Ceiling plastering upto Sixth floor. ▪ Wall plastering upto Sixth floor. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st JANUARY-2024
	<ul style="list-style-type: none"> ◆ Works On Progress <ul style="list-style-type: none"> ▪ Eighth floor Columns Concrete 90% completed. ▪ Ninth floor level slab – 1st Half R.C.C completed. ▪ Block work <ul style="list-style-type: none"> a) In Sixth floor 85% completed. b) In Seventh floor 40% completed. ▪ Ceiling Plastering <ul style="list-style-type: none"> a) In Sixth floor 60% completed. ▪ Wall Plastering <ul style="list-style-type: none"> a) In Sixth floor 55% completed. 	<ul style="list-style-type: none"> ◆ Works On Progress <ul style="list-style-type: none"> ▪ Ninth floor Columns Concrete 50% completed. ▪ Shuttering works for 1st Half of 10th Floor level slab 10% completed. ▪ Block work <ul style="list-style-type: none"> a) In Eighth floor 40% completed. ▪ Ceiling Plastering <ul style="list-style-type: none"> a) In Seventh floor 50% completed. ▪ Wall Plastering <ul style="list-style-type: none"> a) In Seventh floor 50% completed



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

		▪ Electrical conducting works 30% completed.
BLOCK	STATUS AS ON 31st JANUARY-2024	
C1 BLOCK	<p>◆ 100% Completed Works</p> <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Internal Plumbing Line. <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom b) Vitrified Tiles in Halls & Bedrooms c) Vitrified Tiles in Corridor 100% completed. ▪ Fixing of UPVC Windows. ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed. ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank b) Terrace floor Water proofing. ▪ Laying of Green marble for Staircase. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados. b) Laying of Granite Countertop. c) Fixing of S.S Sink. ▪ Lift Cladding works 4 out of 4. 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Fixing of Door Shutters 100% completed (1080 / 1080) 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st JANUARY-2024
C1 BLOCK	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Staircase Hand Rails 3 out of 3 ▪ Lift Installation works 4 out 4. ▪ Application of Exterior Wall Primer Fixing of Door Shutters 97% completed (1050 / 1080) ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of M.S Window Safety Grills 50% completed. ▪ Electrical wire pulling work 46% completed (56/120). ▪ Fire Fighting works 30% completed. ● Model Flat Finishing works 95% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Staircase Hand Rails 3 out of 3 ▪ Lift Installation works 4 out 4. ▪ Application of Exterior Wall Primer. ▪ Electrical wire pulling work 91% completed (110/120). ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of M.S Window Safety Grills 70% completed. ▪ Fire Fighting works 40% completed. ● Model Flat Finishing works 95% completed.
BLOCK	STATUS AS ON 31st JANUARY-2024	
C2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (2 out of 3) (b) Wall Concrete (2 out of 3) (c) Top Cover slab (2 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

C2 BLOCK	<ul style="list-style-type: none"> ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 1 out of 3 ▪ Fixing of Bathroom Wall Tiles completed. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom completed. b) Vitrified Tiles in Halls & Bedrooms completed. c) Vitrified Tiles in Corridor completed. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed. (120 / 120) b) Laying of Granite Countertop 100% completed. (120 / 120). c) Fixing of S.S Sink 100% completed. (120 / 120). ▪ Fixing of UPVC Window 100% completed. (600 / 600) ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed. (240 /240) ▪ Fixing of Main Door & Internal Shutters 100% completed (1080 / 1080) 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st JANUARY-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Application of Exterior Wall Primer ▪ Fixing of Main Door & Internal Shutters 94% completed (1023 / 1080) ▪ Lift Installation works 2 out 4 - 90% completed. ▪ Fixing of UPVC Window 98% completed. (588 / 600) ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 95% completed. (228 /240) ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works – <ul style="list-style-type: none"> 3rd Lift - 75% completed. 4th Lift – 45% completed. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 50% completed. b) Over Head Water Tank 2 out 3 work in progress. ▪ Laying of Green marble for Staircase 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Application of Exterior Wall Primer ▪ Lift Installation works 2 out 4 - 90% completed. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 95% completed. ▪ Laying of Green marble for Staircase 90% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works – <ul style="list-style-type: none"> 3rd Lift - 80% completed. 4th Lift – 80% completed. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 2 out 3 work in progress. ▪ Lift Cladding work 75% completed. ▪ Electrical wire pulling 30% completed (36 /120). ▪ Fire Fighting works 30% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<p>85% completed.</p> <ul style="list-style-type: none"> ▪ Lift Cladding work 70% completed. ▪ Electrical wire pulling started. ▪ Fire Fighting works 15% completed. 	
BLOCK	STATUS AS ON 31st JANUARY-2024	
C3 BLOCK	<p>◆ 100% Completed Works</p> <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (2 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank (1 / 2) completed. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed (100/100) b) Laying of Granite Countertop 100% completed. (100/100). c) Fixing of S.S Sink 100% completed. (100/ 100). ▪ Fixing of Bathroom Wall Tiles 100% completed. (300 /300) ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 100% completed. (300 /300) b) Vitrified Tiles in Halls & Bedrooms 100% completed. (100 / 100) 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st JANUARY-2024
	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails. 	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

C3 BLOCK	<ul style="list-style-type: none"> ▪ Application of Exterior Wall Primer ▪ Fixing of Bathroom Wall Tiles 93% completed. (280 /300) ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 93% completed. (280 /300) b) Vitrified Tiles in Halls & Bedrooms 92% completed. (92 / 100) ◆ Works On Progress <ul style="list-style-type: none"> ▪ 2nd Coat Wall Putty 80% completed. (80 /100). ▪ Fixing of UPVC Window 18% Completed.(91 / 500) ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 35% completed (70 / 200) ▪ Fixing of Main Door & Internal Shutters 10% completed (91 / 900) ▪ Lift Installation works – <ul style="list-style-type: none"> 2 Lifts - 80% completed. 2 Lifts - works now started. ▪ Lift Cladding work 20% completed. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 40% completed. ▪ Laying of Green marble for Staircase 50% completed. 	<ul style="list-style-type: none"> ▪ Application of Exterior Wall Primer ▪ 2nd Coat Wall Putty 90% completed. (90 /100). ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of UPVC Window 64% Completed. (321 / 500). ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 53% completed (107 / 200). ▪ Fixing of Main Door & Internal Shutters 16% completed (150 / 900). ▪ Lift Installation works – <ul style="list-style-type: none"> 2 Lifts - 80% completed. 3rd Lift – 10% completed. 4th Lift – Work on progress ▪ Lift Cladding work 30% completed. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 60% completed. ▪ Laying of Green marble for Staircase 70% completed.
BLOCK	STATUS AS ON 31st JANUARY-2024	
D1 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

D1 BLOCK	<ul style="list-style-type: none"> ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 3 out of 3 b) Terrace floor Water proofing 100% completed. ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles 100% completed. (320 / 320). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 100% completed. (320 / 320) b) Vitrified Tiles in Halls & Bedrooms 100% completed. (80 / 80). ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed. (80 / 80) b) Laying of Granite Countertop 100% completed. (80 / 80). c) Fixing of S.S Sink 100% completed. (80 / 80). ▪ Fixing of Main Door & Internal Shutters 100% completed (880 / 880) 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st JANUARY-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. ▪ Application of External Wall Primer-1st Coat ▪ Vitrified Tiles in Halls & Bedrooms 96% completed. (77 / 80). ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 90% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ 2nd Coat Wall Putty 50% completed. (40 / 80). ▪ Fixing of UPVC Windows 72% completed. (291 / 400). ▪ Fixing of UPVC French Door 21% completed.(without Mosquito mesh shutter) 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. ▪ Application of External Wall Primer-1st Coat ▪ Fixing of UPVC Windows 90% completed. (360 / 400). ◆ Works On Progress <ul style="list-style-type: none"> ▪ 2nd Coat Wall Putty 75% completed. (60 / 80). ▪ Fixing of UPVC French Door 78% completed.(without Mosquito mesh shutter) (125 / 160) ▪ Application of Exterior Wall Primer 75% completed ▪ Lift Installation works



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<p>(35 / 160)</p> <ul style="list-style-type: none"> ▪ Fixing of Main Door & Internal Shutters 79% completed (702 / 880) ▪ Application of Exterior Wall Primer 75% completed ▪ Lift Installation works 2 out 4 - 80% completed. Other 2 Lifts work now started. 	<ul style="list-style-type: none"> a) 2 out 4 - 80% completed. b) 3rd lift - 20% completed. c) 4th lift - work on progress. ▪ Electrical Wire pulling works started (6/ 80).
BLOCK	STATUS AS ON 31st JANUARY-2024	
D2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 3) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom b) Vitrified Tiles in Halls & Bedrooms. c) Vitrified Tiles in Corridor. ▪ Fixing of UPVC Windows. 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

D2 BLOCK	<ul style="list-style-type: none"> ▪ Fixing of Main Door & Internal Shutters. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados. b) Laying of Granite Countertop. c) Fixing of S.S Sink. ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. b) Over Head Water Tank ▪ Laying of Green marble for Staircase. ▪ Fixing of UPVC French Door (without Mosquito mesh shutter). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st JANUARY-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of M.S Window Safety Grills 56% completed. (180 / 320). ▪ Fire Fighting Works 50% completed. ▪ Wire pulling works 10% completed (10/ 80). ● Model Flat Finishing works 95% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of M.S Window Safety Grills 72% completed. (230 / 320). ▪ Fire Fighting Works 60% completed. ▪ Electrical Wire pulling works 53% completed (43/ 80). ● Model Flat Finishing works 95% completed.

BLOCK	STATUS AS ON 31st JANUARY-2024
D3 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

D3 BLOCK	<ul style="list-style-type: none"> ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 1 out of 3 ▪ Fixing of Bathroom Wall Tiles 100% completed. (320 / 320) ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed. (80 / 80) b) Laying of Granite Countertop 100% completed. (80 / 80). ▪ Fixing of S.S Sink 100% completed. (80 / 80). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 100% completed. (320 / 320) b) Vitrified Tiles in Halls & Bedrooms 100% completed. (80 / 80) c) Vitrified Tiles in Corridor 100% completed. ▪ Fixing of Main Door & Internal Shutters 100% completed (880 / 880) ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 100% completed. b) Over Head Water Tank 3 out of 3 completed. ▪ Fixing of UPVC Windows 100% completed. (400 / 400) 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st JANUARY-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Vitrified Tiles in Halls & Bedrooms 97% completed. (78 / 80) b) Vitrified Tiles in Corridor. ▪ Fixing of UPVC Windows 97% completed. (390 / 400) ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 99% completed (159 / 160). ▪ Laying of Green marble for Staircase. ▪ Lift Cladding works 90% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Laying Of Floor Tiles ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 99% completed (159 / 160). ▪ Laying of Green marble for Staircase. ▪ Lift Cladding works 90% completed. ▪ Application of Exterior Wall Primer ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works - 4 out of 4 - 85% completed. ▪ Fixing of M.S Window Safety Grills



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Application of Exterior Wall Primer ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 90% completed. b) Over Head Water Tank 3 out of 3 completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works - 4 out of 4 - 80% completed. ▪ Fixing of M.S Window Safety Grills 31% completed (100/320). ▪ Fire Fighting works 15% completed. 	<p>56% completed (180/320).</p> <ul style="list-style-type: none"> ▪ Firefighting works 25% completed. ▪ Electrical Wire pulling works 10% completed (8/ 80).
BLOCK	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31 st JANUARY-2024
COMMUNITY HALL	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (2 out of 2) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (b) Tank Wall Concrete (c) Top Cover slab Concrete. ▪ Block work upto Fourth floor & Parapet wall. ▪ Ceiling Plastering upto Fourth floor. ▪ Wall plastering upto Fourth floor. ▪ 1st Coat Wall Putty upto Fourth floor. ▪ 2nd Coat Wall Putty upto Fourth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Vitrified Floor Tiles in Hall & rooms 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> b) Ceramic Floor Tiles in Bathrooms. c) Kota Stone in Staircase & Lobby ▪ Fixing of UPVC Windows. ▪ Fixing of Wooden flush Door for rooms. ▪ Fixing of Fire Safety Door for Hall Main Entrance ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. b) Over Head Water Tank. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st JANUARY-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Firefighting works – Installation of Pipelines 80% completed. ▪ Electrical Wire & cables pulling work 75% completed. ▪ Fixing of Sanitary fixtures. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer. ▪ Fire fighting works – Installation of Pipelines 90% completed. ▪ Electrical Wire & cables pulling work 80% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of Sanitary fixtures.

	STATUS AS ON 31st JANUARY-2024
EXTERNAL DEVELOPMENT WORKS	<ul style="list-style-type: none"> ➤ Underground Sump-2 (Near D-Block) <ul style="list-style-type: none"> ▪ Base Slab - R.C.C 100% completed. ▪ Sump Wall - R.C.C 100% completed. ▪ Top slab R.C.C 100% completed. ▪ Outer Wall Waterproof plastering – 100% completed. ▪ Inner Wall Waterproof plastering 60% completed. ▪ Pump room Inner plastering 75% completed. ➤ Underground Sump-1 (Near B-Block) <ul style="list-style-type: none"> ▪ Base Slab R.C.C 100% completed. ▪ Sump Wall - R.C.C 100% completed. ▪ Top slab R.C.C 100% completed. ➤ Sewage Treatment Plant-2 (Near D-Block) <ul style="list-style-type: none"> ▪ Base slab – R.C.C 100% completed. ▪ STP Wall – R.C.C 100% completed. ▪ STP Top Slab – R.C.C 100% completed.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

- | | |
|--|---|
| | <ul style="list-style-type: none">▪ STP Pump Room completed.▪ Outer wall Waterproof plastering 100% completed.▪ Inner Wall Waterproof plastering 50% completed. |
|--|---|

PHOTOGRAPHS OF WORK PROGRESS AS ON 31st JANUARY 2024

Community Hall: Fire Fighting Works – Installation of Pipeline 90% completed. Electrical Wire pulling work 80% completed.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block A1: Fixing of Bathroom & Toilet tiles, Laying of Vitrified floor Tiles, Fixing of UPVC Windows on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block A2 : Laying of bathroom & toilet floor tiles, vitrified tiles & fixing of door shutters on progress.



PROGRESS REPORT CGEWHO – CHENNAI PHASE-III PROJECT

Block B1: Electrical Wire pulling works completed, testing works on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block B2 : Ninth Floor Level slab Concrete casting 100% completed. Ninth floor columns 50% completed. Shuttering works for 1st Half of 10th floor level slab on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT


Block C1: Electrical Wire pulling works, fabrication & fixing of Windows Safety grills works on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block C2: Terrace Water proofing works & laying of Pipelines for Firefighting works on progress.

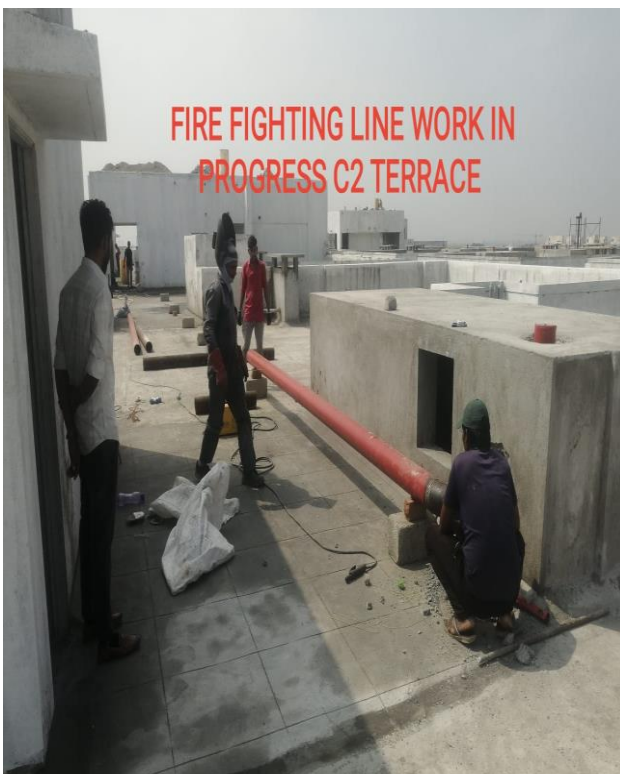

PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block C3: Lift cladding works & Corridor Tile laying works on progress



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block D1: Lift cladding works & Plumbing correction works on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block D2: Electrical wire pulling works & Plumbing line checking works on progress,



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block D3: Electrical wire pulling works & Plumbing line correction works on progress.



PROGRESS REPORT **CGEWHO – CHENNAI PHASE-III PROJECT**

Sewage Treatment Plant 2 (Near D Block). All RCC works completed. Pump room work completed. Internal Water proof plastering works on progress.



U.G Sump 2 (Near D Block) – All RCC works completed. Pump room work completed. Internal Water proof plastering works on progress.



PROGRESS REPORT **CGEWHO – CHENNAI PHASE-III PROJECT**

U.G Sump 1 (Near B Block) – All RCC works completed. Pump room work on progress.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

QUALITY CONTROL

DURING CONSTRUCTION FOLLOWING QUALITY CONTROL TESTS CONDUCTED AT SITE:

Sl.No.	Materials	Source from	Test Done	Result
1	M-Sand	Arcot (T.K), Ranipet (Dist) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2.	P- Sand	Uthiramerur, Kanchipuram (DT) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2	Coarse Aggregate (20mm)	Sriperambathur, Kanchipuram (Dt), Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
3	Coarse Aggregate (12mm)	Sriperambathur, Kanchipuram (Dt) Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
4	Cement	Third party testing is being done.		
5	Steel	Third party testing is being done.		
6	Pile Integrity	Third party testing is being done.		
7	Soil Compaction	Third party testing is being done.		
8	RCC cubes are being tested and Register is being maintained.			
9	Slump test conducted at site to insure workability of concrete.			

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

PHOTOGRAPH OF QUALITY CONTROL AT SITE

Concrete Cube Compressive Strength Testing



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

20mm & 12mm Aggregate Sieve Analysis Testing



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

Fine Aggregate Sieve Analysis Testing

