

**CGEWHO – CHENNAI PHASE-III
PROJECT**



MONTHLY PROGRESS REPORT

STATUS AS ON : 31.12.2023

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

31.12.2023

BLOCK	STATUS AS ON 31 st DECEMBER-2023	
A1 BLOCK	<p>◆ 100% Completed Works</p> <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete 2 out of 2 (b) Tank Wall Concrete 2 out of 2 (c) Top Cover slab Concrete 2 out of 2 ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor ▪ Electrical Conducting works in Tenth floor. ▪ Fixing of Water supply pipe Lines (CPVC) –100% completed (200 / 200). ▪ Fixing of Sanitary Lines (PVC) – 100% completed (200/ 200). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31 st DECEMBER-2023
	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External Plastering 95% completed in all sides. ▪ Fixing of Water supply pipe Lines (CPVC) –97% completed (195 / 200). <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Fixing of Sanitary Lines (PVC) – 80% completed (160/ 200). ▪ Fixing of Vertical Plumbing Lines in Shaft 60% completed. (120/200). ▪ Fixing of Staircase Handrail 75% completed. ▪ Fixing of Bathroom Wall Tiles 20% completed (40/200). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 20% completed (40/200) ▪ Vitrified Tiles in Halls & Bedrooms 18% completed (36/200). 	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External Plastering 95% completed in all sides. ▪ Fixing of Vertical Plumbing Lines in Shaft 90% completed. (180/200). ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank (1 / 2). <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Fixing of Staircase Handrail 85% completed. ▪ Fixing of Bathroom Wall Tiles 33% completed (66/200). ▪ Fixing of Toilet Wall Tiles 12% completed (24/200). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathrooms 33% completed (66/200) b) Ceramic Tiles in Toilets 12% completed (24/200)



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 8% completed (17/200). b) Laying of Granite Countertop 39% completed (79/200). ▪ Fixing of Door Shutters started (26/1200). ▪ Lift Materials 4 out of 4 received. ◆ Model Flat Finishing works 90% completed. 	<ul style="list-style-type: none"> ▪ Vitrified Tiles in Halls & Bedrooms 25% completed (50/200). ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 15% completed (30/200). b) Laying of Granite Countertop 48% completed (96/200). ▪ Fixing of Door Shutters on progress (42/1200). ▪ Lift Materials 4 out of 4 received. Shaft work on progress. ◆ Model Flat Finishing works 90% completed.
BLOCK	STATUS AS ON 31st DECEMBER-2023	
A2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete 2 out of 2 (b) Tank Wall Concrete 2 out of 2 (c) Top Cover slab Concrete 2 out of 2 ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ Electrical Conducting works upto Tenth floor. ▪ Fixing of Water supply pipe Lines (CPVC) –100% completed (200 / 200). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st DECEMBER-2023
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Electrical Conducting works in Tenth floor. ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 90% completed. ▪ Fixing of Water supply pipe Lines (CPVC) –95% completed (190 / 200). 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. ▪ Fixing of Sanitary Lines (PVC) – 95% completed (190/ 200). ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of Vertical Plumbing Lines in



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ 1st Coat Wall Putty in Tenth floor. ▪ Fixing of Sanitary Lines (PVC) – 60% completed (120/ 200). ▪ Fixing of Vertical Plumbing Lines in Shaft started (10/200). ▪ Lift Materials 4 out of 4 received. 	<p>Shaft 60% completed (120/200).</p> <ul style="list-style-type: none"> ▪ Fixing of Bathroom Wall Tiles started (6/200). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom started (6/200) ▪ Vitrified Tiles in Halls & Bedrooms started (3/200). ▪ Lift Materials 4 out of 4 received. Shaft work on progress.
BLOCK	STATUS AS ON 31st DECEMBER-2023	
B1 BLOCK	<p>◆ 100% Completed Works</p> <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 3) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> b) Ceramic Tiles in Bathroom c) Vitrified Tiles in Halls & Bedrooms. d) Vitrified Tiles in Corridor. ▪ Fixing of UPVC Windows. 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BI BLOCK	<ul style="list-style-type: none"> ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) ▪ Kitchen Finishing Works <ul style="list-style-type: none"> c) Fixing of Wall Dados. d) Laying of Granite Countertop. e) Fixing of S.S Sink. ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> b) Terrace floor Water proofing. c) Over Head Water Tank. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st DECEMBER-2023
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 3 out 3. ▪ Lift Cladding works 3 out of 3. ▪ Fixing of Door Shutters 95% completed (800/840). ▪ Laying of Green marble for Staircase. ▪ Application of Exterior Wall Primer ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of M.S Window Safety Grills 40% completed. ▪ Electrical wire pulling work 25% completed (30/120). ● Model Flat Finishing works 95% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 3 out 3. ▪ Lift Cladding works 3 out of 3. ▪ Fixing of Door Shutters 97% completed (820/840). ▪ Laying of Green marble for Staircase. ▪ Application of Exterior Wall Primer ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of M.S Window Safety Grills 60% completed. ▪ Electrical wire pulling work 51% completed (62/120). ▪ Fire Fighting works 50% completed. ● Model Flat Finishing works 95% completed.
BLOCK	STATUS AS ON 31st DECEMBER-2023	
B2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Upto Eighth floor level slab R.C.C ▪ Block work upto Sixth floor. ▪ Ceiling plastering upto Fifth floor. ▪ Wall plastering upto Fifth floor. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st DECEMBER-2023
	<ul style="list-style-type: none"> ◆ Works On Progress <ul style="list-style-type: none"> ▪ Eighth floor level slab – 2nd Half Shuttering & Barbending works 60% completed. ▪ Ninth floor level slab – 1st Half Shuttering works 20% completed. 	<ul style="list-style-type: none"> ◆ Works On Progress <ul style="list-style-type: none"> ▪ Eighth floor Columns Concrete 90% completed. ▪ Ninth floor level slab – 1st Half R.C.C completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Block work <ul style="list-style-type: none"> a) In Sixth floor 60% completed. b) In Seventh floor 20% completed. ▪ Ceiling Plastering <ul style="list-style-type: none"> a) In Fifth floor 50% completed. ▪ Wall Plastering <ul style="list-style-type: none"> a) In Fifth floor 50% completed 	<ul style="list-style-type: none"> ▪ Block work <ul style="list-style-type: none"> a) In Sixth floor 85% completed. b) In Seventh floor 40% completed. ▪ Ceiling Plastering <ul style="list-style-type: none"> a) In Sixth floor 60% completed. ▪ Wall Plastering <ul style="list-style-type: none"> a) In Sixth floor 55% completed
BLOCK	STATUS AS ON 31st DECEMBER-2023	
C1 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Internal Plumbing Line. <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom b) Vitrified Tiles in Halls & Bedrooms c) Vitrified Tiles in Corridor 100% completed. ▪ Fixing of UPVC Windows. ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed. ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Laying of Green marble for Staircase. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados. b) Laying of Granite Countertop. ▪ Fixing of S.S Sink. ▪ Lift Cladding works 4 out of 4. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. 	
	<p style="text-align: center;">STATUS UPTO PREVIOUS MONTH</p> <ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Staircase Hand Rails 3 out of 3 ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. ▪ Lift Installation works 4 out 4. ▪ Application of Exterior Wall Primer ▪ Fixing of Door Shutters 95% completed (1035 / 1080). ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of M.S Window Safety Grills 30% completed. ▪ Electrical wire pulling work 30% completed (36/120). ● Model Flat Finishing works 95% completed. 	<p style="text-align: center;">STATUS AS ON 31st DECEMBER-2023</p> <ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Staircase Hand Rails 3 out of 3 ▪ Lift Installation works 4 out 4. ▪ Application of Exterior Wall Primer Fixing of Door Shutters 97% completed (1050 / 1080) ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of M.S Window Safety Grills 50% completed. ▪ Electrical wire pulling work 46% completed (56/120). ▪ Fire Fighting works 30% completed. ● Model Flat Finishing works 95% completed.
BLOCK	STATUS AS ON 31st DECEMBER-2023	
C2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (2 out of 3) (b) Wall Concrete (2 out of 3) (c) Top Cover slab (2 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 1 out of 3 ▪ Fixing of Bathroom Wall Tiles completed. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom completed. b) Vitrified Tiles in Halls & Bedrooms completed. c) Vitrified Tiles in Corridor completed. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed. (120 / 120) b) Laying of Granite Countertop 100% completed. (120 / 120). c) Fixing of S.S Sink 100% completed. (120 / 120). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st DECEMBER-2023
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Application of Exterior Wall Primer ▪ Fixing of Main Door & Internal Shutters 92% completed (998 / 1080) ▪ Lift Installation works 2 out 4 - 90% completed. ▪ Fixing of UPVC Window 96% completed. (578 / 600) ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 88% completed. (213 /240) ▪ Lift Installation works – 3rd Lift 75% completed. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 50% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Application of Exterior Wall Primer ▪ Fixing of Main Door & Internal Shutters 94% completed (1023 / 1080) ▪ Lift Installation works 2 out 4 - 90% completed. ▪ Fixing of UPVC Window 98% completed. (588 / 600) ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 95% completed. (228 /240) ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works – <ul style="list-style-type: none"> 3rd Lift - 75% completed. 4th Lift – 45% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> b) Over Head Water Tank 2 out 3 work in progress. ▪ Laying of Green marble for Staircase 70% completed. ▪ Lift Cladding work 70% completed. 	<ul style="list-style-type: none"> ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 50% completed. b) Over Head Water Tank 2 out 3 work in progress. ▪ Laying of Green marble for Staircase 85% completed. ▪ Lift Cladding work 70% completed. ▪ Electrical wire pulling started. ▪ Fire Fighting works 15% completed.
BLOCK	STATUS AS ON 31st DECEMBER-2023	
C3 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (2 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank (1 / 2) completed. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed (100/100) b) Laying of Granite Countertop 100% completed. (100/100). c) Fixing of S.S Sink 100% completed. (100/ 100). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st DECEMBER-2023
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Fixing of Staircase Hand Rails. ▪ Application of Exterior Wall Primer ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 90% completed (90/100) b) Laying of Granite Countertop 93% completed. (93/100). c) Fixing of S.S Sink 90% completed. (93/ 100). ◆ Works On Progress <ul style="list-style-type: none"> ▪ 2nd Coat Wall Putty 63% completed. (63 /100). ▪ Fixing of Bathroom Wall Tiles 72% completed. (216 /300) ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 72% completed. (216 /300) b) Vitrified Tiles in Halls & Bedrooms 85% completed. (85 / 100) ▪ Fixing of UPVC Window 13% Completed.(65 / 500) ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 34% completed (68 / 200) ▪ Fixing of Main Door & Internal Shutters on progress (67 / 900) ▪ Lift Installation works – Materials received 4 out 4. Scaffolding works started. ▪ Lift Cladding work 20% completed. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 20% completed. 	<ul style="list-style-type: none"> ▪ Fixing of Staircase Hand Rails. ▪ Application of Exterior Wall Primer ▪ Fixing of Bathroom Wall Tiles 93% completed. (280 /300) ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 93% completed. (280 /300) b) Vitrified Tiles in Halls & Bedrooms 92% completed. (92 / 100) ◆ Works On Progress <ul style="list-style-type: none"> ▪ 2nd Coat Wall Putty 80% completed. (80 /100). ▪ Fixing of UPVC Window 18% Completed.(91 / 500) ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 35% completed (70 / 200) ▪ Fixing of Main Door & Internal Shutters 10% completed (91 / 900) ▪ Lift Installation works – <ul style="list-style-type: none"> 2 Lifts - 80% completed. 2 Lifts - works now started. ▪ Lift Cladding work 20% completed. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 40% completed. ▪ Laying of Green marble for Staircase 50% completed.
BLOCK	STATUS AS ON 31st DECEMBER-2023	
D1 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

D1 BLOCK	<ul style="list-style-type: none"> (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 3 out of 3 ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles 100% completed. (320 / 320). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 100% completed. (320 / 320) ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed. (80 / 80) b) Laying of Granite Countertop 100% completed. (80 / 80). c) Fixing of S.S Sink 100% completed. (80 / 80). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st DECEMBER-2023
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. ▪ Application of External Wall Primer-1st Coat ▪ Fixing of Bathroom Wall Tiles 96% completed. (310 / 320). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 96% completed. (310 / 320) ▪ Vitrified Tiles in Halls & Bedrooms 93% completed. (75 / 80). ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 95% completed. (76 / 80) b) Laying of Granite Countertop 95% completed. (76 / 80). 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. ▪ Application of External Wall Primer-1st Coat ▪ Vitrified Tiles in Halls & Bedrooms 96% completed. (77 / 80). ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 90% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ 2nd Coat Wall Putty 50% completed. (40 / 80). ▪ Fixing of UPVC Windows 72% completed. (291 / 400). ▪ Fixing of UPVC French Door 21%



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<p>c) Fixing of S.S Sink 92% completed. (74 / 80).</p> <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ 2nd Coat Wall Putty 30% completed. (24 / 80). ▪ Fixing of UPVC Windows 35% completed. (141 / 400). ▪ Fixing of Main Door & Internal Shutters 75% completed (662 / 880) ▪ Application of Exterior Wall Primer ▪ Lift Installation works 2 out 4 - 70% completed. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 80% completed. 	<p>completed.(without Mosquito mesh shutter) (35 / 160)</p> <ul style="list-style-type: none"> ▪ Fixing of Main Door & Internal Shutters 79% completed (702 / 880) ▪ Application of Exterior Wall Primer 75% completed ▪ Lift Installation works 2 out 4 - 80% completed. Other 2 Lifts work now started.
BLOCK	STATUS AS ON 31st DECEMBER-2023	
D2 BLOCK	<p>◆ 100% Completed Works</p> <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 3) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

D2 BLOCK	<ul style="list-style-type: none"> ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom b) Vitrified Tiles in Halls & Bedrooms. c) Vitrified Tiles in Corridor. ▪ Fixing of UPVC Windows. ▪ Fixing of Main Door & Internal Shutters. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados. b) Laying of Granite Countertop. c) Fixing of S.S Sink. ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. b) Over Head Water Tank ▪ Laying of Green marble for Staircase. ▪ Fixing of UPVC French Door (without Mosquito mesh shutter). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st DECEMBER-2023
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of M.S Window Safety Grills 47% completed. (152 / 320). ▪ Fire Fighting Works 50% completed. ▪ Wire pulling works on progress. ● Model Flat Finishing works 95% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of M.S Window Safety Grills 56% completed. (180 / 320). ▪ Fire Fighting Works 50% completed. ▪ Wire pulling works 10% completed (10/ 80). ● Model Flat Finishing works 95% completed.
BLOCK	STATUS AS ON 31st DECEMBER-2023	
D3 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

D3 BLOCK	<ul style="list-style-type: none"> ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 1 out of 3 ▪ Fixing of Bathroom Wall Tiles 100% completed. (320 / 320) ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed. (80 / 80) b) Laying of Granite Countertop 100% completed. (80 / 80). ▪ Fixing of S.S Sink 100% completed. (80 / 80). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 100% completed. (320 / 320) ▪ Fixing of Main Door & Internal Shutters 100% completed (880 / 880) 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st DECEMBER-2023
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Vitrified Tiles in Halls & Bedrooms. (72 / 80) b) Vitrified Tiles in Corridor. ▪ Fixing of UPVC Windows 96% completed. (387 / 400) ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 99% completed (159 / 160). ▪ Laying of Green marble for Staircase. ▪ Lift Cladding works 90% completed. ▪ Application of Exterior Wall Primer 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Vitrified Tiles in Halls & Bedrooms 97% completed. (78 / 80) b) Vitrified Tiles in Corridor. ▪ Fixing of UPVC Windows 97% completed. (390 / 400) ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 99% completed (159 / 160). ▪ Laying of Green marble for Staircase. ▪ Lift Cladding works 90% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 90% completed. b) Over Head Water Tank 3 out of 3 completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works - 3 out of 4 - 80% completed & 4th Lift 65% completed. ▪ Fixing of M.S Window Safety Grills 18% completed (60/320). ▪ Fire Fighting works on progress. 	<ul style="list-style-type: none"> ▪ Application of Exterior Wall Primer ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 90% completed. b) Over Head Water Tank 3 out of 3 completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works - 4 out of 4 - 80% completed. ▪ Fixing of M.S Window Safety Grills 31% completed (100/320). ▪ Fire Fighting works 15% completed.
BLOCK	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st DECEMBER-2023
COMMUNITY HALL	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (2 out of 2) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (b) Tank Wall Concrete (c) Top Cover slab Concrete. ▪ Block work upto Fourth floor & Parapet wall. ▪ Ceiling Plastering upto Fourth floor. ▪ Wall plastering upto Fourth floor. ▪ 1st Coat Wall Putty upto Fourth floor. ▪ 2nd Coat Wall Putty upto Fourth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Vitrified Floor Tiles in Hall & rooms 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> b) Ceramic Floor Tiles in Bathrooms. c) Kota Stone in Staircase & Lobby ▪ Fixing of UPVC Windows. ▪ Fixing of Wooden flush Door for rooms. ▪ Fixing of Fire Safety Door for Hall Main Entrance ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. b) Over Head Water Tank. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st DECEMBER-2023
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fire fighting works – Installation of Pipelines 80% completed. ▪ Electrical Wire & cables pulling work 75% completed. ▪ Fixing of Sanitary fixtures. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fire fighting works – Installation of Pipelines 85% completed. ▪ Electrical Wire & cables pulling work 80% completed. ▪ Fixing of Sanitary fixtures.

	STATUS AS ON 31st DECEMBER-2023
EXTERNAL DEVELOPMENT WORKS	<ul style="list-style-type: none"> ➤ Underground Sump-1 (Near D-Block) <ul style="list-style-type: none"> ● Structure Work. <ul style="list-style-type: none"> ◆ Completed <ul style="list-style-type: none"> ▪ Base Slab - R.C.C 100% completed. ▪ Sump Wall - R.C.C 100% completed. ▪ Top slab R.C.C 100% completed. ▪ Outer Wall Waterproof plastering – 100% completed. ◆ On Progress <ul style="list-style-type: none"> ▪ Inner Wall Waterproof plastering started. ▪ Pump room Inner plastering 50% completed. ➤ Underground Sump-2 (Near B-Block) <ul style="list-style-type: none"> ● Structure Work. <ul style="list-style-type: none"> ◆ Completed <ul style="list-style-type: none"> ▪ P.C.C for Base Slab 100% completed. ▪ Base Slab R.C.C 100% completed. ▪ Sump Wall - R.C.C 100% completed.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none">◆ On Progress<ul style="list-style-type: none">▪ Sump Top Slab Reinforcement and Shuttering 95% completed progress➤ Sewage Treatment Plant-1 (Near D-Block)<ul style="list-style-type: none">● Structure Work<ul style="list-style-type: none">▪ Base slab – R.C.C 100% completed.▪ STP Wall – R.C.C 100% completed.▪ STP Top Slab – R.C.C 100% completed.▪ STP Pump Room Column work on progress.
--	---

PHOTOGRAPHS OF WORK PROGRESS AS ON 31st DECEMBER 2023

Community Hall : Fire Fighting Works – Installation of Pipeline 80% completed. Electrical Wire pulling work 75% completed.



PROGRESS REPORT


CGEWHO – CHENNAI PHASE-III PROJECT

Block A1: Laying of floor Tiles, Kitchen Granite & Dados fixing, Fixing of Door Shutters, preparation for laying of Staircase Green marble on progress.



PROGRESS REPORT **CGEWHO – CHENNAI PHASE-III PROJECT**

Block A2 : Vertical plumbing works in shafts 60% completed. Fixing of bathroom Wall tiles & laying of bathroom floor tiles on progress.

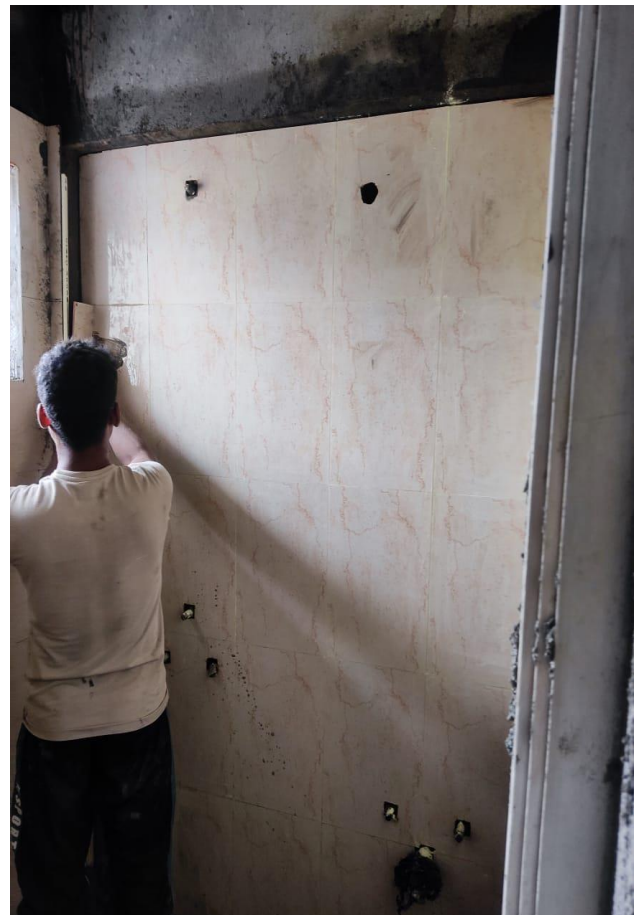

PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT


Block B1: Electrical Wire pulling works 51% completed. Fixing of Window Safety Grills 60% completed .Firefighting works 50% completed.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT


Block B2 : Ninth Floor Level slab 1st half concrete casting 100% completed.

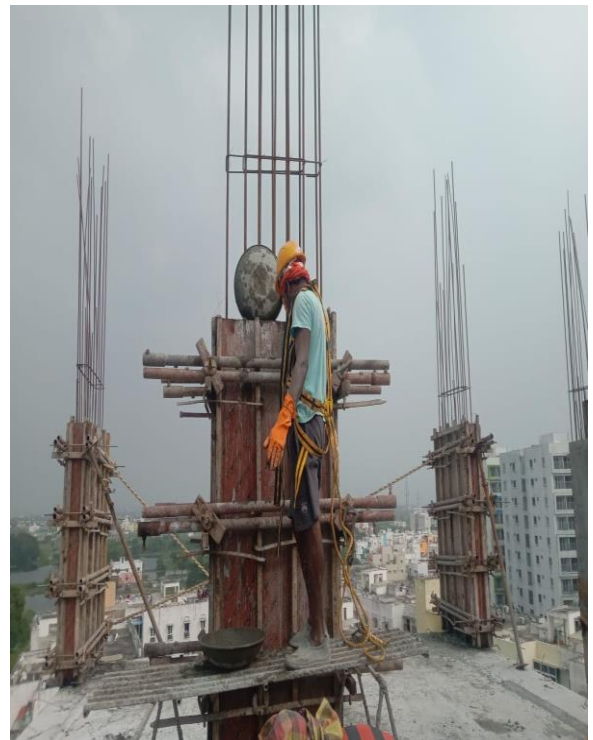

PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT


Block C1: Fixing of Window Safety Grills 50% completed & Electrical Wire pulling works 46% completed.

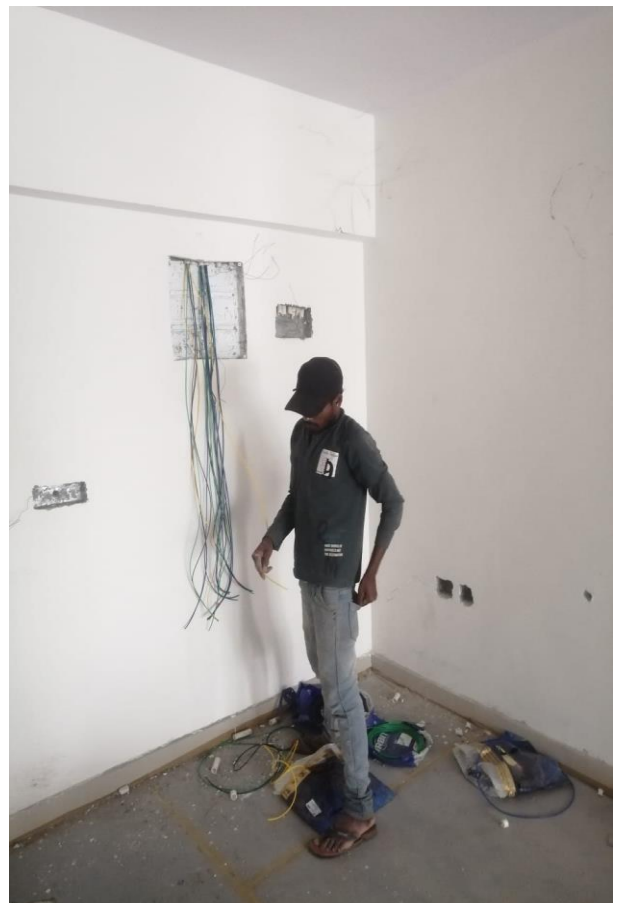

PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block C2: Fixing of Door Shutters 94% completed. Electrical wire pulling work started.

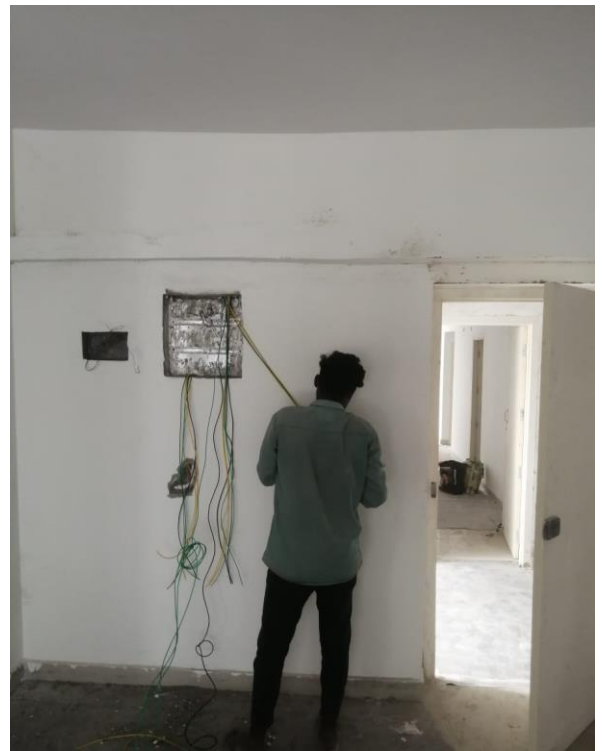

PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT


Block C3: Terrace waterproofing work on progress. Fixing of Internal Door shutters on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT


Block D1: Fixing of Bathroom wall tiles & laying of bathroom floor tiles completed. Fixing of UPVC Windows 72% completed. Stilt floor columns & roof plastering completed.

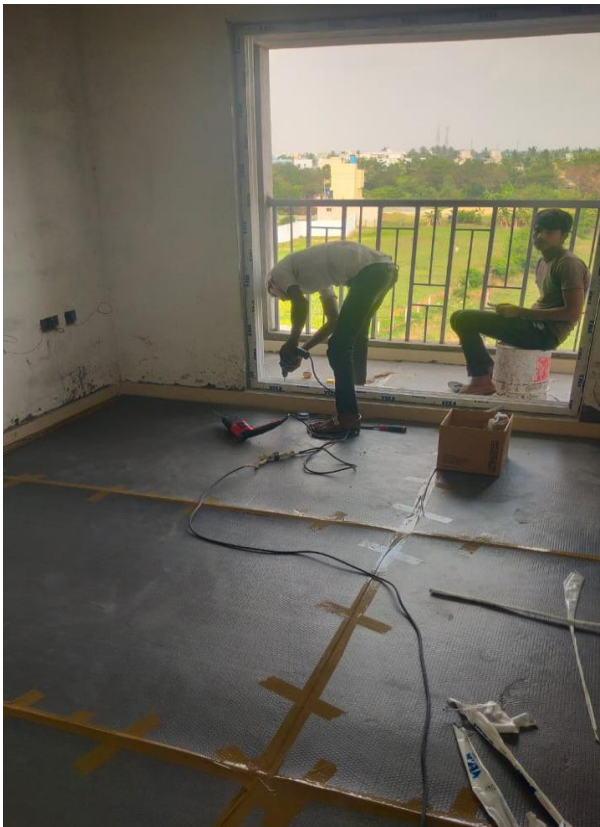

PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block D2: Fire Fighting works 50% completed. Electrical wire pulling 10% completed.

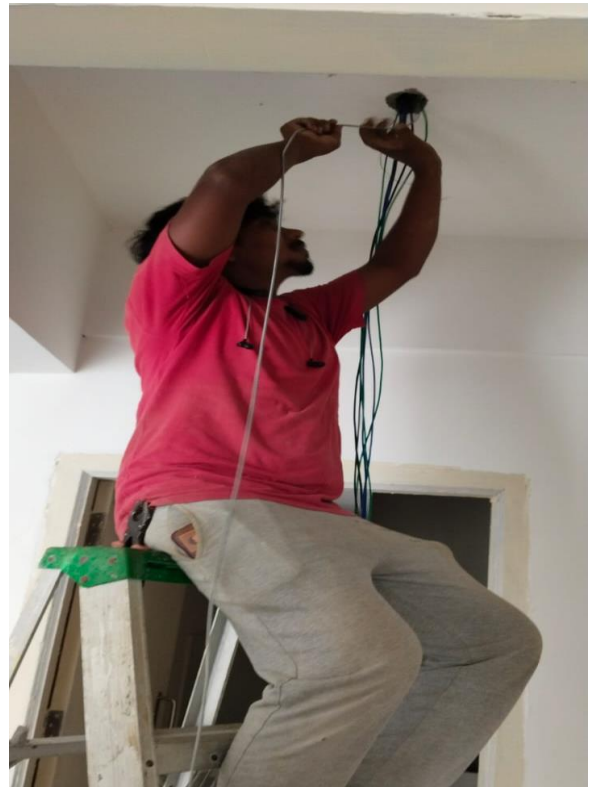

PROGRESS REPORT CGEWHO – CHENNAI PHASE-III PROJECT

Block D3: Fixing of Window Grills & Laying of Vitrified Floor Tiles on progress



PROGRESS REPORT **CGEWHO – CHENNAI PHASE-III PROJECT**

Sewage Treatment Plant 1 (Near D Block) – Base Slab RCC completed. Wall Concrete & Top Slab 100% completed. Pump room Columns work on progress.



U.G Sump 1 (Near D Block) – Base Slab RCC 95% completed. Sump wall & Top Slab Concrete 100% completed. Inner plastering works on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

U.G Sump 2 – Base Slab RCC 95% completed. Sump wall Concrete completed. Shuttering & Barbending works for Top Slab completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

QUALITY CONTROL

DURING CONSTRUCTION FOLLOWING QUALITY CONTROL TESTS CONDUCTED AT SITE:

Sl.No.	Materials	Source from	Test Done	Result
1	M-Sand	Arcot (T.K), Ranipet (Dist) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2.	P- Sand	Uthiramerur, Kanchipuram (DT) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2	Coarse Aggregate (20mm)	Sriperambathur, Kanchipuram (Dt), Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
3	Coarse Aggregate (12mm)	Sriperambathur, Kanchipuram (Dt) Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
4	Cement	Third party testing is being done.		
5	Steel	Third party testing is being done.		
6	Pile Integrity	Third party testing is being done.		
7	Soil Compaction	Third party testing is being done.		
8	RCC cubes are being tested and Register is being maintained.			
9	Slump test conducted at site to insure workability of concrete.			

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

PHOTOGRAPH OF QUALITY CONTROL AT SITE

Concrete Cube Compressive Strength Testing



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

20mm & 12mm Aggregate Sieve Analysis Testing



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

Fine Aggregate Sieve Analysis Testing

