

**CGEWHO – CHENNAI PHASE-III
PROJECT**



MONTHLY PROGRESS REPORT

STATUS AS ON : 29.02.2024

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

29.02.2024

BLOCK	STATUS AS ON 29 th FEBRUARY-2024	
A1 BLOCK	<p>◆ 100% Completed Works</p> <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete 2 out of 2 (b) Tank Wall Concrete 2 out of 2 (c) Top Cover slab Concrete 2 out of 2 ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor ▪ Electrical Conducting works in Tenth floor. ▪ Fixing of Water supply pipe Lines (CPVC). ▪ Fixing of Sanitary Lines (PVC). ▪ Fixing of Vertical Plumbing Lines in Shaft. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank (2 / 2). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 29 th FEBRUARY-2024
	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External Plastering 95% completed in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace Water Proofing 10% completed. <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Fixing of Staircase Handrail 90% completed. ▪ Fixing of Bathroom Wall Tiles 71% completed (143/200). ▪ Fixing of Toilet Wall Tiles 71% completed (143/200). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathrooms 71% completed (143/200) 	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External Plastering 95% completed in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace Water Proofing 10% completed. ▪ Fixing of Staircase Handrail 95% completed. ▪ Fixing of Bathroom Wall Tiles 92% completed (185/200). ▪ Fixing of Toilet Wall Tiles 92% completed (185/200). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathrooms 92% completed (185/200) b) Ceramic Tiles in Toilets 92%



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> b) Ceramic Tiles in Toilets 71% completed (143/200) ▪ Vitrified Tiles in Halls & Bedrooms 71% completed (143/200). ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 63% completed (126/200). b) Laying of Granite Countertop 63% completed (126/200). c) Fixing of S.S Sink 63% completed (126/200) ▪ Fixing of Door Shutters 40% completed (480/1200). ▪ Fixing of UPVC Windows 20% completed (175 /800) ▪ Lift Materials 4 out of 4 received. Shaft work on progress. ➤ Model Flat Finishing works 90% completed. 	<p style="text-align: right;">completed (185/200)</p> <ul style="list-style-type: none"> ▪ Vitrified Tiles in Halls & Bedrooms 911% completed (182/200). ◆ Works On Progress <ul style="list-style-type: none"> ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 65% completed (130/200). b) Laying of Granite Countertop 75% completed (150/200). c) Fixing of S.S Sink 75% completed (150/200) ▪ Fixing of Door Shutters 79% completed (955/1200). ▪ Fixing of UPVC Windows 73% completed (588 /800) ▪ Lift Materials 4 out of 4 received. Shaft work on progress. ➤ Model Flat Finishing works 90% completed.
BLOCK	STATUS AS ON 29th FEBRUARY-2024	
A2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete 2 out of 2 (b) Tank Wall Concrete 2 out of 2 (c) Top Cover slab Concrete 2 out of 2 ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ Electrical Conducting works upto Tenth floor. ▪ Fixing of Water supply pipe Lines (CPVC). ▪ Fixing of Sanitary Lines (PVC). ▪ Fixing of Vertical Plumbing Lines in Shaft. 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 29 th FEBRUARY-2024
	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Fixing of Bathroom Wall Tiles 20% completed (40/200). ▪ Fixing of Toilet Wall Tiles 20% completed (40/200). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 20% completed (40/200) b) Ceramic Tiles in Toilet 20% completed (40/200) ▪ Vitrified Tiles in Halls & Bedrooms 20% completed. (40/200). ▪ Fixing of Door Shutters 20% completed (240/1200). ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 20% completed (40/200). b) Laying of Granite Countertop 20% completed (40/200). c) Fixing of S.S Sink 20% completed (40/200) ▪ Water Proofing Work <ul style="list-style-type: none"> a) Over Head Water Tank 50% completed (1 / 2) b) Terrace Water proofing 10% completed. ▪ Lift Materials 4 out of 4 received. Shaft work on progress. 	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Fixing of Bathroom Wall Tiles 37% completed (74/200). ▪ Fixing of Toilet Wall Tiles 37% completed (74/200). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 37% completed (74/200) b) Ceramic Tiles in Toilet 37% completed (74/200) ▪ Vitrified Tiles in Halls & Bedrooms 35% completed. (70/200). ▪ Fixing of Door Shutters 32% completed (389/1200). ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 20% completed (40/200). b) Laying of Granite Countertop 20% completed (40/200). c) Fixing of S.S Sink 20% completed (40/200) ▪ Water Proofing Work <ul style="list-style-type: none"> a) Over Head Water Tank 50% completed (1 / 2) b) Terrace Water proofing 25% completed. ▪ Lift Materials 4 out of 4 received. Shaft work on progress.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 29 th FEBRUARY-2024
B1 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 3) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom b) Vitrified Tiles in Halls & Bedrooms. c) Vitrified Tiles in Corridor. ▪ Fixing of UPVC Windows. ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados. b) Laying of Granite Countertop. c) Fixing of S.S Sink. ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. b) Over Head Water Tank. ▪ Fixing of Door Shutters 100% completed (840/840). ▪ Electrical wire pulling work 100% completed (120/120).

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BI BLOCK	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 29th FEBRUARY-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 3 out 3. ▪ Lift Cladding works 3 out of 3. ▪ Laying of Green marble for Staircase. ▪ Application of Exterior Wall Primer ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of M.S Window Safety Grills 75% completed. ▪ Electrical wire pulling work 93% completed (112/120). ▪ Firefighting works 60% completed. ● Model Flat Finishing works 95% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 3 out 3. ▪ Lift Cladding works 3 out of 3. ▪ Laying of Green marble for Staircase. ▪ Application of Exterior Wall Primer ▪ Fixing of M.S Window Safety Grills 90% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Firefighting works 60% completed. ● Model Flat Finishing works 95% completed.
BLOCK	STATUS AS ON 29th FEBRUARY-2024	
B2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Upto Ninth floor level slab R.C.C ▪ Ninth floor columns concrete. ▪ Tenth floor level slab 1st Half R.C.C ▪ Block work upto Seventh floor. ▪ Ceiling plastering upto Sixth floor. ▪ Wall plastering upto Sixth floor. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 29th FEBRUARY-2024
	<ul style="list-style-type: none"> ◆ Works On Progress <ul style="list-style-type: none"> ▪ Ninth floor Columns Concrete 50% completed. ▪ Shuttering works for 1st Half of 10th Floor level slab 10% completed. ▪ Block work <ul style="list-style-type: none"> a) In Eighth floor 40% completed. ▪ Ceiling Plastering <ul style="list-style-type: none"> a) In Seventh floor 50% completed. ▪ Wall Plastering <ul style="list-style-type: none"> a) In Seventh floor 50% completed ▪ Electrical conducting works 30% completed. 	<ul style="list-style-type: none"> ◆ Works On Progress <ul style="list-style-type: none"> ▪ Tenth floor Columns Concrete 50% completed. ▪ Shuttering works for 2nd Half of 10th Floor level slab 90% completed. ▪ Block work <ul style="list-style-type: none"> a) In Eighth floor 80% completed. ▪ Ceiling Plastering <ul style="list-style-type: none"> a) In Seventh floor 85% completed. ▪ Wall Plastering <ul style="list-style-type: none"> a) In Seventh floor 85% completed ▪ Electrical conducting works 45% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 29 th FEBRUARY-2024
C1 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Internal Plumbing Line. <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom b) Vitrified Tiles in Halls & Bedrooms c) Vitrified Tiles in Corridor 100% completed. ▪ Fixing of UPVC Windows. ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed. ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank b) Terrace floor Water proofing. ▪ Laying of Green marble for Staircase. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados. b) Laying of Granite Countertop. c) Fixing of S.S Sink. ▪ Lift Cladding works 4 out of 4. ▪ Fixing of Door Shutters 100% completed (1080 / 1080)

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 29 th FEBRUARY-2024
C1 BLOCK	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Staircase Hand Rails 3 out of 3 ▪ Lift Installation works 4 out 4. ▪ Application of Exterior Wall Primer. ▪ Electrical wire pulling work 91% completed (110/120). ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of M.S Window Safety Grills 70% completed. ▪ Fire Fighting works 40% completed. ● Model Flat Finishing works 95% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Staircase Hand Rails 3 out of 3 ▪ Lift Installation works 4 out 4. ▪ Application of Exterior Wall Primer. ▪ Electrical wire pulling work 100% completed (120/120). ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of M.S Window Safety Grills 85% completed. ▪ Fire Fighting works 40% completed. ● Model Flat Finishing works 95% completed.
BLOCK	STATUS AS ON 29th FEBRUARY-2024	
C2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (2 out of 3) (b) Wall Concrete (2 out of 3) (c) Top Cover slab (2 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 3 out of 3 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

C2 BLOCK	<ul style="list-style-type: none"> ▪ Fixing of Bathroom Wall Tiles completed. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom completed. b) Vitrified Tiles in Halls & Bedrooms completed. c) Vitrified Tiles in Corridor completed. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed. (120 / 120) b) Laying of Granite Countertop 100% completed. (120 / 120). c) Fixing of S.S Sink 100% completed. (120 / 120). ▪ Fixing of UPVC Window 100% completed. (600 / 600) ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed. (240 /240) ▪ Fixing of Main Door & Internal Shutters 100% completed (1080 / 1080) ▪ Laying of Green marble for Staircase 100% completed.. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 29th FEBRUARY-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Application of Exterior Wall Primer ▪ Lift Installation works 2 out 4 - 85% completed. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 95% completed. ▪ Laying of Green marble for Staircase 90% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works – <ul style="list-style-type: none"> 3rd Lift - 80% completed. 4th Lift – 80% completed. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 2 out 3 work in progress. ▪ Lift Cladding work 75% completed. ▪ Electrical wire pulling 30% completed (36 /120). ▪ Fire Fighting works 30% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Application of Exterior Wall Primer ▪ Lift Installation works 4 out 4 - 85% completed. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 95% completed. ▪ Lift Cladding work 90% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Electrical wire pulling 65% completed (78 /120). ▪ Fire Fighting works 40% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 29 th FEBRUARY-2024	
C3 BLOCK	<p>◆ 100% Completed Works</p> <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (2 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank (1 / 2) completed. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed (100/100) b) Laying of Granite Countertop 100% completed. (100/100). c) Fixing of S.S Sink 100% completed. (100/ 100). ▪ Fixing of Bathroom Wall Tiles 100% completed. (300 /300) ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 100% completed. (300 /300) b) Vitrified Tiles in Halls & Bedrooms 100% completed. (100 / 100) ▪ Laying of Green marble for Staircase 100% completed. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 29 th FEBRUARY-2024
	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails. ▪ Application of Exterior Wall Primer ▪ 2nd Coat Wall Putty 90% completed. (90 /100). 	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails. ▪ Application of Exterior Wall Primer ▪ 2nd Coat Wall Putty 90% completed. (90 /100).



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

C3 BLOCK	<ul style="list-style-type: none"> ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of UPVC Window 64% Completed. (321 / 500). ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 53% completed (107 / 200). ▪ Fixing of Main Door & Internal Shutters 16% completed (150 / 900). ▪ Lift Installation works – <ul style="list-style-type: none"> 2 Lifts - 80% completed. 3rd Lift – 10% completed. 4th Lift – Work on progress ▪ Lift Cladding work 30% completed. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 60% completed. ▪ Laying of Green marble for Staircase 70% completed. 	<ul style="list-style-type: none"> ▪ Fixing of UPVC Window 93% Completed. (436 / 500). ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 94% completed (188 / 200). ▪ Fixing of Main Door & Internal Shutters 99% completed (898 / 900). ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works – <ul style="list-style-type: none"> 2 Lifts - 85% completed. 3rd Lift - 25% completed. 4th Lift - 10% completed. ▪ Lift Cladding work 40% completed.
BLOCK	STATUS AS ON 29th FEBRUARY-2024	
D1 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 3 out of 3 b) Terrace floor Water proofing 100% completed. ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

D1 BLOCK	<ul style="list-style-type: none"> ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles 100% completed. (320 / 320). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 100% completed. (320 / 320) b) Vitrified Tiles in Halls & Bedrooms 100% completed. (80 / 80). ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed. (80 / 80) b) Laying of Granite Countertop 100% completed. (80 / 80). c) Fixing of S.S Sink 100% completed. (80 / 80). ▪ Fixing of Main Door & Internal Shutters 100% completed (880 / 880) 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 29th FEBRUARY-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. ▪ Application of External Wall Primer-1st Coat ▪ Fixing of UPVC Windows 90% completed. (360 / 400). ◆ Works On Progress <ul style="list-style-type: none"> ▪ 2nd Coat Wall Putty 75% completed. (60 / 80). ▪ Fixing of UPVC French Door 78% completed.(without Mosquito mesh shutter) (125 / 160) ▪ Application of Exterior Wall Primer 75% completed ▪ Lift Installation works <ul style="list-style-type: none"> a) 2 out 4 - 80% completed. b) 3rd lift - 20% completed. c) 4th lift - work on progress. ▪ Electrical Wire pulling works started (6/ 80). 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. ▪ Application of External Wall Primer-1st Coat ▪ Fixing of UPVC Windows 99% completed. (398 / 400). ▪ 2nd Coat Wall Putty 99% completed. (78 / 80). ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of UPVC French Door 98% completed.(without Mosquito mesh shutter) (158 / 160) ▪ Application of Exterior Wall Primer 80% completed ▪ Lift Installation works <ul style="list-style-type: none"> a) 3 out 4 - 80% completed. b) 4th lift - work on progress. ▪ Electrical Wire pulling works 12% completed. (10/ 80).



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 29 th FEBRUARY-2024
D2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 3) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom b) Vitrified Tiles in Halls & Bedrooms. c) Vitrified Tiles in Corridor. ▪ Fixing of UPVC Windows. ▪ Fixing of Main Door & Internal Shutters. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados. b) Laying of Granite Countertop. c) Fixing of S.S Sink. ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. b) Over Head Water Tank ▪ Laying of Green marble for Staircase.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Fixing of UPVC French Door (without Mosquito mesh shutter). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 29th FEBRUARY-2024
D2 BLOCK	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of M.S Window Safety Grills 72% completed. (230 / 320). ▪ Fire Fighting Works 60% completed. ▪ Electrical Wire pulling works 53% completed (43/ 80). • Model Flat Finishing works 95% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer. ▪ Fixing of M.S Window Safety Grills 90% completed. (290 / 320). ▪ Electrical Wire pulling works 99% completed (79/ 80). ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fire Fighting Works 60% completed. • Model Flat Finishing works 95% completed.
BLOCK	STATUS AS ON 29th FEBRUARY-2024	
D3 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ External Plastering in all sides. 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

D3 BLOCK	<ul style="list-style-type: none"> ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 1 out of 3 ▪ Fixing of Bathroom Wall Tiles 100% completed. (320 / 320) ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed. (80 / 80) b) Laying of Granite Countertop 100% completed. (80 / 80). ▪ Fixing of S.S Sink 100% completed. (80 / 80). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 100% completed. (320 / 320) b) Vitrified Tiles in Halls & Bedrooms 100% completed. (80 / 80) c) Vitrified Tiles in Corridor 100% completed. ▪ Fixing of Main Door & Internal Shutters 100% completed (880 / 880) ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 100% completed. b) Over Head Water Tank 3 out of 3 completed. ▪ Fixing of UPVC Windows 100% completed. (400 / 400) 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 29th FEBRUARY-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Laying Of Floor Tiles ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 99% completed (159 / 160). ▪ Laying of Green marble for Staircase. ▪ Lift Cladding works 90% completed. ▪ Application of Exterior Wall Primer ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works - 4 out of 4 - 85% completed. ▪ Fixing of M.S Window Safety Grills 56% completed (180/320). ▪ Firefighting works 25% completed. ▪ Electrical Wire pulling works 10% completed (8/ 80). 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Laying Of Floor Tiles ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 99% completed (159 / 160). ▪ Laying of Green marble for Staircase. ▪ Lift Cladding works 90% completed. ▪ Application of Exterior Wall Primer ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works - 4 out of 4 - 85% completed. ▪ Fixing of M.S Window Safety Grills 62% completed (200/320). ▪ Firefighting works 25% completed. ▪ Electrical Wire pulling works 50% completed (40/ 80).



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 29 th FEBRUARY-2024	
COMMUNITY HALL	<p>◆ 100% Completed Works</p> <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (2 out of 2) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (b) Tank Wall Concrete (c) Top Cover slab Concrete. ▪ Block work upto Fourth floor & Parapet wall. ▪ Ceiling Plastering upto Fourth floor. ▪ Wall plastering upto Fourth floor. ▪ 1st Coat Wall Putty upto Fourth floor. ▪ 2nd Coat Wall Putty upto Fourth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Vitrified Floor Tiles in Hall & rooms b) Ceramic Floor Tiles in Bathrooms. c) Kota Stone in Staircase & Lobby ▪ Fixing of UPVC Windows. ▪ Fixing of Wooden flush Door for rooms. ▪ Fixing of Fire Safety Door for Hall Main Entrance ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. b) Over Head Water Tank. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 29th FEBRUARY-2024
	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. 	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer. ▪ Fire fighting works – Installation of Pipelines 90% completed. ▪ Electrical Wire & cables pulling work 80% completed. <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Fixing of Sanitary fixtures. 	<ul style="list-style-type: none"> ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer. ▪ Fire fighting works – Installation of Pipelines 90% completed. ▪ Electrical Wire & cables pulling work 85% completed. <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Fixing of Sanitary fixtures.
--	--	--

	STATUS AS ON 29 th FEBRUARY-2024
EXTERNAL DEVELOPMENT WORKS	<ul style="list-style-type: none"> ➤ Underground Sump-2 (Near D-Block) <ul style="list-style-type: none"> ▪ Base Slab - R.C.C 100% completed. ▪ Sump Wall - R.C.C 100% completed. ▪ Top slab R.C.C 100% completed. ▪ Outer Wall Waterproof plastering – 100% completed. ▪ Inner Wall Waterproof plastering 75% completed. ▪ Pump room Inner plastering 80% completed. ➤ Underground Sump-1 (Near B-Block) <ul style="list-style-type: none"> ▪ Base Slab R.C.C 100% completed. ▪ Sump Wall - R.C.C 100% completed. ▪ Top slab R.C.C 100% completed. ▪ Outer Wall Waterproof plastering – 85% completed. ▪ Inner Wall Waterproof plastering on progress. ➤ Sewage Treatment Plant-2 (Near D-Block) <ul style="list-style-type: none"> ▪ Base slab – R.C.C 100% completed. ▪ STP Wall – R.C.C 100% completed. ▪ STP Top Slab – R.C.C 100% completed. ▪ STP Pump Room completed. ▪ Outer wall Waterproof plastering 100% completed. ▪ Inner Wall Waterproof plastering 70% completed. ➤ Sewage Treatment Plant-1 (Near C3-Block) <ul style="list-style-type: none"> ▪ Excavation Work started..



PROGRESS REPORT CGEWHO – CHENNAI PHASE-III PROJECT


PHOTOGRAPHS OF WORK PROGRESS AS ON 29th FEBRUARY 2024

Block A1: Fixing of UPVC Windows, laying of Staircase Green marble on progress.



PROGRESS REPORT **CGEWHO – CHENNAI PHASE-III PROJECT**

Block A2 : Laying of bathroom & toilet floor tiles, vitrified tiles on progress.

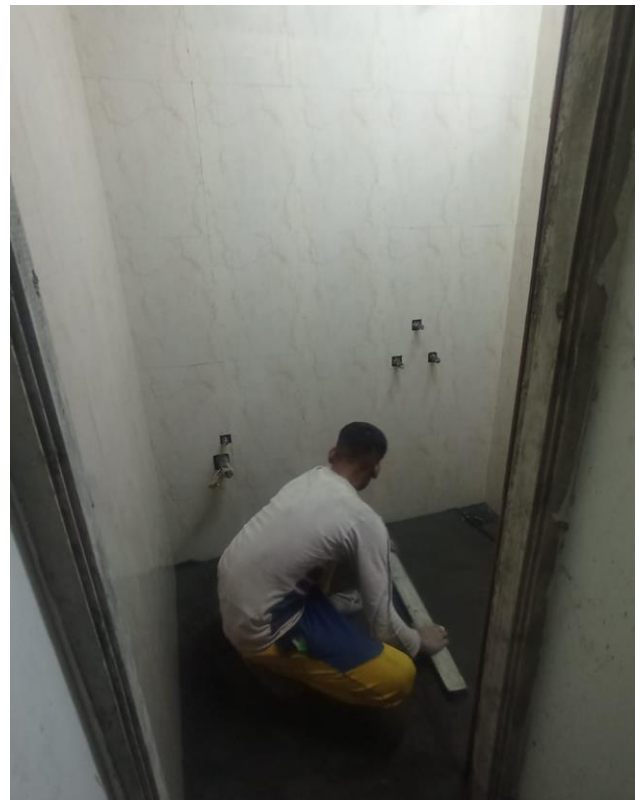

PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block B1: Connection of Plumbing lines in Shaft in Stilt floor on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT


Block B2 : Tenth Floor Level slab 1st half Concrete casting 100% completed. Tenth floor columns 50% completed. Shuttering works for 1st Half of Terrace floor level slab on progress. Blockwork & Plastering work on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT


Block C1: Electrical Wire pulling works completed. Terrace floor Water distribution lines work on progress.

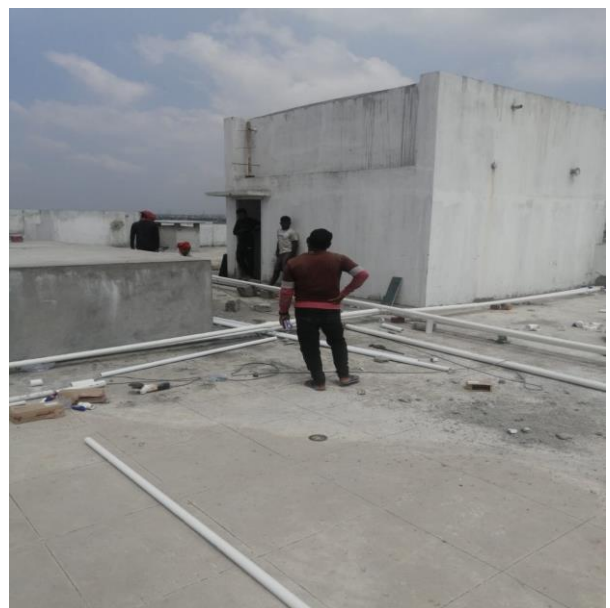

PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block C2: Terrace Water proofing work 95% completed. Internal Electrical Wire pulling works on progress

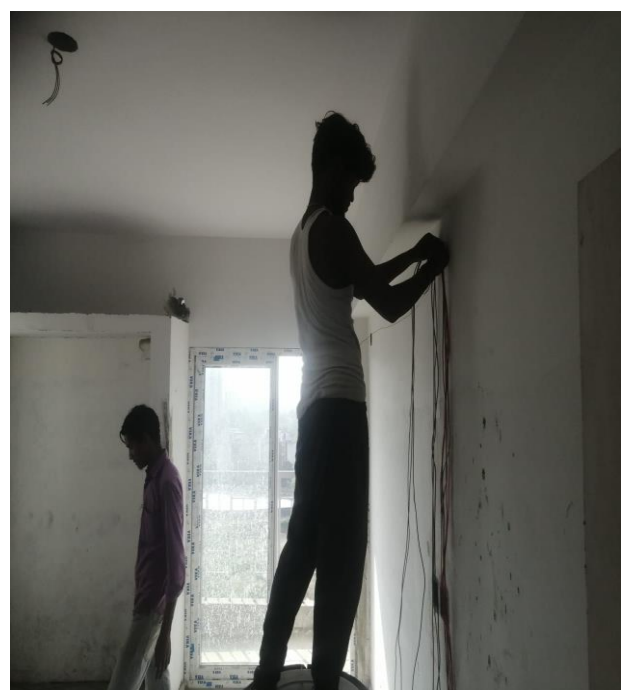

PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block C3: Staircase Green marble work completed. Lift cladding works & Window Grill works on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block D1: Terrace Water proofing works completed. Internal Electrical Wire pulling works on progress



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT


Block D2: Laying of Pipes for Firefighting on progress. Connection of Sewage Lines to Main Sewer lines.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block D3: Electrical wire pulling works. Firefighting works on progress.

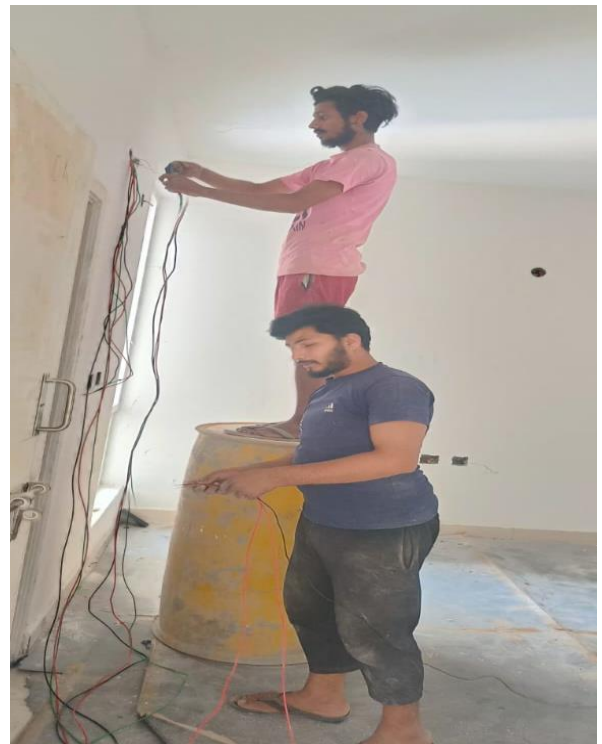

PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

U.G Sump 1 (Near B Block) – All RCC works completed. Internal waterproofing work on progress.



U.G Sump 2 (Near D Block) – All RCC works completed. Pump room Inner plastering & Internal Water proof plastering works on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Sewage Treatment Plant 2 (Near D Block). All RCC works completed. Internal Water proof plastering works on progress.



Sewage Treatment Plant 1 (Near C Block). Earthwork excavation works on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

External Sewerage Lines : Laying of External Sewage line & construction of Chambers around D2 & D3 Block



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

QUALITY CONTROL

DURING CONSTRUCTION FOLLOWING QUALITY CONTROL TESTS CONDUCTED AT SITE:

Sl.No.	Materials	Source from	Test Done	Result
1	M-Sand	Arcot (T.K), Ranipet (Dist) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2.	P- Sand	Uthiramerur, Kanchipuram (DT) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2	Coarse Aggregate (20mm)	Sriperambathur, Kanchipuram (Dt), Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
3	Coarse Aggregate (12mm)	Sriperambathur, Kanchipuram (Dt) Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
4	Cement	Third party testing is being done.		
5	Steel	Third party testing is being done.		
6	Pile Integrity	Third party testing is being done.		
7	Soil Compaction	Third party testing is being done.		
8	RCC cubes are being tested and Register is being maintained.			
9	Slump test conducted at site to insure workability of concrete.			

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

PHOTOGRAPH OF QUALITY CONTROL AT SITE

Concrete Cube Compressive Strength Testing



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

20mm & 12mm Aggregate Sieve Analysis Testing



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

Fine Aggregate Sieve Analysis Testing

