

**CGEWHO – CHENNAI PHASE-III
PROJECT**



MONTHLY PROGRESS REPORT

STATUS AS ON : 31.05.2024

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

31.05.2024

BLOCK	STATUS AS ON 31 st MAY-2024	
A1 BLOCK	<p>◆ 100% Completed Works</p> <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete 2 out of 2 (b) Tank Wall Concrete 2 out of 2 (c) Top Cover slab Concrete 2 out of 2 ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor ▪ Electrical Conducting works in Tenth floor. ▪ Fixing of Water supply pipe Lines (CPVC). ▪ Fixing of Sanitary Lines (PVC). ▪ Fixing of Vertical Plumbing Lines in Shaft. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank (2 / 2). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31 st MAY-2024
	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External Plastering 95% completed in all sides. ▪ Fixing of Staircase Handrail 95% completed. ▪ Fixing of Bathroom Wall Tiles 99% completed (198/200). ▪ Fixing of Toilet Wall Tiles 99% completed (198/200). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathrooms 99% completed (198/200) b) Ceramic Tiles in Toilets 99% completed (198/200) ▪ Vitrified Tiles in Halls & Bedrooms 99% completed (198/200). 	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External Plastering 95% completed in all sides. ▪ Fixing of Staircase Handrail 95% completed. ▪ Fixing of Bathroom Wall Tiles 100% completed (200/200). ▪ Fixing of Toilet Wall Tiles 100% completed (200/200). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathrooms 100% completed (200/200) b) Ceramic Tiles in Toilets 100% completed (200/200) ▪ Vitrified Tiles in Halls & Bedrooms 100% completed (200/200).



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Fixing of Door Shutters 94% completed (1134/1200). ▪ Fixing of UPVC Windows 95% completed (760 /800) ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 95% completed (190/200). b) Laying of Granite Countertop 95% completed (190/200). c) Fixing of S.S Sink 95% completed (190/200) ◆ Works On Progress <ul style="list-style-type: none"> ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace Water Proofing 80% completed. ▪ Lift Materials 4 out of 4 received. Bulket fittings completed. ▪ Fire fighting works 15% completed. ▪ Electrical wire pulling work 55% completed (110/200). ▪ Fixing of Modular Switches & Sockets 55% completed. (110/200) ➤ Model Flat Finishing works 90% completed. 	<ul style="list-style-type: none"> ▪ Fixing of Door Shutters 99% completed (1192/1200). ▪ Fixing of UPVC Windows 96% completed (773 /800) ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed (200/200). b) Laying of Granite Countertop 100% completed (200/200). c) Fixing of S.S Sink 100% completed (200/200) ◆ Works On Progress <ul style="list-style-type: none"> ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace Water Proofing 100% completed. ▪ Lift Materials 4 out of 4 received. <ul style="list-style-type: none"> a) Lift 1 – Work started. ▪ Fire fighting works 17% completed. ▪ Electrical wire pulling work 100% completed (200/200). ▪ Fixing of Modular Switches & Sockets 100% completed. (200/200) ➤ Model Flat Finishing works 90% completed.
BLOCK	STATUS AS ON 31st MAY-2024	
A2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank ● Base Slab Concrete 2 out of 2 ● Tank Wall Concrete 2 out of 2 ● Top Cover slab Concrete 2 out of 2 <ul style="list-style-type: none"> ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. 	



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Electrical Conducting works upto Tenth floor. ▪ Fixing of Water supply pipe Lines (CPVC). ▪ Fixing of Sanitary Lines (PVC). ▪ Fixing of Vertical Plumbing Lines in Shaft. ▪ Over Head Water Tank 100% completed (2 / 2) 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st MAY-2024
	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. ▪ Fixing of Bathroom Wall Tiles 94% completed (188/200). ▪ Fixing of Toilet Wall Tiles 94% completed (188/200). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 94% completed (188/200) b) Ceramic Tiles in Toilet 94% completed (188/200). ▪ Vitrified Tiles in Halls & Bedrooms 93% completed. (186/200). ▪ Water Proofing Work <ul style="list-style-type: none"> a) Terrace Water proofing 90% completed. <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Fixing of Door Shutters 89% completed (1069/1200). ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 53% completed (106/200). b) Laying of Granite Countertop 67% completed (135/200). c) Fixing of S.S Sink 67% completed (135/200) ▪ Lift Materials 4 out of 4 received. Bulket fittings completed. ▪ Fire fighting works 15% completed. 	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. ▪ Fixing of Bathroom Wall Tiles 99% completed (198/200). ▪ Fixing of Toilet Wall Tiles 99% completed (198/200). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 99% completed (198/200) b) Ceramic Tiles in Toilet 99% completed (198/200). ▪ Vitrified Tiles in Halls & Bedrooms 99% completed. (198/200). ▪ Water Proofing Work <ul style="list-style-type: none"> a) Terrace Water proofing 100% completed. ▪ Fixing of Door Shutters 95% completed (1150/1200). ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 98% completed (195/200). b) Laying of Granite Countertop 100% completed (200/200). c) Fixing of S.S Sink 100% completed (200/200) <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Lift Materials 4 out of 4 received. Bulket fittings completed. ▪ Fire fighting works 17% completed. ▪ Electrical wire pulling work started (10/200).



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

		<ul style="list-style-type: none"> ▪ Fixing of Modular Switches & Sockets started. (10/200)
BLOCK	STATUS AS ON 31 st MAY-2024	
B1 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 3) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom b) Vitrified Tiles in Halls & Bedrooms. c) Vitrified Tiles in Corridor. ▪ Fixing of UPVC Windows. ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados. b) Laying of Granite Countertop. c) Fixing of S.S Sink. ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BI BLOCK	b) Over Head Water Tank. <ul style="list-style-type: none"> ▪ Fixing of Door Shutters 100% completed (840/840). ▪ Electrical wire pulling work 100% completed (120/120). ▪ Fixing of Modular Switches & Sockets 100% completed. (120/120) 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st MAY-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 3 out 3. ▪ Lift Cladding works 3 out of 3. ▪ Laying of Green marble for Staircase 100% completed. ▪ Application of Exterior Wall Primer ▪ Fixing of M.S Window Safety Grills 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Firefighting works 88% completed. ▪ Terrace Water supply Ring main works 80% completed. <p>Model Flat Finishing works 95% completed.</p>	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 3 out 3. ▪ Lift Cladding works 3 out of 3. ▪ Laying of Green marble for Staircase 100% completed. ▪ Application of Exterior Wall Primer ▪ Fixing of M.S Window Safety Grills 95% completed. ▪ Firefighting works 91% completed. ▪ Terrace Water supply Ring main works 90% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Electrical Panel room- Trench works & cable tray fixing works on progress. ▪ Construction of Earth Pit chambers on progress. ● Model Flat Finishing works 95% completed.
BLOCK	STATUS AS ON 31st MAY-2024	
B2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Upto Terrace floor level slab R.C.C ▪ Parapet Columns Concrete 100% completed ▪ Block work upto Ninth floor. ▪ Ceiling plastering upto Eighth floor. ▪ Wall plastering upto Eighth floor. ▪ 1st Coat Wall Putty upto Fifth floor completed. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st MAY-2024
	<ul style="list-style-type: none"> ◆ Works On Progress <ul style="list-style-type: none"> ▪ Block work <ul style="list-style-type: none"> a) In Tenth floor 60% completed. 	<ul style="list-style-type: none"> ◆ Works On Progress <ul style="list-style-type: none"> ▪ Block work <ul style="list-style-type: none"> a) In Tenth floor 100% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Ceiling Plastering <ul style="list-style-type: none"> a) In Ninth floor 85% completed. ▪ Wall Plastering <ul style="list-style-type: none"> a) In Ninth floor 85% completed ▪ Electrical conducting works 80% completed. (96/120) ▪ 1st Coat Wall Putty in Sixth floor 15% completed. ▪ Fixing of Internal Water supply pipeline (CPVC) 80% completed (96 / 120) ▪ External Plastering 15% completed. 	<ul style="list-style-type: none"> ▪ Ceiling Plastering <ul style="list-style-type: none"> a) In Ninth floor 100% completed. ▪ Wall Plastering <ul style="list-style-type: none"> a) In Ninth floor 100% completed ▪ Electrical conducting works 93% completed. (112/120) ▪ 1st Coat Wall Putty in Sixth floor 45% completed. ▪ Fixing of Internal Water supply pipeline (CPVC) 83% completed (100 / 120) ▪ Fixing of Internal Sanitary lines (PVC) 16% completed.(20 / 120) ▪ External Plastering 20% completed.
BLOCK	STATUS AS ON 31st MAY-2024	
C1 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Internal Plumbing Line. <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom b) Vitrified Tiles in Halls & Bedrooms 	

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

C1 BLOCK	<ul style="list-style-type: none"> c) Vitrified Tiles in Corridor 100% completed. ▪ Fixing of UPVC Windows. ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed. ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank b) Terrace floor Water proofing. ▪ Laying of Green marble for Staircase. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados. b) Laying of Granite Countertop. c) Fixing of S.S Sink. ▪ Lift Cladding works 4 out of 4. ▪ Fixing of Door Shutters 100% completed (1080 / 1080) ▪ Electrical wire pulling work 100% completed (120/120). ▪ Fixing of Modular Switches & Sockets 100% completed. (120/120) 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st MAY-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Staircase Hand Rails (3 out of 3) 95% completed. ▪ Lift Installation works 4 out 4. ▪ Application of Exterior Wall Primer. ▪ Terrace Water supply Ring main works 95% completed. ▪ Fixing of M.S Window Safety Grills 90% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fire Fighting works 78% completed. ▪ Model Flat Finishing works 95% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Staircase Hand Rails (3 out of 3) 95% completed. ▪ Lift Installation works 4 out 4. ▪ Application of Exterior Wall Primer. ▪ Terrace Water supply Ring main works 100% completed. ▪ Fixing of M.S Window Safety Grills 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fire Fighting works 85% completed. ▪ Laying of External Sewerage lines 80% completed. ▪ Laying of External water supply lines 80% completed. ▪ Electrical Panel room- Trench works & cable tray fixing works on progress. ▪ Construction of Earth Pit chambers on progress. ● Model Flat Finishing works 95% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 31 st MAY-2024
C2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (2 out of 3) (b) Wall Concrete (2 out of 3) (c) Top Cover slab (2 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 3 out of 3 ▪ Fixing of Bathroom Wall Tiles completed. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom completed. b) Vitrified Tiles in Halls & Bedrooms completed. c) Vitrified Tiles in Corridor completed. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed. (120 / 120) b) Laying of Granite Countertop 100% completed. (120 / 120). c) Fixing of S.S Sink 100% completed. (120 / 120). ▪ Fixing of UPVC Window 100% completed. (600 / 600) ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed. (240 /240) ▪ Fixing of Main Door & Internal Shutters 100% completed (1080 / 1080) ▪ Laying of Green marble for Staircase 100% completed.. ▪ Electrical wire pulling 100% completed (120 /120).
C2 BLOCK	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31 st MAY-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Application of Exterior Wall Primer ▪ Lift Installation works 4 out 4 - 85% completed. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 95% completed. ▪ Lift Cladding work 90% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fire fighting works 54% completed. ▪ Fixing of Modular Switches & Sockets 84% completed. (101/120). ▪ Terrace Water supply Ring main works 75% completed 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Application of Exterior Wall Primer ▪ Lift Installation works 4 out 4 - 85% completed. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 95% completed. ▪ Lift Cladding work 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fire fighting works 57% completed. ▪ Fixing of Modular Switches & Sockets 100% completed. (120/120). ▪ Terrace Water supply Ring main works 80% completed. ▪ Laying of External Sewerage lines 75% completed. ▪ Laying of External water supply lines 50% completed.
BLOCK	STATUS AS ON 31 st MAY-2024	
C3 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (2 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

C3 BLOCK	<ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank (2 / 2) completed. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed (100/100) b) Laying of Granite Countertop 100% completed. (100/100). c) Fixing of S.S Sink 100% completed. (100/ 100). ▪ Fixing of Bathroom Wall Tiles 100% completed. (300 /300) ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 100% completed. (300 /300) b) Vitrified Tiles in Halls & Bedrooms 100% completed. (100 / 100) ▪ Laying of Green marble for Staircase 100% completed. ▪ Electrical wire pulling 100% completed (100 /100). ▪ Fixing of UPVC Window 100% Completed. (500 / 500). ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed (200 / 200). ▪ Fixing of Main Door & Internal Shutters 100% completed (900 / 900). ▪ Electrical wire pulling 100% completed (100 /100). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st MAY-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails. ▪ Application of Exterior Wall Primer ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works – <ul style="list-style-type: none"> 2 Lifts - 85% completed. 3rd Lift - 45% completed. 4th Lift - 30% completed. ▪ Lift Cladding work 50% completed. ▪ Fixing of Modular Switches & Sockets 70% completed. (70/100). ▪ Fire fighting works 54% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails. ▪ Application of Exterior Wall Primer ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works – <ul style="list-style-type: none"> 2 Lifts - 85% completed. 3rd Lift - 75% completed. 4th Lift - 45% completed. ▪ Lift Cladding work 60% completed. ▪ Fixing of Modular Switches & Sockets 85% completed. (85/100). ▪ Fire fighting works 55% completed. ▪ Laying of External Sewerage lines 50% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 31 st MAY-2024
D1 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 3 out of 3 b) Terrace floor Water proofing 100% completed. ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles 100% completed. (320 / 320). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 100% completed. (320 / 320) b) Vitrified Tiles in Halls & Bedrooms 100% completed. (80 / 80). ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed. (80 / 80) b) Laying of Granite Countertop 100% completed. (80 / 80). c) Fixing of S.S Sink 100% completed. (80 / 80). ▪ Fixing of Main Door & Internal Shutters 100% completed (880 / 880)
D1 BLOCK	<ul style="list-style-type: none"> ▪ Electrical Wire pulling works 100% completed. (80/ 80). ▪ Fixing of Modular Switches & Sockets 100% completed. (80/80) ▪ Fixing of UPVC Windows 100% completed. (400 / 400). ▪ Fixing of UPVC French Door 100% completed.(without Mosquito mesh shutter) (160 / 160) ▪ Electrical Wire pulling works 100% completed. (80/ 80).



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Fixing of Modular Switches & Sockets 100% completed. (80/80). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st MAY-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. ▪ Application of External Wall Primer- 1st Coat ◆ Works On Progress <ul style="list-style-type: none"> ▪ Application of Exterior Wall Damp proof Paint 50% completed. ▪ Lift Installation works <ul style="list-style-type: none"> a) 3 out 4 - 85% completed. b) 4th lift – 25% completed. ▪ Fire fighting works 77% completed. ▪ Laying of External Sewerage lines 90% completed ▪ Laying of External Water supply lines 90% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. ▪ Application of External Wall Primer- 1st Coat ◆ Works On Progress <ul style="list-style-type: none"> ▪ Application of Exterior Wall Damp proof Paint 60% completed. ▪ Lift Installation works <ul style="list-style-type: none"> a) 3 out 4 - 85% completed. b) 4th lift – 35% completed. ▪ Fire fighting works 85% completed. ▪ Laying of External Sewerage lines 95% completed ▪ Laying of External Water supply lines 95% completed. ▪ Construction of Earth Pit chambers 45% completed.
BLOCK	STATUS AS ON 31st MAY-2024	
D2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 3) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails 	



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

D2 BLOCK	<ul style="list-style-type: none"> ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom b) Vitrified Tiles in Halls & Bedrooms. c) Vitrified Tiles in Corridor. ▪ Fixing of UPVC Windows. ▪ Fixing of Main Door & Internal Shutters. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados. b) Laying of Granite Countertop. c) Fixing of S.S Sink. ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. b) Over Head Water Tank ▪ Laying of Green marble for Staircase. ▪ Fixing of UPVC French Door (without Mosquito mesh shutter). ▪ Electrical Wire pulling works 100% completed (80/ 80). ▪ Fixing of Modular Switches & Sockets 100% completed. (80/80). ▪ Fire Fighting Works 100% completed. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st MAY-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer. ▪ Fixing of M.S Window Safety Grills 98% completed. (315 / 320). ▪ Laying of External Sewerage lines 95% completed. ▪ Laying of External Water supply lines 95% completed. ▪ Laying of Storm Water drain pipes 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer. ▪ Fixing of M.S Window Safety Grills 100% completed. (320 / 320). ▪ Laying of External Sewerage lines 95% completed. ▪ Laying of External Water supply lines 95% completed. ▪ Laying of Storm Water drain pipes



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<p>90% completed.</p> <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Application of Exterior Wall Damp proof Paint 45% completed. ▪ Fire Fighting Works 95% completed. ▪ Model Flat Finishing works 95% completed. 	<p>90% completed.</p> <ul style="list-style-type: none"> ▪ Fire Fighting Works 95% completed. <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Application of Exterior Wall Damp proof Paint 55% completed. ▪ Electrical Panel room- Trench works & cable tray fixing works on progress. ▪ Construction of Earth Pit chambers 70% completed. • Model Flat Finishing works 95% completed.
BLOCK	STATUS AS ON 31st MAY-2024	
D3 BLOCK	<p>◆ 100% Completed Works</p> <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 1 out of 3 ▪ Fixing of Bathroom Wall Tiles 100% completed. (320 / 320) 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

D3 BLOCK	<ul style="list-style-type: none"> ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed. (80 / 80) b) Laying of Granite Countertop 100% completed. (80 / 80). ▪ Fixing of S.S Sink 100% completed. (80 / 80). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 100% completed. (320 / 320) b) Vitrified Tiles in Halls & Bedrooms 100% completed. (80 / 80) c) Vitrified Tiles in Corridor 100% completed. ▪ Fixing of Main Door & Internal Shutters 100% completed (880 / 880) ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 100% completed. b) Over Head Water Tank 3 out of 3 completed. ▪ Fixing of UPVC Windows 100% completed. (400 / 400) ▪ Electrical Wire pulling works 100% completed (80/ 80). ▪ Fixing of Modular Switches & Sockets 100% completed. (80/80). ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed (160 / 160). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31st MAY-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Laying of Green marble for Staircase. ▪ Lift Cladding works 90% completed. ▪ Application of Exterior Wall Primer ▪ Laying of External Sewerage lines 90% completed. ▪ Laying of External water supply lines 90% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works - 4 out of 4 - 85% completed. ▪ Fixing of M.S Window Safety Grills 78% completed (250/320). ▪ Firefighting works 77% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Laying of Green marble for Staircase. ▪ Lift Cladding works 90% completed. ▪ Application of Exterior Wall Primer ▪ Laying of External Sewerage lines 95% completed. ▪ Laying of External water supply lines 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works - 4 out of 4 - 85% completed. ▪ Fixing of M.S Window Safety Grills 85% completed (273/320). ▪ Firefighting works 85% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 31 st MAY-2024
COMMUNITY HALL	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (2 out of 2) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (b) Tank Wall Concrete (c) Top Cover slab Concrete. ▪ Block work upto Fourth floor & Parapet wall. ▪ Ceiling Plastering upto Fourth floor. ▪ Wall plastering upto Fourth floor. ▪ 1st Coat Wall Putty upto Fourth floor. ▪ 2nd Coat Wall Putty upto Fourth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Vitrified Floor Tiles in Hall & rooms b) Ceramic Floor Tiles in Bathrooms. c) Kota Stone in Staircase & Lobby ▪ Fixing of UPVC Windows. ▪ Fixing of Wooden flush Door for rooms. ▪ Fixing of Fire Safety Door for Hall Main Entrance ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. b) Over Head Water Tank.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31 st MAY-2024
	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer. ▪ Fire fighting works – Installation of Pipelines 95% completed. ▪ Electrical Wire & cables pulling work 95% completed. ▪ Fixing of Modular Switches & Sockets 95% completed. <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Fixing of Sanitary fixtures 20% completed. ▪ Excavation for laying of Firefighting Hydrant pipes 75% completed. ▪ Application of Exterior Wall Damp proof Paint 15% completed. 	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer. ▪ Fire fighting works – Installation of Pipelines 95% completed. ▪ Electrical Wire & cables pulling work 95% completed. ▪ Fixing of Modular Switches & Sockets 95% completed. <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Fixing of Sanitary fixtures 35% completed. ▪ Excavation for laying of Firefighting Hydrant pipes 90% completed. ▪ Application of Exterior Wall Damp proof Paint 45% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

STATUS AS ON 31 st MAY-2024	
EXTERNAL DEVELOPMENT WORKS	<ul style="list-style-type: none"> ➤ Underground Sump-1 (Near B-Block) <ul style="list-style-type: none"> ▪ Base Slab R.C.C 100% completed. ▪ Sump Wall - R.C.C 100% completed. ▪ Top slab R.C.C 100% completed. ▪ Outer Wall Waterproof plastering – 100% completed. ▪ Inner Wall Waterproof plastering – 100% completed. ▪ Pump room Inner plastering – 100% completed. ➤ Underground Sump-2 (Near D-Block) <ul style="list-style-type: none"> ▪ Base Slab - R.C.C 100% completed. ▪ Sump Wall - R.C.C 100% completed. ▪ Top slab R.C.C 100% completed. ▪ Outer Wall Waterproof plastering – 100% completed. ▪ Inner Wall Waterproof plastering 100% completed. ▪ Pump room Inner plastering 100% completed. ➤ Sewage Treatment Plant-2 (Near D-Block) <ul style="list-style-type: none"> ▪ Base slab – R.C.C 100% completed. ▪ STP Wall – R.C.C 100% completed. ▪ STP Top Slab – R.C.C 100% completed. ▪ STP Pump Room completed. ▪ Outer wall Waterproof plastering 100% completed. ▪ Inner Wall Waterproof plastering 100% completed. ▪ Installation of STP 80% completed. ➤ Sewage Treatment Plant-1 (Near C3-Block) <ul style="list-style-type: none"> ▪ Excavation Work completed. ▪ Base slab RCC completed. ▪ STP Wall Reinforcement 100% completed. ▪ STP Wall shuttering 40% completed. ➤ Laying of External Sewer lines <ul style="list-style-type: none"> ▪ Type D All Blocks – 95% completed. ▪ C1 Block – 80% completed ▪ C2 Block – 75% completed. ▪ C3 Block – 50% completed. ➤ Laying of External Water Supply lines <ul style="list-style-type: none"> ▪ Type D All Blocks – 95% completed. ▪ C1 Block – 80% completed ▪ C2 Block – 50% completed. ➤ Laying of Storm Water Drainage. <ul style="list-style-type: none"> ▪ Type D All Blocks – 70% completed.

PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

PHOTOGRAPHS OF WORK PROGRESS AS ON 31st MAY 2024


Community Hall: External Painting final coat on progress. DG Sets for Community Hall, STP, Sump, D1,D2 & D3 blocks reached.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block A1: Internal Wire pulling works on progress. Fixing of Firefighting hydrant pipes at Terrace on progress.

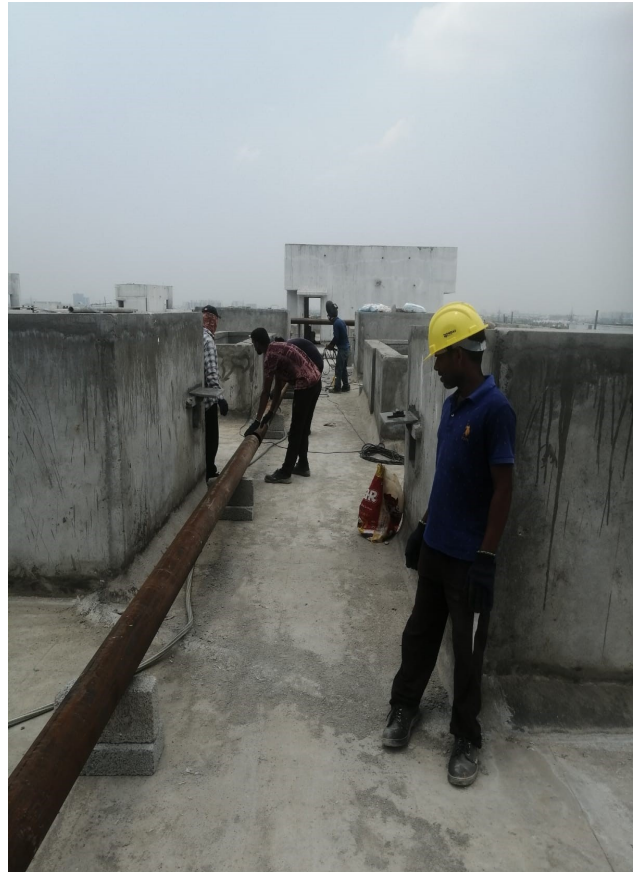

PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block A2 : Terrace Ring main works on progress. PCC for External Sewer lines on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block B1: Excavation in Stilt floor for laying of Sewer lines on progress. Trench & Cable tray works in Meter Panel room on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block B2 : Fixing of concealed internal water supply lines (CPVC) on progress. Core cutting & fixing of PVC pipes for internal sanitary lines on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block C1: External Painting works on progress. Gully trap connection works & finishing works in Stilt floor on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT


Block C2: Plumbing lines Connection works in Stilt floor on progress. Fire alarm cabling works in corridor on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block C3: Marking for Gully Chamber & PCC works for Sewer lines on progress. Fixing of UPVC French Windows on progress.

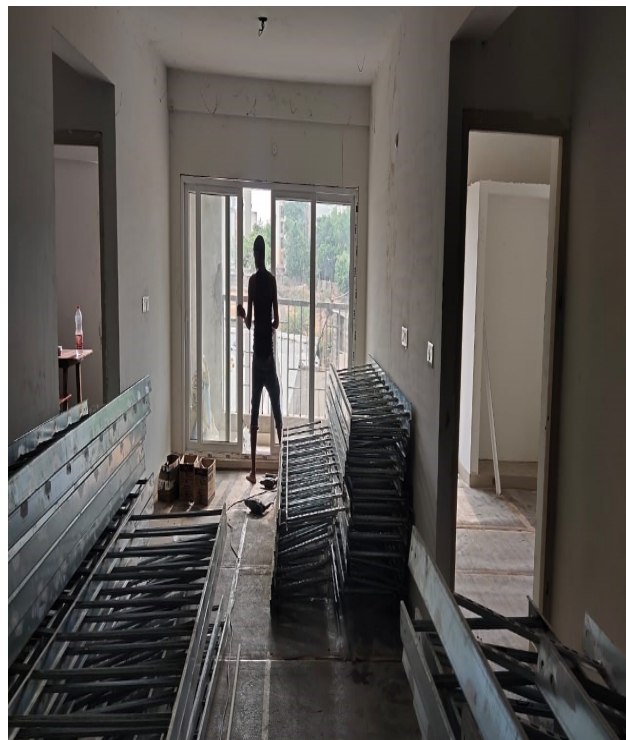

PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block D1: External Painting works on progress. Fixing of Electrical Distribution Box & False ceiling works in bathroom on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block D2: External Painting works on progress. Electrical Trench works & laying of conduits for fixing of Meter panels on progress.



PROGRESS REPORT CGEWHO – CHENNAI PHASE-III PROJECT

Block D3: Fixing of UPVC Windows & French Doors on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

U.G Sump 1 (Near B Block) – All RCC works completed. Internal Waterproofing work in Sump & Pump room completed.



U.G Sump 2 (Near D Block) – All RCC works completed. Water proofing works completed. Excavation for laying of Water supply main lines on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Sewage Treatment Plant 2 (Near D Block). All RCC works completed. Internal Water proof plastering works 100% completed. Installation of STP 80% completed.



Sewage Treatment Plant 1 (Near C Block). Base slab RCC completed. Reinforcement works for Wall completed. Shuttering work for Wall on progress.



PROGRESS REPORT CGEWHO – CHENNAI PHASE-III PROJECT

External Sewerage Lines : Laying of External Sewage line & construction of Chambers around C2 block on progress.



Laying of External Sewage line & construction of Chambers around C3 block & B1 block on progress.



C3-BLOCK



B1-BLOCK

PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Storm Water Drainage: Masonry work for Strom water Drainage around D1 & D2 blocks on progress.



D1- BLOCK



D2-BLOCK

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

QUALITY CONTROL

DURING CONSTRUCTION FOLLOWING QUALITY CONTROL TESTS CONDUCTED AT SITE:

Sl.No.	Materials	Source from	Test Done	Result
1	M-Sand	Arcot (T.K), Ranipet (Dist) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2.	P- Sand	Uthiramerur, Kanchipuram (DT) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2	Coarse Aggregate (20mm)	Sriperambathur, Kanchipuram (Dt), Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
3	Coarse Aggregate (12mm)	Sriperambathur, Kanchipuram (Dt) Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
4	Cement	Third party testing is being done.		
5	Steel	Third party testing is being done.		
6	Pile Integrity	Third party testing is being done.		
7	Soil Compaction	Third party testing is being done.		
8	RCC cubes are being tested and Register is being maintained.			
9	Slump test conducted at site to insure workability of concrete.			

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

PHOTOGRAPH OF QUALITY CONTROL AT SITE

Concrete Cube Compressive Strength Testing



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

20mm & 12mm Aggregate Sieve Analysis Testing



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

Fine Aggregate Sieve Analysis Testing

