

**PROGRESS REPORT**  
**CGEWHO - CHENNAI PHASE-III PROJECT**

31.03.2020

BLOCK	STATUS AS ON 23.03.2020
A1 BLOCK	<ul style="list-style-type: none"> <li>• Piling work 100% completed.</li> <li>• Earth work excavation for Pile Cap works 100% completed.</li> <li>• Plain Cement Concrete (P.C.C) For Pile Cap work 100% completed.</li> <li>• Pile Chipping Work 100% completed.</li> <li>• Pile Cap casting 100% completed.</li> <li>• Earthwork backfilling 100% completed.</li> <li>• Stilt Floor Plain Cement Concrete (P.C.C) work 100% completed.</li> <li>• Stilt floor Columns Concrete 100% completed.</li> <li>• First floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Second floor level 100% completed.</li> <li>• Second floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Third floor level 85% completed.</li> <li>• Shuttering and Bar bending work for First half of Third Floor level slab 10% Completed and balance work on progress.</li> </ul>
BLOCK	STATUS AS ON 23.03.2020
A2 BLOCK	<ul style="list-style-type: none"> <li>• Piling work 100% completed.</li> <li>• Earth work excavation for Pile Cap works 100% completed.</li> <li>• Plain Cement Concrete (P.C.C) For Pile Cap work 100% completed.</li> <li>• Pile Chipping Work 100% completed.</li> <li>• Pile Cap casting 100% completed.</li> <li>• Earthwork backfilling 100% completed.</li> <li>• Stilt Floor Plain Cement Concrete (P.C.C) work 100% completed.</li> <li>• Stilt floor Columns Concrete 100% completed.</li> <li>• First floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Second floor level 50% completed</li> </ul>
BLOCK	STATUS AS ON 23.03.2020
B1 BLOCK	<ul style="list-style-type: none"> <li>• Piling work 100% completed.</li> <li>• Pile cap casting 100% completed.</li> <li>• Columns up to First floor level 100% completed.</li> <li>• First floor level slab Concrete Casting 100% Completed</li> <li>• Columns up to Second floor level 100% completed.</li> <li>• Second floor level slab Concrete Casting 100% Completed</li> <li>• Columns up to Third floor Level 100%Completed.</li> </ul>



**Progress Report No.21 (07.03.2017- 23.03.2020)**

**NOTE : FROM 24.03.2020 ONWARDS CONSTRUCTION SITE UNDER LOCK DOWN  
DUE TO COVID 19**

**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

	<ul style="list-style-type: none"> <li>• Third floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Fourth floor Level 100% Completed</li> <li>• Fourth floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Fifth floor Level 100%Completed.</li> <li>• Fifth floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Sixth floor Level 100%Completed</li> <li>• Sixth floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Seventh floor Level 100%Completed</li> <li>• Seventh floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Eighth floor level 100% completed</li> <li>• Eighth floor level slab First half Concrete casting 100% completed.</li> <li>• Shuttering work for Second half of Eighth Floor level slab 10% Completed and balance work on progress.</li> <li>• Block work in First floor 85% completed.</li> <li>• Block work in Second floor 80% completed</li> <li>• Block work in Third floor 70% completed.</li> <li>• Block work in Fourth floor 65% completed.</li> <li>• Block work in Fifth floor 30% completed.</li> <li>• Model Flat Finishing works Completed.</li> </ul>
<b>BLOCK</b>	<b>STATUS AS ON 23.03.2020</b>
B2 BLOCK	<ul style="list-style-type: none"> <li>• Piling work 100% completed.</li> <li>• Earth work excavation for Pile Cap works 100% completed.</li> <li>• PCC for pile cap 100% completed.</li> <li>• Pile Cap Casting 100% completed</li> <li>• Columns up to First floor level 100% completed.</li> <li>• First floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Second floor level 100% completed.</li> <li>• Second floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Third floor level 100% completed.</li> <li>• Third floor level slab Concrete Casting 100% Completed.</li> <li>• Bar bending fabrication works for Columns up to Fourth Floor level on progress.</li> <li>• Block work in First floor 30% completed.</li> </ul>
<b>BLOCK</b>	<b>STATUS AS ON 23.03.2020</b>
C1 BLOCK	<ul style="list-style-type: none"> <li>• Piling work 100% completed.</li> <li>• Pile cap casting 100% completed.</li> <li>• Columns up to First floor level 100% completed.</li> <li>• First floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Second floor level 100% completed.</li> </ul>



**Progress Report No.21 (07.03.2017- 23.03.2020)**

**NOTE : FROM 24.03.2020 ONWARDS CONSTRUCTION SITE UNDER LOCK DOWN DUE TO COVID 19**

**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

	<ul style="list-style-type: none"> <li>• Second floor level slab Concrete Casting 100% Completed</li> <li>• Columns up to Third floor level 100% completed.</li> <li>• Third floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Fourth floor level 100% completed.</li> <li>• Fourth floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Fifth floor level 100% completed.</li> <li>• Fifth floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Sixth floor level 100% completed.</li> <li>• Sixth floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Seventh floor level 100% completed.</li> <li>• Seventh floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Eighth floor level 100% completed.</li> <li>• Eight floor level slab First Half Concrete Casting 100% Completed.</li> <li>• Shuttering and Bar bending work for Second half of Eighth Floor level slab 10% Completed and balance work on progress.</li> <li>• Block work in First Floor Level 85% completed.</li> <li>• Block work in Second Floor Level 85% completed.</li> <li>• Block work in Third Floor Level 70% completed.</li> <li>• Block work in Fourth Floor Level 35% completed.</li> <li>• Block work in Fifth Floor Level 15% completed.</li> <li>• Model Flat Finishing Works completed.</li> <li>• Stilt ceiling plastering 85% completed</li> <li>• First Floor ceiling plastering 85% completed</li> </ul>
<b>BLOCK</b>	<b>STATUS AS ON 23.03.2020</b>
C2 BLOCK	<ul style="list-style-type: none"> <li>• Piling work 100% completed.</li> <li>• Pile cap casting 100% completed.</li> <li>• Columns up to First floor level 100% completed.</li> <li>• First floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Second Floor level 100% Completed.</li> <li>• Second floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Third Floor level 100% Completed.</li> <li>• Third floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Fourth Floor level 100% Completed.</li> <li>• Fourth floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Fifth Floor level 100% Completed.</li> <li>• Fifth floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Sixth Floor level 100% Completed.</li> <li>• Sixth floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Seventh Floor level 70% Completed.</li> <li>• Shuttering &amp; Bar bending work for First half of Seventh floor level slab work 80% completed and balance work on progress.</li> <li>• Block work in First Floor Level 70% completed.</li> <li>• Block work in Second Floor Level 10% completed.</li> </ul>



**Progress Report No.21 (07.03.2017- 23.03.2020)**

**NOTE : FROM 24.03.2020 ONWARDS CONSTRUCTION SITE UNDER LOCK DOWN  
DUE TO COVID 19**

**PROGRESS REPORT**  
**CGEWHO - CHENNAI PHASE-III PROJECT**

	<ul style="list-style-type: none"> <li>• Stilt floor ceiling plastering 80% completed.</li> </ul>
<b>BLOCK</b>	<b>STATUS AS ON 23.03.2020</b>
C3 BLOCK	<ul style="list-style-type: none"> <li>• Piling work 100% completed.</li> <li>• Pile cap casting 100% completed.</li> <li>• Columns up to Stilt floor level 100% completed.</li> <li>• PCC flooring for Stilt Floor 100% Completed.</li> <li>• Columns up to First floor level 100% completed.</li> <li>• First floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Second floor level 100% completed.</li> <li>• Second floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Third floor level 100% completed.</li> <li>• Third floor level slab concrete casting 100% completed.</li> <li>• Columns up to Fourth floor level 100% completed.</li> <li>• Fourth floor level slab First half Concrete Casting 100% completed.</li> <li>• Fourth floor level slab Second half Concrete Casting 75% completed.</li> <li>• Columns up to Fifth floor level 60% completed.</li> <li>• Shuttering and bar bending works for First half of Fifth floor level slab 50% completed and balance works on progress.</li> <li>• Stilt floor ceiling plastering 80% completed.</li> </ul>
<b>BLOCK</b>	<b>STATUS AS ON 23.03.2020</b>
D1 BLOCK	<ul style="list-style-type: none"> <li>• Piling work 100% completed.</li> <li>• Earth work excavation for Pile Cap works 100% completed.</li> <li>• Plain Cement Concrete (PCC) For Pile Cap work 100% completed.</li> <li>• Pile Chipping Work 100% completed.</li> <li>• Pile Cap casting 100% completed.</li> <li>• Earthwork backfilling 100% completed.</li> <li>• Stilt Floor Plain Cement Concrete (P.C.C) work 100% completed.</li> <li>• Stilt Floor Columns Concrete work 100% Completed.</li> <li>• First floor level slab Concrete Casting 100% Completed.</li> <li>• Columns upto Second floor level 100% completed.</li> <li>• Shuttering and Bar bending work for First half of Second Floor level slab 20% completed and balance work on progress.</li> </ul>
<b>BLOCK</b>	<b>STATUS AS ON 23.03.2020</b>
D2 BLOCK	<ul style="list-style-type: none"> <li>• Piling work 100% completed.</li> <li>• Pile cap casting 100% completed.</li> <li>• Columns up to First floor level 100% completed.</li> <li>• First floor level slab Concrete Casting 100% Completed</li> </ul>



**Progress Report No.21 (07.03.2017- 23.03.2020)**

**NOTE : FROM 24.03.2020 ONWARDS CONSTRUCTION SITE UNDER LOCK DOWN  
DUE TO COVID 19**

11

**PROGRESS REPORT**  
**CGEWHO - CHENNAI PHASE-III PROJECT**

	<ul style="list-style-type: none"> <li>• Columns up to Second floor level 100% completed.</li> <li>• Second floor level slab Concrete Casting 100% Completed</li> <li>• Columns up to Third floor level 100% completed.</li> <li>• Third floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Fourth floor level 100% completed.</li> <li>• Fourth floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Fifth Floor level Slab 100% Completed.</li> <li>• Fifth floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Sixth Floor level Slab 100% Completed.</li> <li>• Sixth floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Seventh Floor level Slab 100% Completed..</li> <li>• Seventh floor level slab First Half Concrete Casting 100% Completed.</li> <li>• Shuttering and Bar bending work for Second half of Seventh Floor level slab 50% completed and balance work on progress.</li> <li>• Columns up to Eight Floor level Slab 10% Completed..</li> <li>• Block work in First Floor Level 85% completed.</li> <li>• Block work in Second Floor Level 70% completed.</li> <li>• Block work in Third Floor Level 15% completed.</li> <li>• Block work in Fourth Floor Level 10% completed.</li> <li>• Model Flat Finishing Works on progress.</li> </ul>
<b>BLOCK</b>	<b>STATUS AS ON 23.03.2020</b>
D3 BLOCK	<ul style="list-style-type: none"> <li>• Piling work 100% completed.</li> <li>• Pile cap casting 100% completed.</li> <li>• Columns up to First floor level 100% completed.</li> <li>• First floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Second floor level 100% completed.</li> <li>• Second floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Third floor level 100% completed.</li> <li>• Third floor level Slab Concrete Casting 100% Completed.</li> <li>• Columns up to Fourth floor level 100% completed.</li> <li>• Fourth floor level Slab Concrete Casting 100% Completed</li> <li>• Columns up to Fifth floor level 50% completed.</li> <li>• Shuttering and Barbending work for First half of Fifth floor level slab 20% completed.</li> <li>• Block work in First Floor Level 60% completed.</li> <li>• Block work in Second Floor Level 45% completed.</li> <li>• Block work in Third Floor Level 30% completed.</li> </ul>
<b>BLOCK</b>	<b>STATUS AS ON 23.03.2020</b>



**Progress Report No.21 (07.03.2017- 23.03.2020)**

**NOTE : FROM 24.03.2020 ONWARDS CONSTRUCTION SITE UNDER LOCK DOWN  
DUE TO COVID 19**


## **PROGRESS REPORT**

### **CGEWHO - CHENNAI PHASE-III PROJECT**

COMMUNITY HALL	<ul style="list-style-type: none"> <li>• Piling work 100% completed.</li> <li>• Earth work excavation for Pile Cap works 100% Completed.</li> <li>• PCC for pile cap 100% completed</li> <li>• Pile cap casting 100% completed.</li> <li>• Earthwork backfilling 100% completed</li> <li>• Columns up to First floor level 100% completed.</li> <li>• First floor level slab Concrete Casting 100% Completed</li> <li>• Columns up to Second floor level 100% completed.</li> <li>• Second floor level slab Concrete Casting 100% Completed.</li> <li>• Columns up to Third Floor level concrete casting 100% completed.</li> <li>• Shuttering and barbending works for Third floor level slab 40% Completed and balance work on progress.</li> </ul>
----------------	---

#### **PHOTOGRAPHS OF WORK PROGRESS AS ON 23.03.2020**

Block A1: Columns concrete work upto Third floor level 80% completed. Shuttering and barbending work on progress for 1<sup>st</sup> Half of Third Floor level.

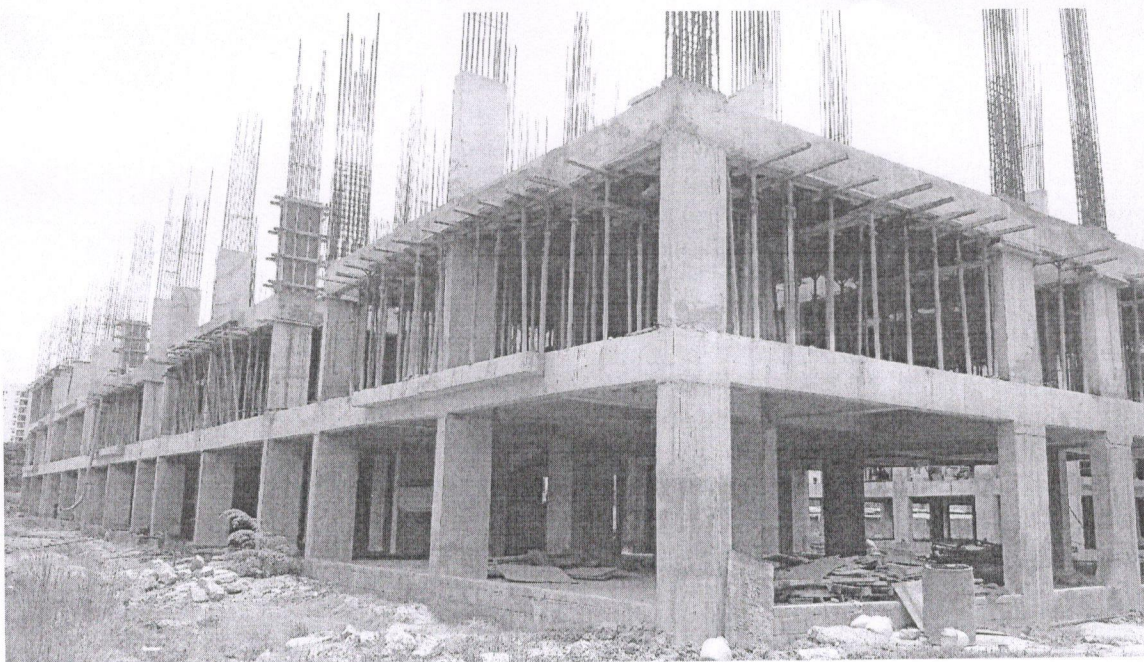

Block A2: Columns concrete work upto Second floor level 50% completed . Shuttering and barbending work on progress for 1<sup>st</sup> Half of Second Floor level.



**Progress Report No.21 (07.03.2017- 23.03.2020)**

**NOTE : FROM 24.03.2020 ONWARDS CONSTRUCTION SITE UNDER LOCK DOWN DUE TO COVID 19**

## PROGRESS REPORT CGEWHO – CHENNAI PHASE-III PROJECT

---



Block B1: Eight Floor Level slab 1<sup>st</sup> Half concrete casting 100% completed. Shuttering & Barbending work for on progress for 2<sup>nd</sup> floor level slab.



Block B2: Third Floor Level slab concrete 100% completed. Bar bending works for Columns up to fourth floor level on progress.




**Progress Report No.21 (07.03.2017- 23.03.2020)**

**NOTE : FROM 24.03.2020 ONWARDS CONSTRUCTION SITE UNDER LOCK DOWN  
DUE TO COVID 19**

**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

---

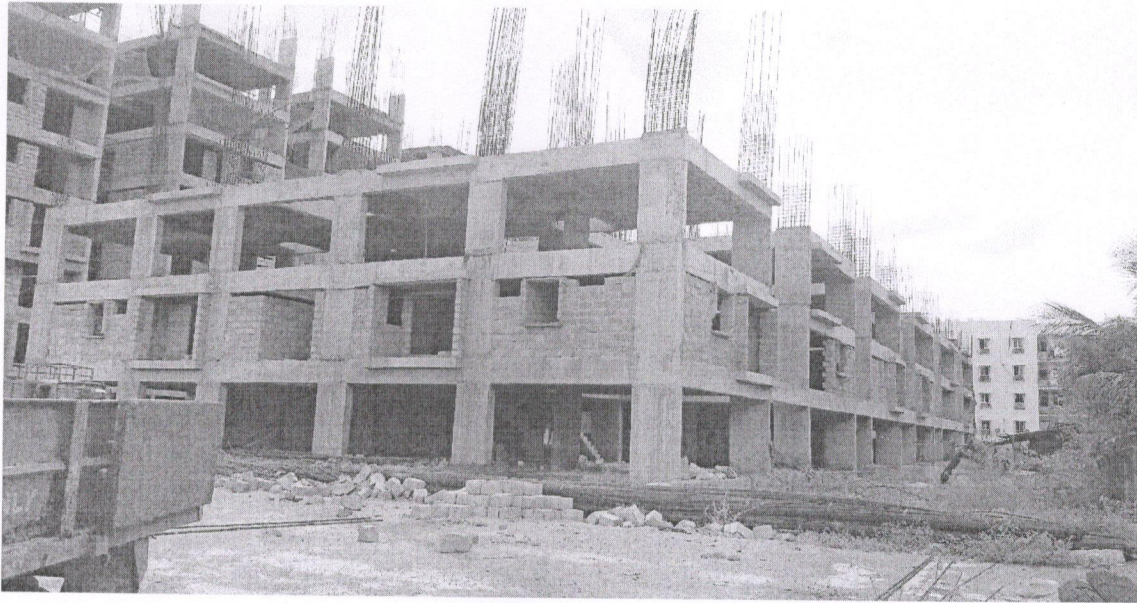

Block C1: Eight Floor Level slab 1<sup>st</sup> half concrete casting 100% completed. Shuttering & barbending work on progress for 2<sup>nd</sup> half of Eight Floor level slab.



Block C2: Sixth Floor level slab concrete casting completed. Shuttering and Barbending work for 1<sup>st</sup> half of Seventh Floor level slab 80% completed.



**Progress Report No.21 (07.03.2017- 23.03.2020)**

**NOTE : FROM 24.03.2020 ONWARDS CONSTRUCTION SITE UNDER LOCK DOWN  
DUE TO COVID 19**




7

## PROGRESS REPORT CGEWHO - CHENNAI PHASE-III PROJECT

---



Block C3: Fourth Floor Level slab 1<sup>st</sup> Half concrete casting completed & 2<sup>nd</sup> half concrete casting 75% completed. Shuttering works for 1<sup>st</sup> half of Fifth Floor level slab 50% completed.

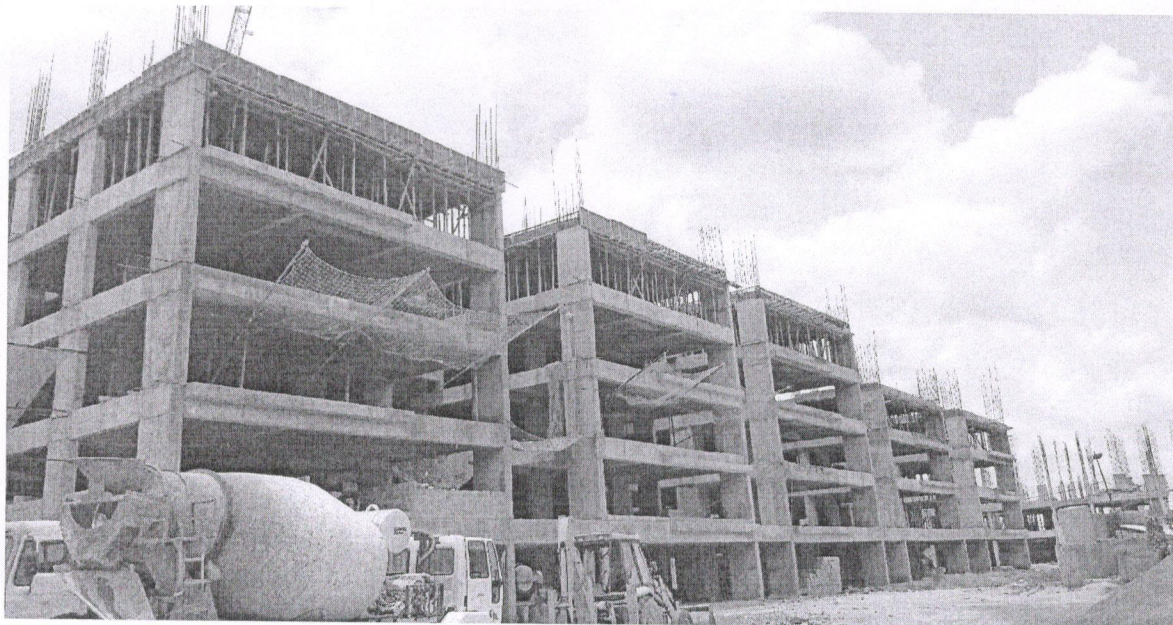

Block D1: Columns upto Second floor Level slab 100% completed. Shuttering works & Barbending works for 1<sup>st</sup> Half of Second floor level 20% completed..




**Progress Report No.21 (07.03.2017- 23.03.2020)**

**NOTE : FROM 24.03.2020 ONWARDS CONSTRUCTION SITE UNDER LOCK DOWN  
DUE TO COVID 19**

**PROGRESS REPORT**  
**CGEWHO - CHENNAI PHASE-III PROJECT**

---

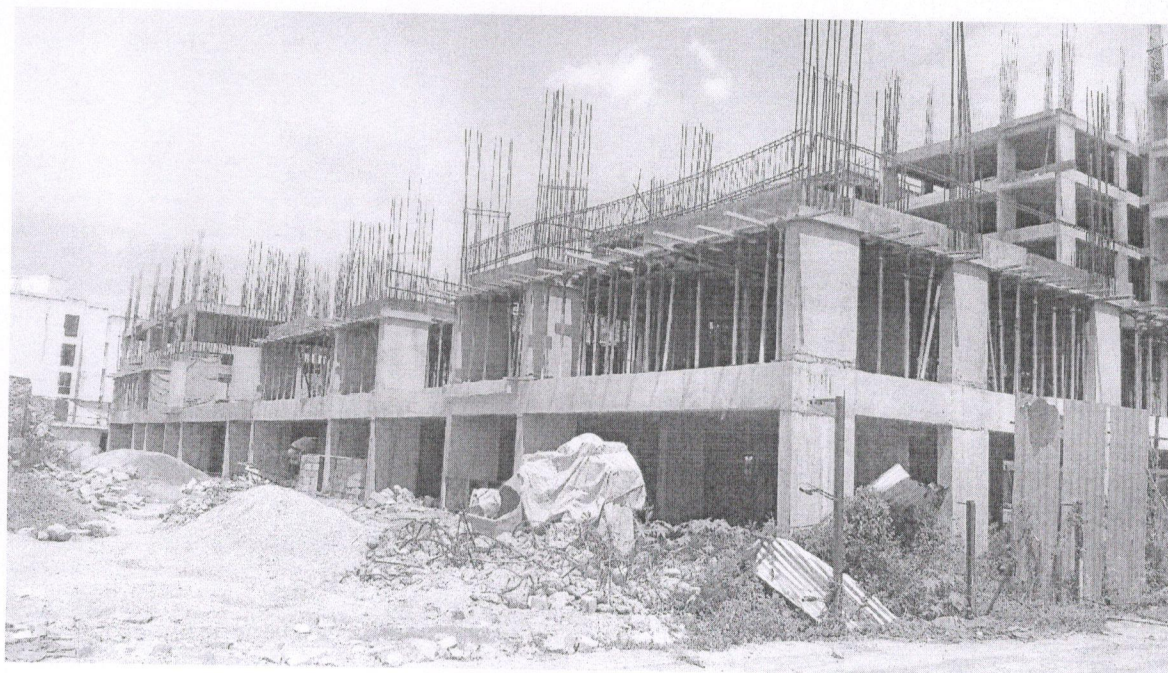

Block D2: Shuttering & Barbending works for 2<sup>nd</sup> Half of Seventh floor level slab 40% completed. Columns work upto Eight floor level on progress.



Block D3: Shuttering works & Barbending works for 1<sup>st</sup> Half of Fifth floor level slab 20% completed.




**Progress Report No.21 (07.03.2017- 23.03.2020)**

**NOTE : FROM 24.03.2020 ONWARDS CONSTRUCTION SITE UNDER LOCK DOWN  
DUE TO COVID 19**


5

**PROGRESS REPORT**  
**CGEWHO - CHENNAI PHASE-III PROJECT**

---

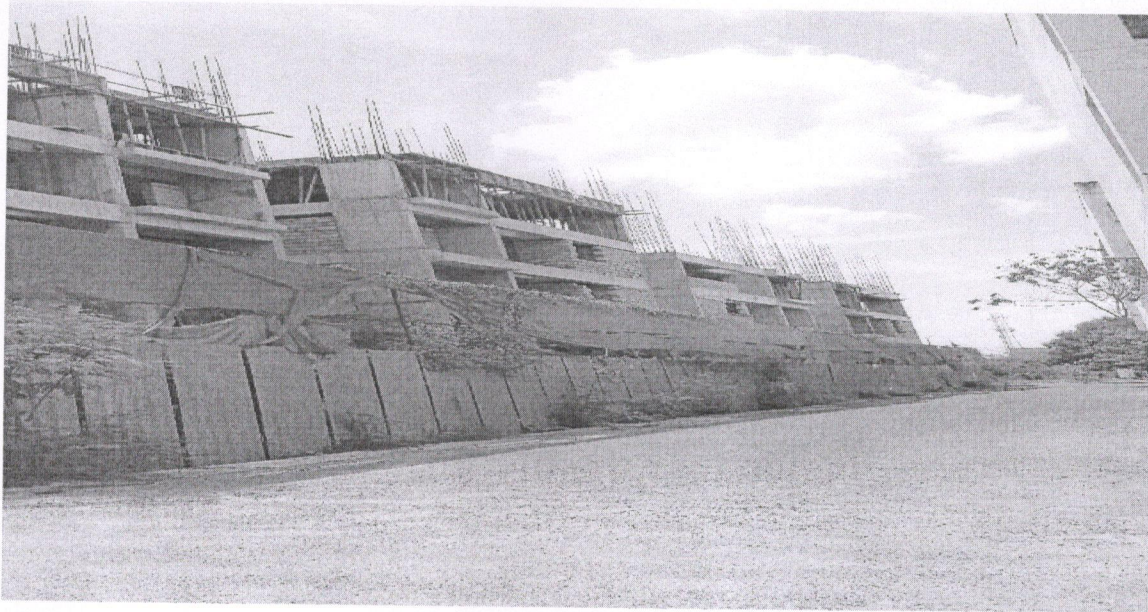

Community Hall: Shuttering & Barbending works for Third floor level slab 40% completed and balance work on progress.

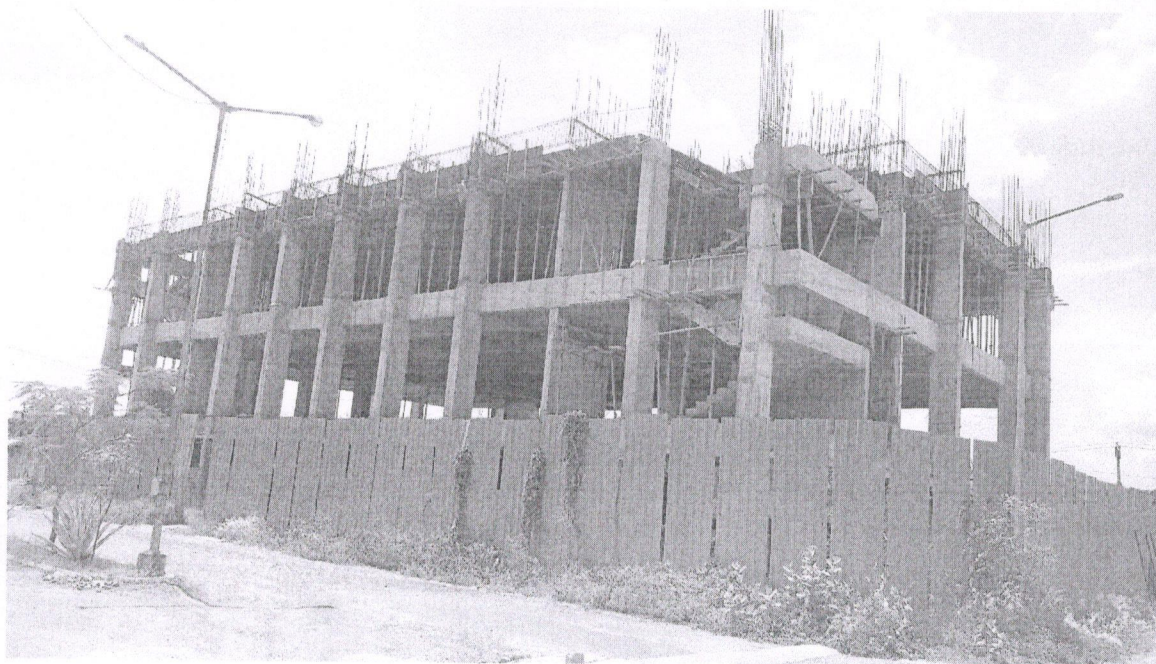

**QUALITY CONTROL**

**DURING CONSTRUCTION FOLLOWING QUALITY CONTROL TESTS CONDUCTED AT SITE:**

---



**Progress Report No.21 (07.03.2017- 23.03.2020)**

**NOTE : FROM 24.03.2020 ONWARDS CONSTRUCTION SITE UNDER LOCK DOWN DUE TO COVID 19**

**PROGRESS REPORT**  
**CGEWHO - CHENNAI PHASE-III PROJECT**

Sl.No.	Materials	Source from	Test Done	Result
1	M-Sand	Sriperambathur, Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2	Coarse Aggregate (20mm)	Sriperambathur, Kanchipuram (Dt)	Each Truck	Sieve Analysis
3	Coarse Aggregate (12mm)	Sriperambathur, Kanchipuram (Dt)	Each Truck	Sieve Analysis
4	Cement	Third party testing is being done.		
5	Steel	Third party testing is being done.		
6	Pile Integrity	Third party testing is being done.		
7	Soil Compaction	Third party testing is being done.		
8	RCC cubes are being tested and Register is being maintained.			
9	Slump test conducted at site to insure workability if concrete.			

**PHOTOGRAPH OF QUALITY CONTROL AT SITE**



Progress Report No.21 (07.03.2017- 23.03.2020)

**NOTE :** FROM 24.03.2020 ONWARDS CONSTRUCTION SITE UNDER LOCK DOWN  
DUE TO COVID 19

**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

---

**Concrete Cube Compressive Strength Testing**



**20mm & 12mm Aggregate Sieve Analysis Testing**




**Progress Report No.21 (07.03.2017- 23.03.2020)**

**NOTE : FROM 24.03.2020 ONWARDS CONSTRUCTION SITE UNDER LOCK DOWN  
DUE TO COVID 19**

**PROGRESS REPORT**  
**CGEWHO - CHENNAI PHASE-III PROJECT**

---

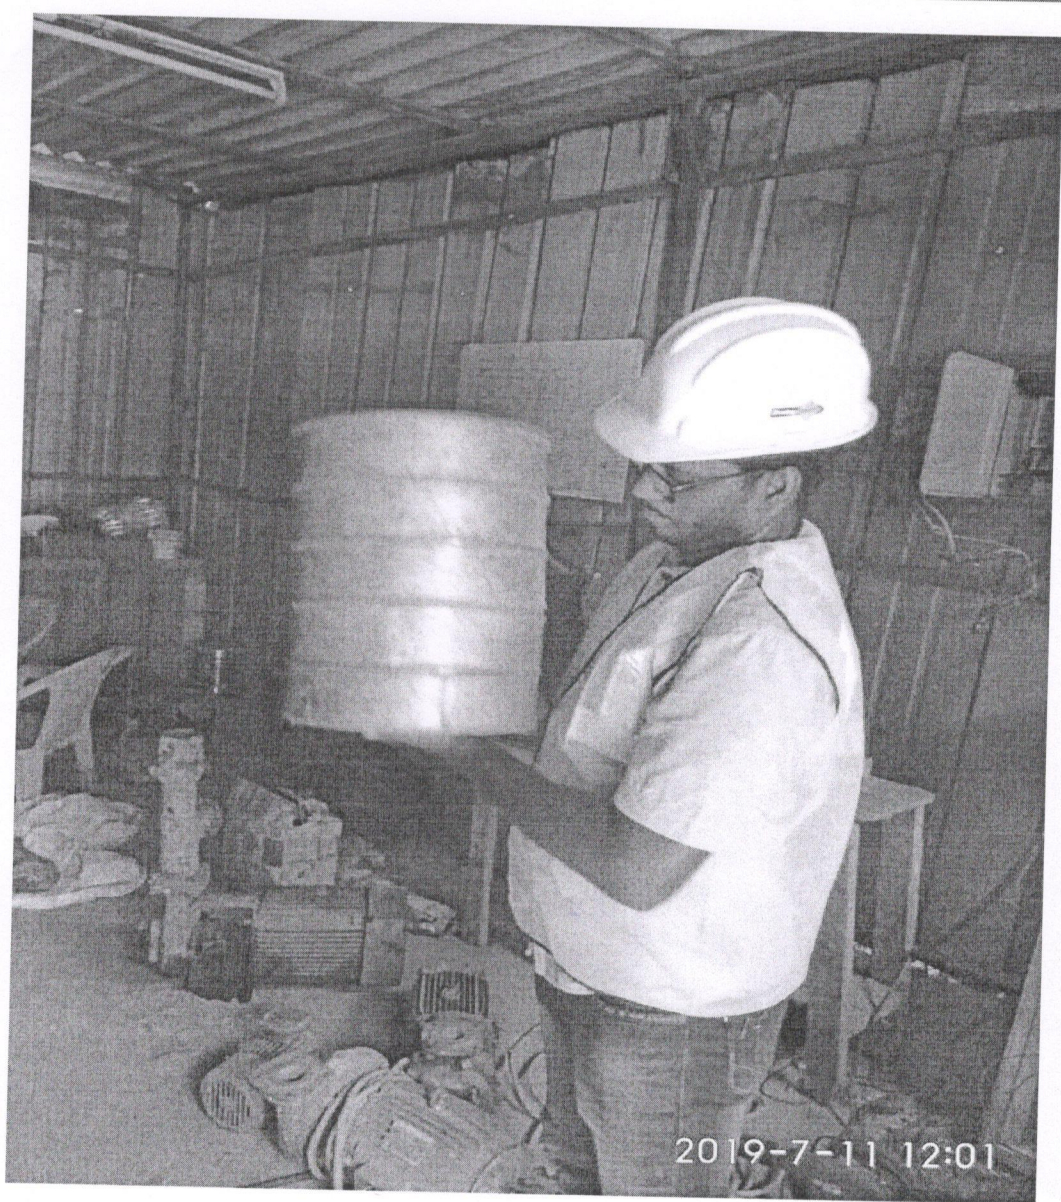

**Fine Aggregate Sieve Analysis Testing**




**Progress Report No.21 (07.03.2017- 23.03.2020)**

**NOTE : FROM 24.03.2020 ONWARDS CONSTRUCTION SITE UNDER LOCK DOWN  
DUE TO COVID 19**

**PROGRESS REPORT**  
**CGEWHO - CHENNAI PHASE-III PROJECT**

---

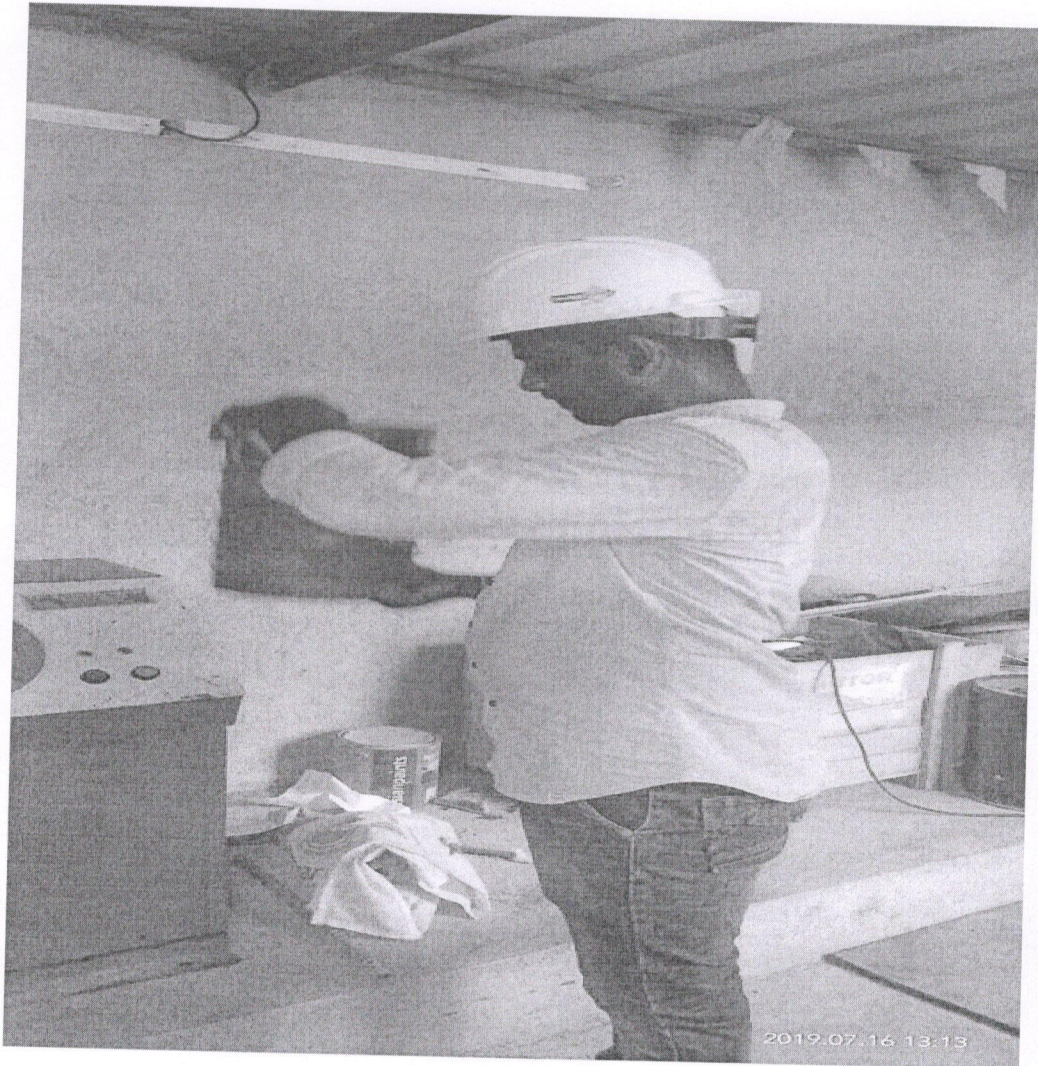

**Progress Report No.21 (07.03.2017- 23.03.2020)**

**NOTE : FROM 24.03.2020 ONWARDS CONSTRUCTION SITE UNDER LOCK DOWN  
DUE TO COVID 19**
