

PROGRESS REPORT **CGEWHO – CHENNAI PHASE-III PROJECT**

30.06.2022

BLOCK	STATUS AS ON 30.06.2022
A1 BLOCK	<ul style="list-style-type: none"> • Piling work 100% completed. • Earth work excavation for Pile Cap works 100% completed. • Plain Cement Concrete (P.C.C) For Pile Cap work 100% completed. • Pile Chipping Work 100% completed. • Pile Cap casting 100% completed. • Earthwork backfilling 100% completed. • Stilt Floor Plain Cement Concrete (P.C.C) work 100% completed. • Stilt floor Columns Concrete 100% completed. • First floor level slab Concrete Casting 100% completed. • Columns up to Second floor level 100% completed. • Second floor level slab Concrete Casting 100% completed. • Columns up to Third floor level 100% completed. • Third floor level slab Concrete Casting 100% completed. • Columns up to Fourth floor level 100% completed. • Fourth floor level slab Concrete Casting 100% completed. • Columns up to Fifth floor level 100% completed. • Fifth floor level slab First half Concrete Casting 100% completed • Shuttering & Barbending works for Second half of Fifth floor level slab 75% completed and balance works on progress. • Columns up to Sixth floor level 50% completed. • Block work in First floor 95% completed. • Block work in Second floor 95% completed. • Block work in Third floor 50% completed • Stilt ceiling plastering 50% completed. • First ceiling plastering 45% completed. • First wall plastering 10% completed. • Model Flat Finishing works 85% completed.
BLOCK	STATUS AS ON 30.06.2022
A2 BLOCK	<ul style="list-style-type: none"> • Piling work 100% completed. • Earth work excavation for Pile Cap works 100% completed. • Plain Cement Concrete (P.C.C) For Pile Cap work 100% completed. • Pile Chipping Work 100% completed. • Pile Cap casting 100% completed. • Earthwork backfilling 100% completed. • Stilt Floor Plain Cement Concrete (P.C.C) work 100% completed. • Stilt floor Columns Concrete 100% completed. • First floor level slab Concrete Casting 100% completed. • Columns up to Second floor level 100% completed.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> • Second floor level slab Concrete Casting 100% completed. • Columns up to Third floor level 100% completed. • Third floor level slab Concrete Casting 100% completed. • Columns up to Fourth floor level 100% completed. • Fourth floor level slab Concrete Casting 100% completed. • Columns up to Fifth floor level 50% completed. • Shuttering works for First half of Fifth floor level slab 25% completed and balance works on progress. • Block work in First floor 95% completed. • Block work in Second floor 90% completed. • Block work in Third floor 10% completed. • Stilt Ceiling plastering works 65% completed. • First Floor ceiling plastering 90% completed. • Second Floor ceiling plastering 10% completed. • First Floor wall plastering 90% completed.
BLOCK	STATUS AS ON 30.06.2022
B1 BLOCK	<ul style="list-style-type: none"> • Piling work 100% completed. • Pile cap casting 100% completed. • Columns up to First floor level 100% completed. • First floor level slab Concrete Casting 100% Completed. • Columns up to Second floor level 100% completed. • Second floor level slab Concrete Casting 100% Completed • Columns up to Third floor Level 100%Completed. • Third floor level slab Concrete Casting 100% Completed. • Columns up to Fourth floor Level 100% Completed • Fourth floor level slab Concrete Casting 100% Completed. • Columns up to Fifth floor Level 100%Completed. • Fifth floor level slab Concrete Casting 100% Completed. • Columns up to Sixth floor Level 100%Completed • Sixth floor level slab Concrete Casting 100% Completed. • Columns up to Seventh floor Level 100%Completed • Seventh floor level slab Concrete Casting 100% Completed. • Columns up to Eighth floor level 100% completed • Eighth floor level slab Concrete casting 100% completed. • Columns up to Ninth floor level 100% completed. • Ninth floor level slab Concrete casting 100% completed. • Columns up to Tenth floor level 100% completed. • Tenth floor level slab Concrete casting 100% completed. • Columns up to Terrace floor level 100% completed. • Terrace floor level slab Concrete casting 100% completed. • Parapet Columns concrete casting 100% completed • Block work in First floor 95% completed. • Block work in Second floor 95% completed. • Block work in Third floor 95% completed. • Block work in Fourth floor 95% completed.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> • Block work in Fifth floor 90% completed. • Block work in Sixth floor 90% completed. • Block work in Seventh floor 85% completed. • Block work in Eighth floor 85% completed. • Block work in Ninth floor 85% completed. • Block work in Tenth floor 75% completed. • Parapet wall Block work 50% completed. • Stilt ceiling plastering 80% completed. • First Floor ceiling plastering 90% completed. • Second Floor ceiling plastering 90% completed. • Third Floor ceiling plastering 90% completed. • Fourth Floor ceiling plastering 90% completed. • Fifth Floor ceiling plastering 90% completed. • Sixth Floor ceiling plastering 75% completed. • Seventh Floor ceiling plastering 60% completed. • Eighth Floor ceiling plastering 35% completed. • First Floor Wall plastering 90% completed. • Second Floor Wall plastering 90% completed. • Third Floor Wall plastering 90% completed. • Fourth Floor Wall plastering 90% completed. • Fifth Floor Wall plastering 90% completed. • Sixth Floor Wall plastering 50% completed. • External Plastering – South Side Elevation 60% completed • Model Flat Finishing works Completed.
BLOCK	STATUS AS ON 30.06.2022
B2 BLOCK	<ul style="list-style-type: none"> • Piling work 100% completed. • Earth work excavation for Pile Cap works 100% completed. • PCC for pile cap 100% completed. • Pile Cap Casting 100% completed • Columns up to First floor level 100% completed. • First floor level slab Concrete Casting 100% Completed. • Columns up to Second floor level 100% completed. • Second floor level slab Concrete Casting 100% Completed. • Columns up to Third floor level 100% completed. • Third floor level slab Concrete Casting 100% Completed. • Columns up to Fourth floor level 80% completed • Shuttering works for First half of Fourth floor level slab 10% completed. • Block work in First floor 50% completed.
BLOCK	STATUS AS ON 30.06.2022
C1 BLOCK	<ul style="list-style-type: none"> • Piling work 100% completed. • Pile cap casting 100% completed. • Columns up to First floor level 100% completed.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none">• First floor level slab Concrete Casting 100% Completed.• Columns up to Second floor level 100% completed.• Second floor level slab Concrete Casting 100% Completed• Columns up to Third floor level 100% completed.• Third floor level slab Concrete Casting 100% Completed.• Columns up to Fourth floor level 100% completed.• Fourth floor level slab Concrete Casting 100% Completed.• Columns up to Fifth floor level 100% completed.• Fifth floor level slab Concrete Casting 100% Completed.• Columns up to Sixth floor level 100% completed.• Sixth floor level slab Concrete Casting 100% Completed.• Columns up to Seventh floor level 100% completed.• Seventh floor level slab Concrete Casting 100% Completed.• Columns up to Eighth floor level 100% completed.• Eighth floor level slab Concrete Casting 100% Completed.• Columns upto Ninth floor level 100% completed.• Ninth floor level slab Concrete Casting 100% Completed.• Columns upto Tenth floor level 100% completed.• Tenth floor level slab Concrete Casting 100% Completed.• Columns upto Terrace floor level 100% completed.• Terrace floor level slab Concrete Casting 100% Completed.• Parapet Column concrete 90% completed• Block work in First Floor Level 95% completed.• Block work in Second Floor Level 95% completed.• Block work in Third Floor Level 95% completed.• Block work in Fourth Floor Level 95% completed.• Block work in Fifth Floor Level 95% completed.• Block work in Sixth Floor Level 95% completed.• Block work in Seventh Floor Level 95% completed.• Block work in Eighth Floor Level 90% completed.• Block work in Ninth Floor Level 90% completed.• Block work in Tenth Floor Level 40% completed.• Stilt ceiling plastering 85% completed.• First Floor ceiling plastering 95% completed.• Second Floor ceiling plastering 95% completed.• Third Floor ceiling plastering 95% completed.• Fourth Floor ceiling plastering 90% completed.• Fifth Floor ceiling plastering 90% completed.• Sixth Floor ceiling plastering 50% completed.• First Floor Wall plastering 95% completed.• Second Floor Wall plastering 95% completed.• Third Floor Wall plastering 90% completed.• Fourth Floor Wall plastering 90% completed.• Fifth Floor Wall plastering 85% completed.• Sixth Floor Wall plastering 50% completed.• Model Flat Finishing Works completed.
--	--



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 30.06.2022
C2 BLOCK	<ul style="list-style-type: none"> • Piling work 100% completed. • Pile cap casting 100% completed. • Columns up to First floor level 100% completed. • First floor level slab Concrete Casting 100% Completed. • Columns up to Second Floor level 100% Completed. • Second floor level slab Concrete Casting 100% Completed. • Columns up to Third Floor level 100% Completed. • Third floor level slab Concrete Casting 100% Completed. • Columns up to Fourth Floor level 100% Completed. • Fourth floor level slab Concrete Casting 100% Completed. • Columns up to Fifth Floor level 100% Completed. • Fifth floor level slab Concrete Casting 100% Completed. • Columns up to Sixth Floor level 100% Completed. • Sixth floor level slab Concrete Casting 100% Completed. • Columns up to Seventh Floor level 100% Completed. • Seventh floor level slab concrete casting 100% completed. • Columns up to Eight Floor level 100% Completed. • Eight floor level slab concrete casting 100% completed. • Columns up to Ninth Floor level 100% completed. • Ninth floor level slab concrete casting 100% completed. • Columns up to Tenth Floor level 100% completed. • Tenth floor level slab Concrete casting 100% completed. • Columns up to Terrace Floor level 90% completed. • Terrace floor level slab First half Concrete casting 100% completed. • Shuttering works for Second half of Terrace floor level slab 10% completed and balance works on progress. • Block work in First Floor Level 95% completed • Block work in Second Floor Level 95% completed. • Block work in Third Floor Level 95% completed. • Block work in Fourth Floor Level 95% completed. • Block work in Fifth Floor Level 95% completed. • Block work in Sixth Floor Level 95% completed. • Block work in Seventh Floor Level 95% completed. • Stilt floor ceiling plastering 90% completed. • First floor ceiling plastering 90% completed. • Second floor ceiling plastering 90% completed. • Third floor ceiling plastering 90% completed. • Fourth floor ceiling plastering 90% completed. • Fifth floor ceiling plastering 70% completed. • First floor wall plastering 90% completed. • Second floor wall plastering 90% completed. • Third floor wall plastering 90% completed. • Fourth floor wall plastering 90% completed • Fifth floor wall plastering 70% completed



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 30.06.2022
C3 BLOCK	<ul style="list-style-type: none"> • Piling work 100% completed. • Pile cap casting 100% completed. • Columns up to Stilt floor level 100% completed. • PCC flooring for Stilt Floor 100% Completed. • Columns up to First floor level 100% completed. • First floor level slab Concrete Casting 100% Completed. • Columns up to Second floor level 100% completed. • Second floor level slab Concrete Casting 100% Completed. • Columns up to Third floor level 100% completed. • Third floor level slab concrete casting 100% completed. • Columns up to Fourth floor level 100% completed. • Fourth floor level Slab Concrete Casting 100% completed. • Columns up to Fifth floor level 100% completed. • Fifth floor level slab concrete casting 100% completed. • Columns up to Sixth floor level 100% completed • Sixth floor level slab concrete casting 100% completed. • Columns up to Seventh floor level 100% completed. • Seventh floor level slab First half concrete casting 100% completed. • Shuttering & Barbending works for Second half of Seventh floor level slab 80% completed and balance works on progress • Columns up to Eighth floor level 50% completed. • Block work in First floor level 90% completed. • Block work in Second floor level 90% completed. • Block work in Third Floor Level 90% completed. • Block work in Fourth Floor Level 50% completed. • Stilt floor ceiling plastering 90% completed. • First floor ceiling plastering 90% completed. • Second floor ceiling plastering 90% completed. • Third floor ceiling plastering 50% completed. • First floor Wall plastering 90% completed. • Second floor Wall plastering 15% completed.
BLOCK	STATUS AS ON 30.06.2022
D1 BLOCK	<ul style="list-style-type: none"> • Piling work 100% completed. • Earth work excavation for Pile Cap works 100% completed. • Plain Cement Concrete (PCC) For Pile Cap work 100% completed. • Pile Chipping Work 100% completed. • Pile Cap casting 100% completed. • Earthwork backfilling 100% completed. • Stilt Floor Plain Cement Concrete (P.C.C) work 100% completed. • Stilt Floor Columns Concrete work 100% Completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> • First floor level slab Concrete Casting 100% Completed. • Columns up to Second floor level 100% completed. • Second floor level Slab Concrete Casting 100% Completed. • Columns up to Third floor level 100% completed. • Third floor level Slab Concrete Casting 100% Completed. • Columns up to Fourth floor level 100% completed. • Fourth floor level Slab Concrete Casting 100% Completed. • Columns up to Fifth floor level 100% completed. • Fifth floor level Slab Concrete Casting 100% Completed. • Columns up to Sixth floor level 100% completed. • Sixth floor level Slab Concrete Casting 100% Completed. • Columns up to Seventh floor level 100% completed. • Seventh floor level slab Concrete Casting 100% Completed. • Columns up to Eighth floor level 100% completed. • Eighth floor level slab First half Concrete Casting 100% Completed. • Shuttering & Barbending works for Second half of Eighth floor level slab 25% completed and balance works on progress • Block work in First floor level 90% completed. • Block work in Second floor level 90% completed. • Block work in Third floor level 90% completed. • Block work in Fourth floor level 90% completed. • Block work in Fifth floor level 10% completed. • First floor ceiling plastering 90% completed. • Second floor ceiling plastering 70% completed. • First floor Wall plastering 60% completed.
BLOCK	STATUS AS ON 30.06.2022
D2 BLOCK	<ul style="list-style-type: none"> • Piling work 100% completed. • Pile cap casting 100% completed. • Columns up to First floor level 100% completed. • First floor level slab Concrete Casting 100% Completed • Columns up to Second floor level 100% completed. • Second floor level slab Concrete Casting 100% Completed • Columns up to Third floor level 100% completed. • Third floor level slab Concrete Casting 100% Completed. • Columns up to Fourth floor level 100% completed. • Fourth floor level slab Concrete Casting 100% Completed. • Columns up to Fifth Floor level Slab 100% Completed. • Fifth floor level slab Concrete Casting 100% Completed. • Columns up to Sixth Floor level Slab 100% Completed. • Sixth floor level slab Concrete Casting 100% Completed. • Columns up to Seventh Floor level Slab 100% Completed. • Seventh floor level slab Concrete Casting 100% Completed. • Columns up to Eight Floor level Slab 100% Completed • Eight floor level slab Concrete Casting 100% Completed.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> • Columns up to Ninth Floor level Slab 100% Completed. • Ninth floor level slab Concrete Casting 100% Completed. • Columns up to Tenth Floor level Slab 100% Completed. • Tenth floor level slab Concrete Casting 100% Completed. • Columns up to Terrace Floor level Slab 100% Completed. • Terrace floor level slab Concrete Casting 100% Completed. • Parapet Columns concrete casting 80% completed • Block work in First Floor Level 95% completed. • Block work in Second Floor Level 95% completed. • Block work in Third Floor Level 95% completed. • Block work in Fourth Floor Level 95% completed. • Block work in Fifth Floor Level 95% completed. • Block work in Sixth Floor Level 90% completed. • Block work in Seventh Floor Level 90% completed. • Block work in Eighth Floor Level 90% completed. • Block work in Ninth Floor Level 90% completed. • Block work in Tenth Floor Level 60% completed. • Parapet Wall Block work 50% completed • Stilt ceiling plastering 80% completed. • First Floor ceiling plastering 90% completed. • Second Floor ceiling plastering 90% completed. • Third Floor ceiling plastering 70% completed. • Fourth Floor ceiling plastering 70% completed. • Fifth Floor ceiling plastering 50% completed. • Sixth Floor ceiling plastering 15% completed. • Seventh Floor ceiling plastering 50% completed. • Eighth Floor ceiling plastering 20% completed. • First Floor Wall plastering 90% completed. • Second Floor Wall plastering 90% completed. • Third Floor Wall plastering 65% completed. • Fourth Floor Wall plastering 50% completed. • Fifth Floor Wall plastering 50% completed • Model Flat Finishing Works completed.
BLOCK	STATUS AS ON 30.06.2022
D3 BLOCK	<ul style="list-style-type: none"> • Piling work 100% completed. • Pile cap casting 100% completed. • Columns up to First floor level 100% completed. • First floor level slab Concrete Casting 100% Completed. • Columns up to Second floor level 100% completed. • Second floor level slab Concrete Casting 100% Completed. • Columns up to Third floor level 100% completed. • Third floor level Slab Concrete Casting 100% Completed. • Columns up to Fourth floor level 100% completed. • Fourth floor level Slab Concrete Casting 100% Completed



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> • Columns up to Fifth floor level 50% completed. • Fifth floor level Slab Concrete Casting 100% Completed. • Columns up to Sixth floor level 100% completed. • Sixth floor level Slab Concrete Casting 100% Completed. • Columns up to Seventh floor level 100% completed. • Seventh floor level slab Concrete Casting 100% Completed. • Columns up to Eight floor level 100% completed. • Eighth floor level slab Concrete Casting 100% Completed. • Columns up to Ninth floor level 100% completed. • Ninth floor level slab Concrete Casting 100% Completed. • Columns up to Tenth floor level 100% completed. • Tenth floor level slab First half Concrete Casting 100% Completed. • Shuttering works for Second half of Tenth floor level slab 90% Completed. • Block work in First Floor Level 95% completed. • Block work in Second Floor Level 95% completed. • Block work in Third Floor Level 95% completed. • Block work in Fourth Floor Level 90% completed. • Block work in Fifth Floor Level 90% completed. • Block work in Sixth Floor Level 90% completed. • Block work in Seventh Floor Level 90% completed. • Block work in Eighth Floor Level 60% completed. • Stilt ceiling plastering 85% completed. • First Floor ceiling plastering 90% completed. • Second Floor ceiling plastering 90% completed. • Third Floor ceiling plastering 90% completed. • Fourth Floor ceiling plastering 75% completed. • First Floor Wall plastering 90% completed. • Second Floor Wall plastering 90% completed. • Third Floor Wall plastering 90% completed. • Fourth Floor Wall plastering 75% completed.
BLOCK	STATUS AS ON 30.06.2022
COMMUNITY HALL	<ul style="list-style-type: none"> • Piling work 100% completed. • Earth work excavation for Pile Cap works 100% Completed. • PCC for pile cap 100% completed • Pile cap casting 100% completed. • Earthwork backfilling 100% completed • Columns up to First floor level 100% completed. • First floor level slab Concrete Casting 100% Completed • Columns up to Second floor level 100% completed. • Second floor level slab Concrete Casting 100% Completed. • Columns up to Third Floor level concrete casting 100% completed. • Third floor level slab Concrete Casting 100% Completed. • Columns up to Fourth Floor level concrete casting 100% completed. • Fourth floor level slab Concrete Casting 100% completed.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none">• Columns upto Terrace floor level 100% completed.• Terrace floor level slab Concrete Casting 100% completed.• Parapet Column concrete casting 90% completed.• Block work in First floor 95% completed.• Block work in Second floor 95% completed.• Block work in Third floor 75% completed.• Stilt Floor ceiling plastering 90% completed.• Stilt Floor 1st Coat Inner painting 65% completed.• First Floor ceiling plastering 95% completed.• Second Floor ceiling plastering 95% completed.• First Floor Wall plastering 95% completed.• Second Floor Wall plastering 95% completed.• First Floor ceiling Putty 95% completed.• Second Floor ceiling putty 80% completed.• First Floor wall Putty 95% completed.• Second Floor wall Putty 70% completed.• First Floor 1st Coat Inner painting 95% completed.• First Floor – Floor Tile laying 95% completed.• First Floor UPVC Window fixing 95% completed.• External plastering in West Side elevation 70% completed• External plastering in South Side elevation 30% completed• External plastering in North Side elevation 25% completed
--	---



PROGRESS REPORT CGEWHO - CHENNAI PHASE-III PROJECT

PHOTOGRAPHS OF WORK PROGRESS AS ON 30.06.2022

Block A1: Fifth Floor Level slab 1st Half Concrete casting 100% completed. Shuttering & Barbending works for 2nd Half of Fifth floor level slab 75% completed.



Block A2: Fourth Floor level slab concrete casting 100% completed. Shuttering works for 1st half of Fifth floor level slab 25% completed.



PROGRESS REPORT **CGEWHO – CHENNAI PHASE-III PROJECT**

Block B1 : Terrace floor level slab concrete casting 100% completed. Parapet Column casting 80% completed. External plastering work –South Side elevation 60% completed.




PROGRESS REPORT **CGEWHO – CHENNAI PHASE-III PROJECT**

Block B2: Third Floor Level slab concrete casting 100% completed. Shuttering works for 1st half of Fourth floor level slab 10% completed.



PROGRESS REPORT CGEWHO – CHENNAI PHASE-III PROJECT

Block C1: Terrace Floor level slab concrete 100% completed. Parapet Column concrete 90% completed.

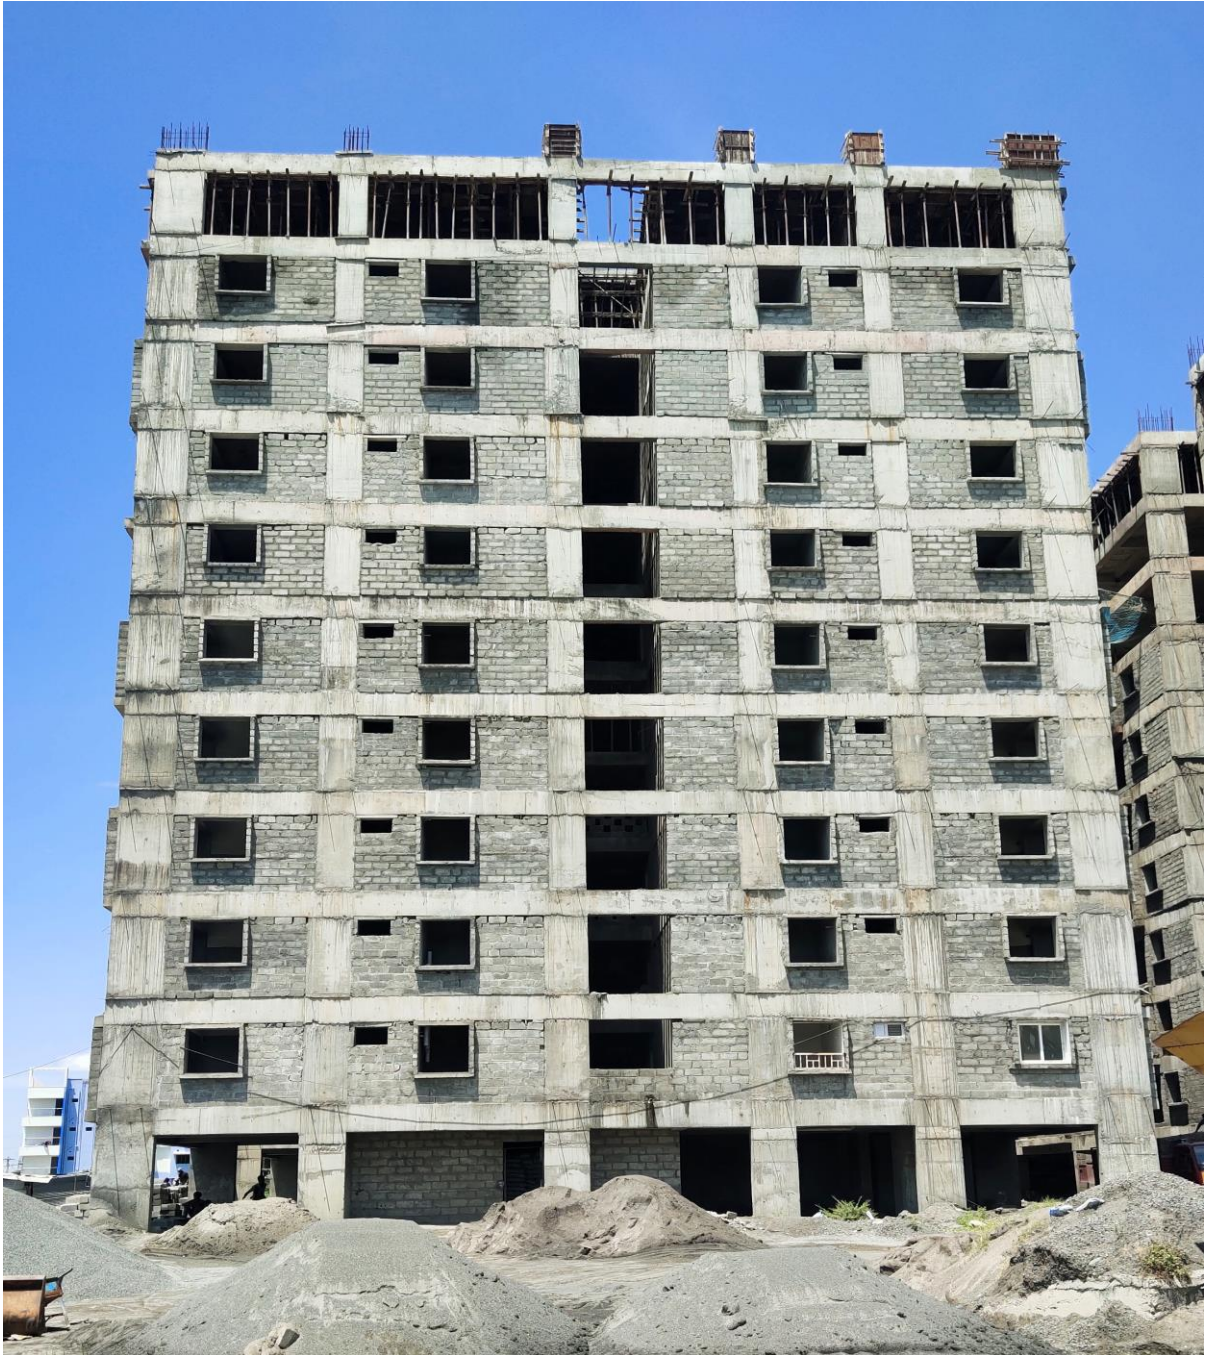

PROGRESS REPORT **CGEWHO - CHENNAI PHASE-III PROJECT**

Block C2: Terrace floor level slab 1st half concrete casting 100% completed. Shuttering works for 2nd half 10% completed and balance works on progress.



PROGRESS REPORT **CGEWHO – CHENNAI PHASE-III PROJECT**

Block C3: Shuttering & Barbending works for 2nd half of Seventh floor level slab 80% completed and balance works on progress.



PROGRESS REPORT **CGEWHO - CHENNAI PHASE-III PROJECT**

Block D1: Eighth Floor level slab 1st half Concrete casting 100% completed. Shuttering & Barbending works for 2nd half of Eighth Floor level slab 25% completed and balance works on progress.



PROGRESS REPORT **CGEWHO – CHENNAI PHASE-III PROJECT**

Block D2: Terrace floor slab Concrete casting 100% completed. Parapet Columns concrete 80% completed. Parapet Wall Block work 50% completed.



PROGRESS REPORT **CGEWHO – CHENNAI PHASE-III PROJECT**

Block D3: Tenth Floor level slab Concrete casting 100% completed. Shuttering works for 2nd half of Tenth Floor level slab 90% completed and balance works on progress.



PROGRESS REPORT **CGEWHO – CHENNAI PHASE-III PROJECT**

Community Hall: Terrace Floor level Concrete casting 100% completed. Parapet Column concrete casting 90% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

QUALITY CONTROL

DURING CONSTRUCTION FOLLOWING QUALITY CONTROL TESTS CONDUCTED AT SITE:

Sl.No.	Materials	Source from	Test Done	Result
1	M-Sand	Uthiramerur, Kanchipuram (DT) Sriperambathur, Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2	Coarse Aggregate (20mm)	Uthiramerur, Kanchipuram (DT) Sriperambathur, Kanchipuram (Dt)	Each Truck	Sieve Analysis
3	Coarse Aggregate (12mm)	Uthiramerur, Kanchipuram (DT) Sriperambathur, Kanchipuram (Dt)	Each Truck	Sieve Analysis
4	Cement	Third party testing is being done.		
5	Steel	Third party testing is being done.		
6	Pile Integrity	Third party testing is being done.		
7	Soil Compaction	Third party testing is being done.		
8	RCC cubes are being tested and Register is being maintained.			
9	Slump test conducted at site to insure workability of concrete.			



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

PHOTOGRAPH OF QUALITY CONTROL AT SITE

Concrete Cube Compressive Strength Testing



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

20mm & 12mm Aggregate Sieve Analysis Testing



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

Fine Aggregate Sieve Analysis Testing

